



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

**Project Title:** Headquarters R&R

Project Number: 11206  
BCC District: 03  
Delivery Method: Construction Management  
Category: S06-Sheriff - FDO  
Status: Close Out  
Designer: Leo Daly  
Contractor: Kast Construction  
Project Manager: Terri Wolfe

### SCOPE

The project consists of the exterior hardening of the entire building consisting of new exterior walls, impact resistant doors and windows, roof replacement and structural tie-ins as well as the R&R of all major building systems and interior renovation of approx. 75% of the building. As part of the project, the Board has also approved the temp. relocation of employees occupying approx. 70% of the space to ensure continuity of operations during the construction, reduce the overall duration of the project and therefore total project cost. This project is funded in:  
FY 2017 IST \$1,600,000, FY 2019 IST \$11,047,000  
FY 2020 IST \$10,835,000, FY 2021 IST \$17,620,000  
FY 2022 IST \$6,577,994  
Ad Valorem Fund Allocated to date \$8,953,189

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/14/2016	3/14/2016
Design Start	5/9/2017	5/9/2017
Construction Start	1/31/2019	3/22/2021
Substantial Completion	8/23/2022	12/8/2023
Project Completion	3/24/2023	

### PARTICIPATION


#### Consultant

SBE 24.71%  
Local 100%  
WBE N/A  
MBE N/A

#### Contractor

SBE 12.75%  
Local 100%  
WBE N/A  
MBE N/A

### FUNDING

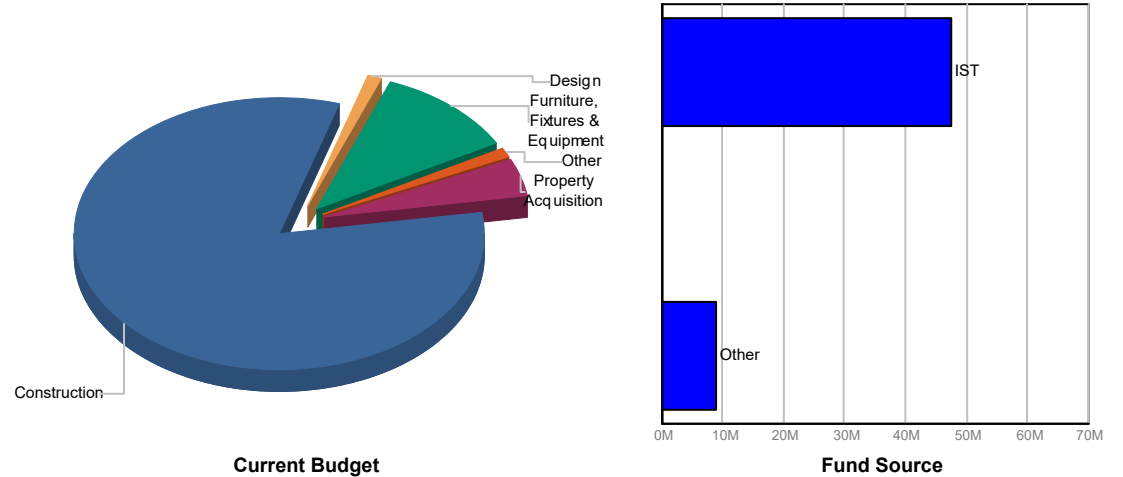

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Property Acquisition	\$2,537,653	\$2,478,256	97.66%	\$2,537,653
Design	\$667,425	\$83,588	12.52%	\$83,588
Construction	\$46,514,675	\$45,679,256	98.20%	\$45,672,332
Furniture, Fixtures & Equipment	\$6,365,963	\$5,381,821	84.54%	\$5,304,157
Other	\$544,359	\$469,672	86.28%	\$417,736
<b>TOTAL</b>	<b>\$56,630,075</b>	<b>\$54,092,594</b>	<b>95.52%</b>	<b>\$54,015,467</b>

### NOTES

Final pay application #41 is still pending due to the need for updated schedules and the Fire Alarm closeout documents. Kast staff is working to rectify.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Ocean Inlet Park and Marina Renovation

Project Number: 13367  
BCC District: 04  
Delivery Method: Hard Bid  
Category: P08-Public Building Repair Replacement & Expansion  
Status: Construction  
Designer: Alan Gerwig & Associates, Inc.  
Contractor: Poseidon  
Project Manager: Rich Avery

#### SCOPE

The project consists of the replacement of marina components as well as new components including bulkhead wall, floating docks, floating finger docks, fixed dock, boat lifts, floating wave attenuator, landscaping, and replacement of the current Marina/Restroom and concession buildings. The project will be constructed in two phases. Phase one will consist of marina bulkhead, dock reconstruction and wave attenuator construction. The remaining scope to be completed during phase 2.

Total available funding for this project consists of \$2,500,000 FY18 IST funds, \$2,500,000 FY20 Find Grant funds, \$3,200,000 FY23 IST funds, and \$5,408,000 FY24 IST funds.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Phase I Start	2/5/2018	2/4/2018
Design Start	10/22/2018	10/22/2018
Construction Start	12/3/2019	11/1/2021
Substantial Completion	11/1/2022	7/8/2024

#### PARTICIPATION



##### Consultant

SBE 82.50%  
Local 100%  
WBE N/A  
MBE N/A

##### Contractor

SBE 92.67  
Local 92.67  
WBE N/A  
MBE N/A

#### FUNDING

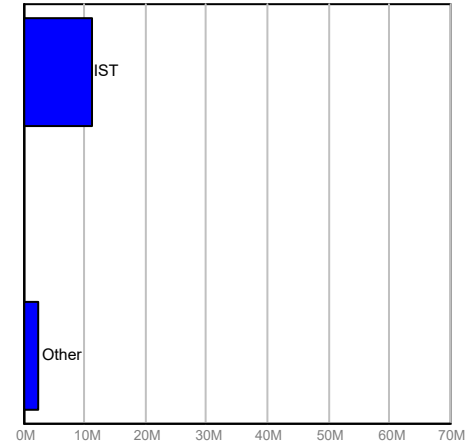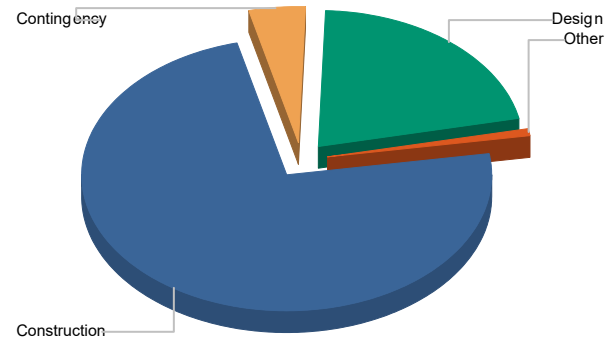

Current Budget

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,900,600	\$355,555	12.26%	\$310,290
Construction	\$10,027,806	\$1,803,329	17.98%	\$1,693,136
Other	\$108,500	\$136,715	126.00%	\$136,702
Contingency	\$600,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$13,636,906</b>	<b>\$2,295,599</b>	<b>16.83%</b>	<b>\$2,140,128</b>

#### NOTES

The dock platform extensions fabricator has provided preliminary design drawings and product data for the Southern dock extension for review. Currently awaiting the design drawing for the Northern dock extension, and the escape ladders are also to be installed. Fabrication and installation are still on track to be completed prior to the Memorial Day weekend. Negotiations with the General Contractor for the main project to resolve pending change proposals is continuing to be addressed.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title: Evidence Building**

Project Number: 14218  
BCC District: 03  
Delivery Method: Construction Management  
Category: S06-Sheriff - FDO  
Status: Close Out  
Designer: Leo Daly  
Contractor: Pirtle Construction  
Project Manager: Jeffrey Halverson

#### SCOPE

The project consists of a new 2-story Evidence Storage/Crime Scene/Crime Lab Facility (Approximately 87,000 GSF) and a 12,000 GSF metal building for impound vehicle storage. The main facility will house property seized by the Sheriff's Office, Administrative Offices, Evidence Processing via the crime scene investigation unit and the crime lab. Monitored cameras, motion detectors, and restricted access with electronic logging will be provided. The facility will accommodate secure vehicle garage bays that can store large vehicles (i.e. 56' long trailers) holding evidence for investigation or transport. Site Development (16 Acres) to include user parking (public, booking officers & staff), a fenced/gated impound lot (350 surface spaces). IST Funding: FY17 \$4,395,000 FY18 \$13,202,000 FY19 \$3,739,540. Other Fund: \$10,217,539.5

#### PHOTO



Palm Beach County Sheriff's Office Forensic Facility



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/30/2016	12/21/2016
Design Start	6/28/2017	6/28/2017
Construction Start	7/5/2018	4/29/2019
Substantial Completion	11/5/2019	10/30/2020
Project Completion	11/26/2019	

#### PARTICIPATION

##### Consultant

SBE 33.21%

Local 78.96%

WBE N/A

MBE N/A

##### Contractor


SBE 21.60%

Local 55%

WBE N/A

MBE N/A

#### FUNDING

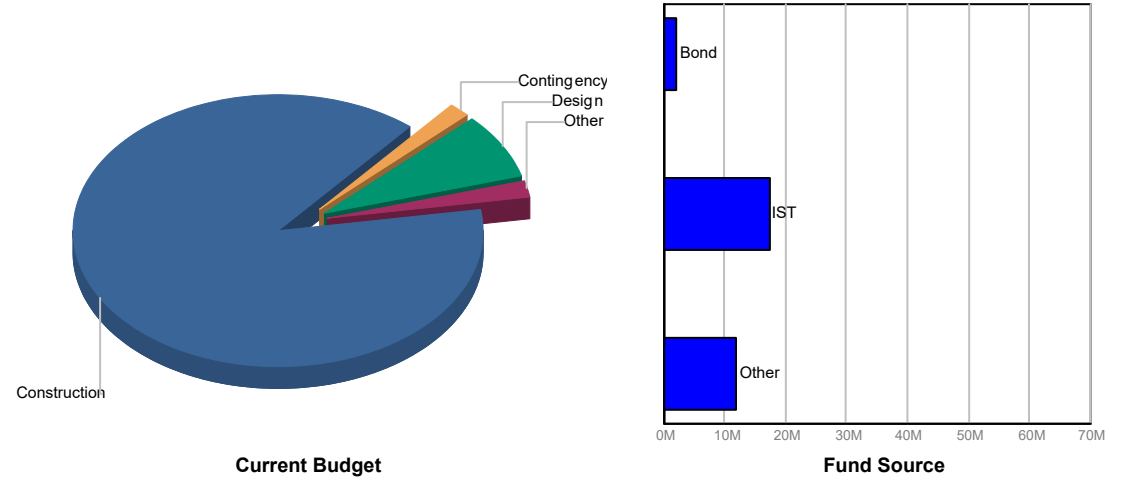

Current Budget

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,461,526	\$2,461,526	100.00%	\$2,452,041
Construction	\$27,998,127	\$27,998,128	100.00%	\$27,491,609
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$602,158	\$602,158	100.00%	\$602,158
Contingency	\$492,268	\$492,268	100.00%	\$492,268
<b>TOTAL</b>	<b>\$31,554,080</b>	<b>\$31,554,080</b>	<b>100.00%</b>	<b>\$31,038,077</b>

#### NOTES

The CM is preparing the proposal for the AHU #6 enhancements back-up power supply solution. PBSO has selected a replacement freezer and cooler for which the Architect is to prepare a redundant power supply system.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** CR 880 Canal Bank Stabilization

Project Number: 1448  
BCC District: 06  
Delivery Method: Bid Contract Award  
Category: C02-CR 880 Canal Bank Stabilization  
Status: Construction  
Designer: Wantman Group  
Contractor: Dickerson Florida, Inc.  
Project Manager: Holly Knight

#### SCOPE

This project will repair, restore, and stabilize the embankment along a portion of County Road 880. The South Florida Water Management District's L-13 Canal parallels and is very close to County Road 880. The embankment area for County Road 880 to the canal is minimal. The undermining of the County Road 880 embankment continues due to storm events and increased South Florida Water Management District pumping and has progressively deteriorated. Repair of the embankment is necessary to prevent the eventual collapse of County Road 880 and to ensure the integrity of County Road 880 and provide a safe roadway for the public.

IST Funds: FY17 \$1,000,000 FY18 \$2,000,000 FY24 \$2,000,000.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Construction Notice to Proceed	6/5/2017	6/5/2017
Phase III Construction Complete	11/2/2017	10/20/2017
Phase IV-Construction Notice to Proceed	6/1/2018	7/9/2018
Phase IV-Construction Complete	12/1/2018	3/27/2019
Phase V-Construction Notice to Proceed	6/1/2019	7/1/2019
Phase V-Construction Complete	12/1/2019	11/20/2019

#### PARTICIPATION


##### Consultant

SBE 15%  
Local 100%  
WBE 0%  
MBE 0%


##### Contractor

SBE 23.4%  
Local 23.4%  
WBE 0%  
MBE 0%

#### FUNDING

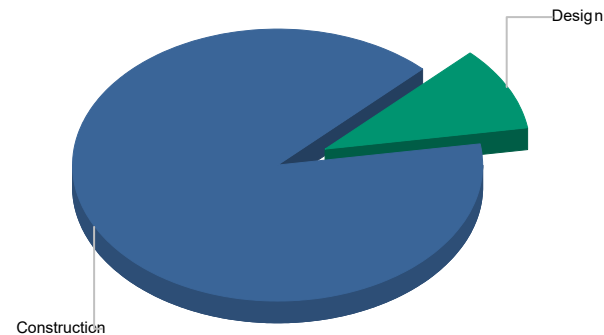

Current Budget

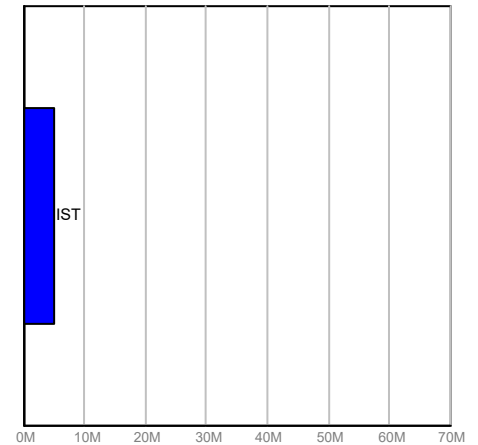

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$75,698	15.14%	\$75,698
Construction	\$4,500,000	\$2,544,219	56.54%	\$2,318,489
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$5,000,000</b>	<b>\$2,619,917</b>	<b>52.40%</b>	<b>\$2,394,188</b>

#### NOTES

Phases I and II (constructing adjacent locations) were completed in FY 2015 and FY 2016 using non-IST funding. Phase III construction is funded at \$1,000,000 in FY 2017. Construction for Phases IV & V are funded at \$2,000,000 in FY 2018. Construction is complete for Phases III, IV and V. Phase VI construction is delayed pending design review/revision and bid process.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** 6th Ave. So. over Lake Osborne (LWDD E-4 Canal)(S Br/ East bound) (934307)  
**Project Number:** 1464  
**BCC District:** 03  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Close Out  
**Designer:** Stantec  
**Contractor:** Ranger  
**Project Manager:** Will Carey

#### SCOPE

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes and barrier walls), improve roadway drainage, and enhance pedestrian sidewalk safety. The new bridge will also provide greater vertical clearance.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	7/17/2018	7/17/2018
Design Completion	12/1/2020	2/14/2021
Construction Bid Date	3/1/2021	5/4/2021
Construction Start	12/1/2021	2/14/2022
Construction Complete	5/1/2024	

#### PARTICIPATION


##### Consultant

SBE 25%  
Local 100%  
WBE 0%  
MBE 0%

##### Contractor

SBE 11%  
Local 100%  
WBE 0%  
MBE 0%

#### FUNDING

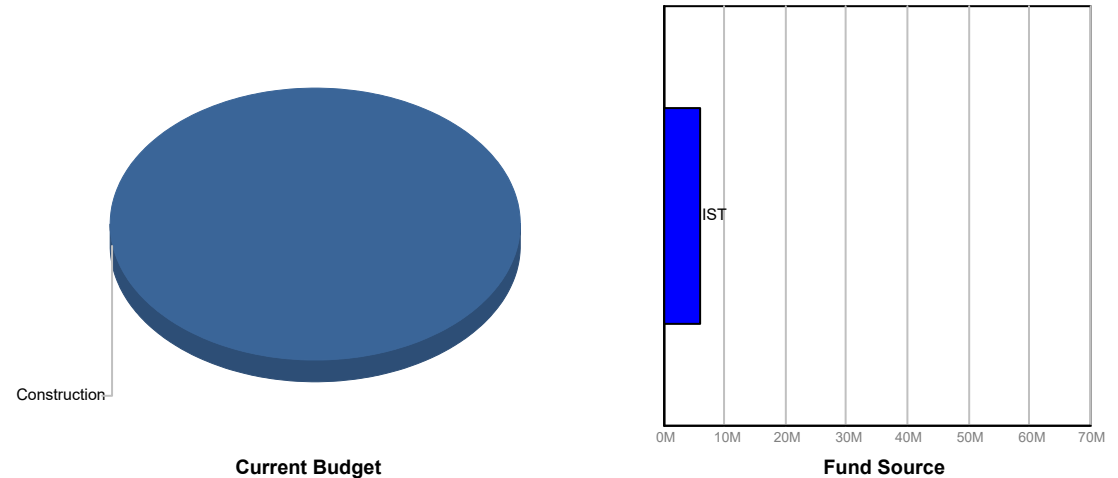

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$5,907,670	98.46%	\$5,761,982
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$5,907,670</b>	<b>98.46%</b>	<b>\$5,761,982</b>

#### NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using RP funds) is complete. The project was bid on 5/4/21 - with apparent low bid of \$ 11.1m The IST partially funds the construction of the project at \$6m in FY 2020. Construction is complete - working on closing documents.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> CR 880 (Old SR 80) Over C-51 Canal (930940)</p> <p>Project Number: 1480</p> <p>BCC District: 06</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Design</p> <p>Designer: Alan Gerwig &amp; Assoc.</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>This project will replace an existing bridge that was built over 80 years ago. The new bridge will improve traffic safety (lane widths and vehicle barrier walls). The current bridge is weight restricted.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Design Contract Notice to Proceed</td><td>11/9/2018</td><td>11/9/2018</td></tr><tr><td>Design Completion</td><td>12/1/2025</td><td></td></tr><tr><td>Construction Bid Date</td><td>4/1/2026</td><td></td></tr><tr><td>Construction Start</td><td>9/1/2026</td><td></td></tr><tr><td>Construction Complete</td><td>6/1/2028</td><td></td></tr></tbody></table>		Original	Actual	Design Contract Notice to Proceed	11/9/2018	11/9/2018	Design Completion	12/1/2025		Construction Bid Date	4/1/2026		Construction Start	9/1/2026		Construction Complete	6/1/2028		<p><b>Consultant</b></p> <p>SBE 94.3%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><div></div><div>IST</div></div> <p>0M 10M 20M 30M 40M 50M 60M 70M</p> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																		
Design Contract Notice to Proceed	11/9/2018	11/9/2018																		
Design Completion	12/1/2025																			
Construction Bid Date	4/1/2026																			
Construction Start	9/1/2026																			
Construction Complete	6/1/2028																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using 5-Year RP funds) is ongoing (80% complete). The construction of the project is currently estimated at \$5.8m. The IST partially funds the construction of the project at \$2.7m in FY 2019. The project is currently scheduled to begin construction in late FY25. The scheduled dates have been revised to depict design and permitting delays.</p>
	A	B	C=B/A	D	
Construction	\$2,700,000	\$13,710	0.51%	\$13,710	
TOTAL	\$2,700,000	\$13,710	0.51%	\$13,710	





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Main Detention Center Electronics

Project Number: 15218  
BCC District: 03  
Delivery Method: Construction Management  
Category: S06-Sheriff - FDO  
Status: Close Out  
Designer: Leo A. Daly  
Contractor: Hedrick Brothers Construction  
Project Manager: Jeffrey Halverson

#### SCOPE

Phase II - Electronics for the South, East, and West Towers at the Main Detention Center, which have continually operated since the early 1980's. These systems include door controls, intercom, nurse's call system, CCTV, upgrade of EST3 software for fire alarm and new infrastructure for the future expansion of the CCTV system.  
Main Detention Center Electronics (B594) IST Funding  
FY 2017 IST \$5,600,000  
FY 2018 IST \$4,700,000  
FY 2024 IST \$ 1,256,600  
Ad Valorem \$1,021,161

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	7/9/2015	6/9/2015
Design Start	6/21/2016	6/21/2016
Construction Start	3/19/2018	5/17/2018
Substantial Completion	3/15/2022	8/10/2020
Project Completion	6/30/2022	

#### PARTICIPATION


##### Consultant

SBE 22.60%  
Local 67%  
WBE N/A  
MBE N/A

##### Contractor

SBE 76.79%  
Local 80%  
WBE N/A  
MBE N/A

#### FUNDING

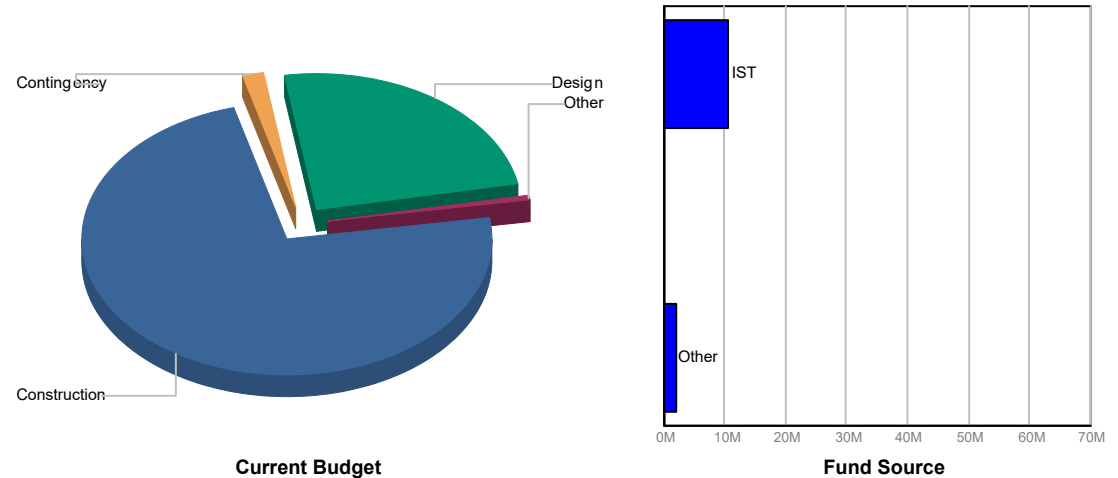

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,096,507	\$3,053,730	98.62%	\$2,933,781
Construction	\$9,210,331	\$7,227,727	78.47%	\$7,189,534
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$55,740	\$62,260	111.70%	\$62,260
Contingency	\$215,183	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$12,577,761</b>	<b>\$10,343,717</b>	<b>82.24%</b>	<b>\$10,185,575</b>

#### NOTES

The closeout target date is delayed pending Fire Marshal approval. The remaining funds will be used for replacement of the fire alarm system, which is now approaching end of life.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

**Project Title:** Palm Beach Lakes Blvd over FEC R/R

Project Number: 1532  
 BCC District: 07  
 Delivery Method: Design CCNA  
 Category: B04-Bridge Modifications  
 Status: Design  
 Designer: HNTB  
 Contractor: TBD  
 Project Manager: Maroun Azzi

### SCOPE

This project will rehabilitate an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, pedestrian barrier, railings) and may involve other improvements such as shoulders, bike lanes, and sidewalks.  
 FY 2017 IST \$1,500,000  
 FY 2021 IST \$4,500,000  
 FY 2025 IST \$8,300,000

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
Project Start	9/30/2017	9/30/2017
Consultant Procurement Finish	9/3/2019	12/1/2019
Study Start	4/7/2020	4/7/2020
Design Complete	4/1/2026	
Permit Application	6/1/2024	
Permit Issued	12/25/2025	
Construction Start	1/1/2027	
Construction Complete	1/1/2029	
Study Complete	5/1/2022	4/1/2022
Design Start	4/1/2023	5/10/2023

### PARTICIPATION


#### Consultant

SBE 36.5%  
 Local 96%  
 WBE TBD  
 MBE TBD


#### Contractor

SBE TBD  
 Local TBD  
 WBE TBD  
 MBE TBD

### FUNDING

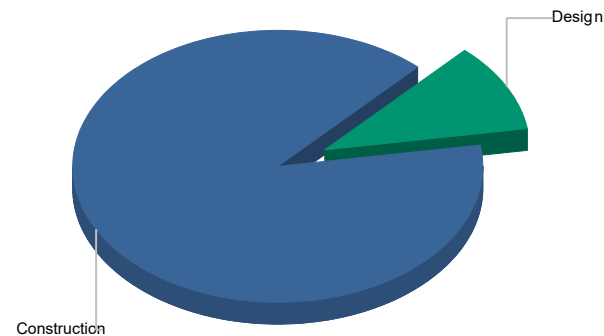

Current Budget

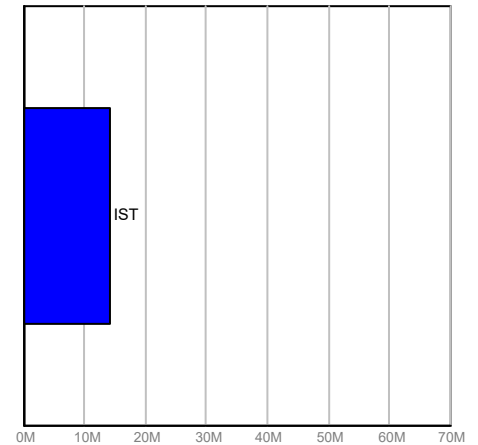

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$1,608,316	107.22%	\$574,350
Construction	\$12,800,000	\$61,011	0.48%	\$61,011
Other	\$0	\$15,327	0.00%	\$15,327
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$14,300,000</b>	<b>\$1,684,654</b>	<b>11.78%</b>	<b>\$650,688</b>

### NOTES

Initial coordination has been completed with stakeholders including the City of West Palm Beach and the Community Redevelopment Agency to determine scope and design parameters for the rehabilitation of the bridge superstructure. Design is ongoing (35% complete). The scheduled dates have been revised to depict coordination, planning, and scope delays.





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Sections of Jog Road

Project Number: 1537  
BCC District: Multiple  
Delivery Method: Annual Striping Contract  
Category: S16-Striping  
Status: Construction  
Designer: N/A  
Contractor: Oglesby  
Project Manager: Larry Kelly

#### SCOPE

This project consists of restriping sections of Jog Road.

FY 2017 \$350,000  
FY 2021 \$150,000  
FY 2022 \$100,000  
FY 2023 \$100,000  
FY 2024 \$200,000  
FY 2026 \$200,000

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Summit to Gun Club Complete	9/20/2017	9/20/2017
PGA to Hood Complete	10/31/2017	10/31/2017
10th Avenue N. to Summit Complete	1/22/2018	1/22/2018
Wallis to Roebuck Complete	3/7/2018	3/7/2018
Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018
Glades to NW 55th St.	3/19/2019	3/19/2019
Hood to Donald Ross	12/2/2020	12/12/2020
N. Oriole to Lake Ida	4/3/2021	3/9/2021
Beeline to Northlake	5/11/2023	5/11/2023
Yamato to Clint Moore	11/3/2023	11/3/2023
45th Street to Beeline	2/7/2025	2/7/2025

#### PARTICIPATION

##### Consultant

SBE N/A

Local N/A

WBE N/A

MBE N/A

##### Contractor


SBE 61%

Local 61%

WBE 0%

MBE 0%

#### FUNDING

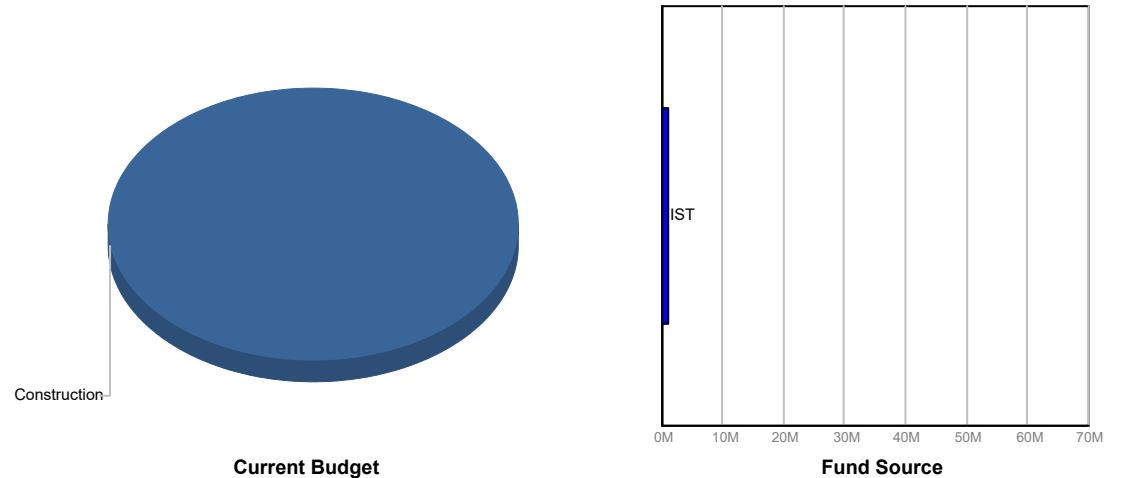

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$1,100,000	\$494,448	44.95%	\$494,448
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,100,000</b>	<b>\$494,448</b>	<b>44.95%</b>	<b>\$494,448</b>

#### NOTES

Jog Road is a North-South major County thoroughfare. This project consists of re-striping sections of Jog Road. Restriping continues on an as needed basis.






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Brown's Farms Road</p> <p>Project Number: 1540 BCC District: 06 Delivery Method: Annual Construction Contract Category: R04-Resurfacing Status: Construction Designer: N/A Contractor: Community Project Manager: Darren Prainito</p>	<p>Resurfacing approximately 2 miles (4 lane miles) of a portion of Brown's Farm Road from CR 880 to South Terminus each year.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																														
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>FY 2017 Construction Complete</td><td>12/22/2017</td><td>12/22/2017</td></tr><tr><td>FY 2018 Construction Complete</td><td>12/1/2018</td><td>11/30/2018</td></tr><tr><td>FY 2019 Construction Complete</td><td>12/31/2019</td><td>11/1/2019</td></tr><tr><td>FY 2020 Construction Complete</td><td>12/18/2020</td><td>12/2/2020</td></tr><tr><td>FY2021 Construction Complete</td><td>12/17/2021</td><td>10/18/2021</td></tr><tr><td>FY 2022 Construction Complete</td><td>12/22/2022</td><td>7/19/2022</td></tr><tr><td>FY 2023 Construction Complete</td><td>12/19/2023</td><td>12/1/2023</td></tr><tr><td>FY 2024 Construction Complete</td><td>12/24/2024</td><td>1/9/2025</td></tr><tr><td>FY 2025 Construction Complete</td><td>12/24/2025</td><td></td></tr></tbody></table>		Original	Actual	FY 2017 Construction Complete	12/22/2017	12/22/2017	FY 2018 Construction Complete	12/1/2018	11/30/2018	FY 2019 Construction Complete	12/31/2019	11/1/2019	FY 2020 Construction Complete	12/18/2020	12/2/2020	FY2021 Construction Complete	12/17/2021	10/18/2021	FY 2022 Construction Complete	12/22/2022	7/19/2022	FY 2023 Construction Complete	12/19/2023	12/1/2023	FY 2024 Construction Complete	12/24/2024	1/9/2025	FY 2025 Construction Complete	12/24/2025		<p><b>Consultant</b></p> <p>SBE N/A Local N/A WBE N/A MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 7.4% Local 94.4% WBE 0% MBE 0%</p>	<div><div></div><div>IST</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																														
FY 2017 Construction Complete	12/22/2017	12/22/2017																														
FY 2018 Construction Complete	12/1/2018	11/30/2018																														
FY 2019 Construction Complete	12/31/2019	11/1/2019																														
FY 2020 Construction Complete	12/18/2020	12/2/2020																														
FY2021 Construction Complete	12/17/2021	10/18/2021																														
FY 2022 Construction Complete	12/22/2022	7/19/2022																														
FY 2023 Construction Complete	12/19/2023	12/1/2023																														
FY 2024 Construction Complete	12/24/2024	1/9/2025																														
FY 2025 Construction Complete	12/24/2025																															

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>Brown's Farm Road is approximately 14 miles in length. This project entails resurfacing a portion of Brown's Farm Road each year. Construction complete for FY2017 thru 2024.</p>
	A	B	C=B/A	D	
Design	\$0	\$1,588	0.00%	\$1,588	
Construction	\$2,300,000	\$1,820,163	79.14%	\$1,820,163	
Contingency	\$0	\$0	0.00%	\$0	
<b>TOTAL</b>	<b>\$2,300,000</b>	<b>\$1,821,751</b>	<b>79.21%</b>	<b>\$1,821,751</b>	



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Prosperity Farms Rd. over SFWMD C-17 Canal (934116)

Project Number: 1555

BCC District: 01

Delivery Method: Design CCNA

Category: B08-Bridge Replacements

Status: Design

Designer: Scalar

Contractor: TBD - (bid)

Project Manager: Will Carey

#### SCOPE

This project will replace an existing bridge that was built over 60 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety. Note the current bridge is weight restricted.

FY 2018 IST \$500,000

FY 2021 IST \$1,500,000

FY 2022 IST \$6,000,000

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/19/2019	11/19/2019
Design Completion	7/1/2025	
Construction Bid Date	11/1/2025	
Construction Start	2/6/2026	
Construction Complete	2/1/2028	

#### PARTICIPATION

##### Consultant

SBE 98%

Local 100%

WBE 0%

MBE 0%

##### Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

#### FUNDING

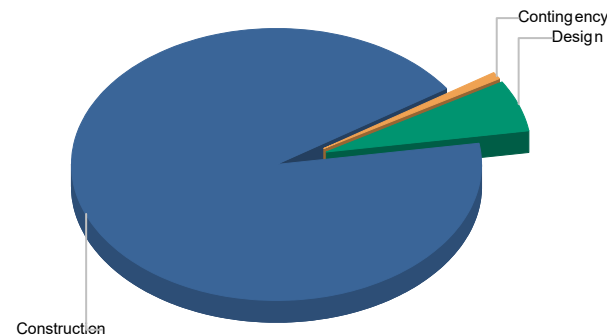

Current Budget

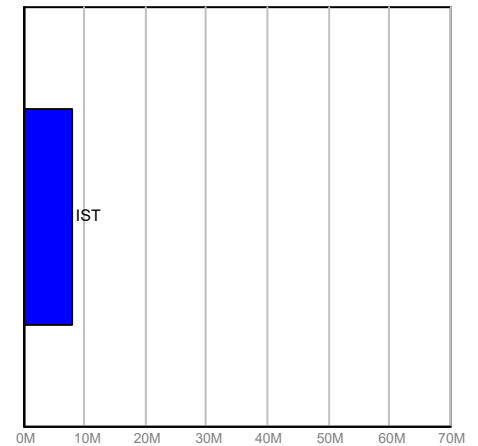

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$496,323	99.26%	\$422,436
Construction	\$7,450,000	\$10,810	0.15%	\$10,794
Contingency	\$50,000	\$8,365	16.73%	\$8,365
<b>TOTAL</b>	<b>\$8,000,000</b>	<b>\$515,498</b>	<b>6.44%</b>	<b>\$441,595</b>

#### NOTES

Design is ongoing (95% complete). The scheduled dates have been revised to depict design and permitting delays. It is anticipated that a Florida Department of Environmental Protection (FDEP) Resiliency grant of \$4m will be received for the project.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Belvedere Rd over E-3 canal (934205 & 934206)

**Project Number:** 1556

**BCC District:** 02

**Delivery Method:** Design CCNA

**Category:** B08-Bridge Replacements

**Status:** Design

**Designer:** Stantec

**Contractor:** TBD (bid)

**Project Manager:** Maroun Azzi

This project will replace the existing bridges that were built over 40 years ago. The new bridge(s) will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.

FY 2018 IST \$450,000  
FY 2021 IST \$1,350,000  
FY 2022 IST \$300,000



### SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	10/22/2019	10/22/2019
Design Completion	6/1/2025	
Construction Bid Date	10/1/2025	
Construction Start	3/1/2026	
Construction Complete	12/1/2027	

### PARTICIPATION

#### Consultant

SBE 30%

Local 100%

WBE 0%

MBE 0%

#### Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

### FUNDING

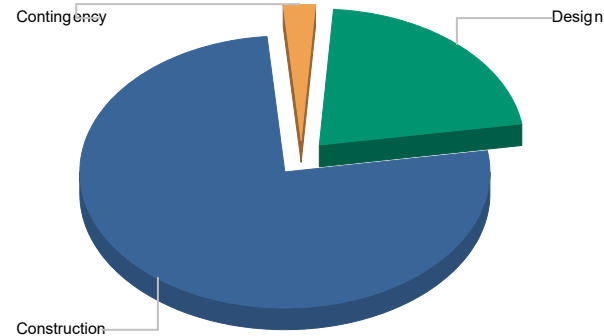

Current Budget

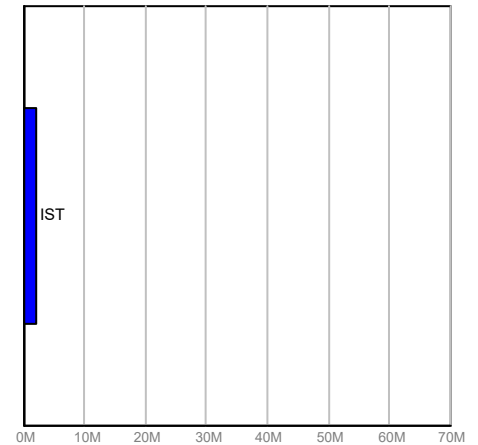

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$450,000	\$402,311	89.40%	\$282,540
Construction	\$1,600,000	\$212,801	13.30%	\$5,770
Contingency	\$50,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,100,000</b>	<b>\$615,113</b>	<b>29.29%</b>	<b>\$288,310</b>

### NOTES

Design is ongoing (90% complete). The scheduled dates have been revised to reflect design and permitting delays.





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Various other locations Countywide

Project Number: 1558  
BCC District: Multiple  
Delivery Method: Annual Construction Contract  
Category: D02-Drainage (Pipe Replacements)  
Status: Construction  
Designer: N/A  
Contractor: Hinterland  
Project Manager: Darren Prainito

#### SCOPE

This project will repair and/or replace existing pipe culverts and drainage structures along various roads and canals Countywide. These repairs are needed in order to properly drain and maintain the various roads and canals in a safe operating condition.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Jupiter Farms (133rd Rd. & 156th St.)	8/1/2018	3/12/2018
1069 Edgehill Road	8/15/2018	6/12/2018
Limestone Creek & Palm Garden St.	8/1/2018	7/17/2018
3261 Atlantic Road	8/15/2018	7/1/2018
Van Buren Road @ E-3 Canal	8/1/2018	6/15/2018
19506 Trails End Terrace	8/1/2018	5/11/2018
Jupiter Farms (4 locates)	10/15/2018	8/21/2018
6361 Wood Lake Rd./19650 Red Maple F	10/1/2018	10/1/2018
19598 Trails End Terrace	9/15/2018	8/20/2018
19582 Trails End Terrace	9/1/2018	9/1/2018
6558 Wood Lake Road	9/15/2018	9/14/2018
6126 Wood Lake Road	10/15/2018	12/12/2018
6528 Wood Lake Road	11/1/2018	12/12/2018

#### PARTICIPATION


##### Consultant

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

##### Contractor

SBE 100%  
Local 100%  
WBE 0%  
MBE 0%

#### FUNDING

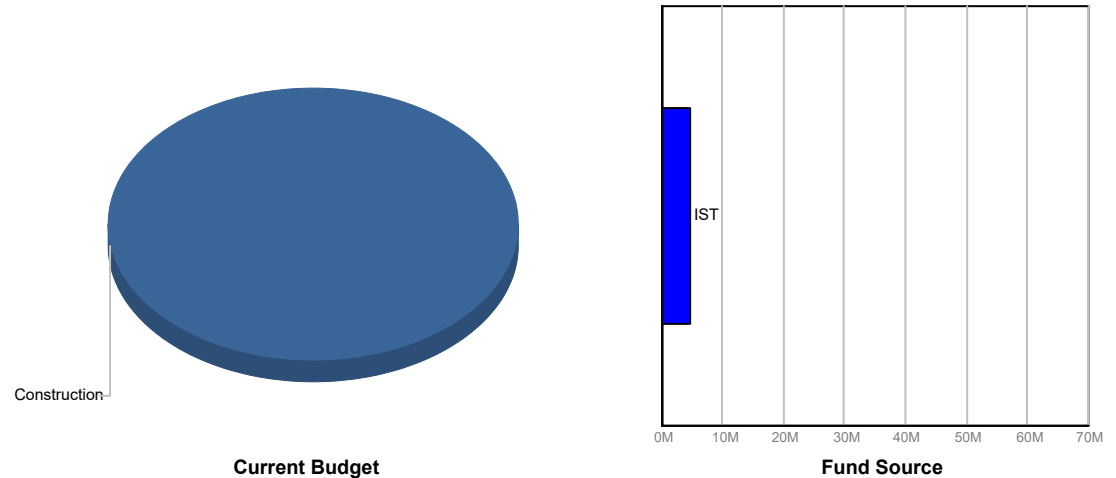

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$4,700,000	\$4,188,266	89.11%	\$3,923,610
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$4,700,000</b>	<b>\$4,188,266</b>	<b>89.11%</b>	<b>\$3,923,610</b>

#### NOTES

This project is funded in:  
FY 2018 \$500,000, FY 2021 \$500,000, FY 2022 \$200,000  
FY 2023 \$200,000, FY 2024 \$3,200,000, FY 2025 \$100,000

The total project is estimated at \$4,700,000.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Video Detection (80 +/- intersection)

Project Number: 1580  
BCC District: Multiple  
Delivery Method: Annual Traffic Signals Contract  
Category: S08-Signals and Signal Systems  
Status: Construction  
Designer: N/A  
Contractor: Gerelco  
Project Manager: Fattoush Jafar

#### SCOPE

This project will replace the traffic detection at numerous signalized intersections from the existing inductive loop system to video detection. The video detection system is more reliable and easier to maintain.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Military Tr. & Garden Lake	8/1/2018	11/21/2018
Gateway & Renaissance Commons	9/1/2018	4/3/2019
Australian & Turnage	10/1/2018	1/7/2019
Woolbright & Hagen Ranch	11/1/2018	4/4/2019
Belvedere & Country Club Road	12/1/2018	4/4/2019
Palm Beach Lakes & Wellesley	1/1/2019	4/4/2019

#### PARTICIPATION

##### Consultant

SBE N/A

Local N/A

WBE N/A

MBE N/A

##### Contractor


SBE 0%

Local 23%

WBE 0%

MBE 0%

#### FUNDING

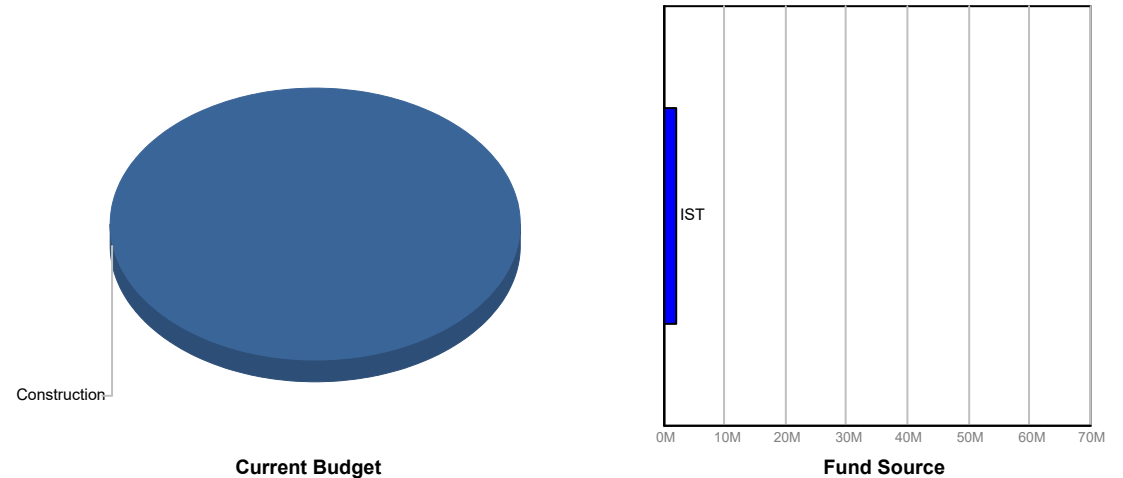

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,200,000	\$202,397	9.20%	\$202,397
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$2,200,000</b>	<b>\$202,397</b>	<b>9.20%</b>	<b>\$202,397</b>

#### NOTES

Work has been completed at six intersections. This project is funded in:

FY 2018 \$200,000

FY 2023 \$300,000

FY 2024 \$800,000

FY 2026 \$900,000

The total project is estimated at \$2,200,000.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** CW Street Lighting FY18 frmly Hypoluxo Rd (Hagen Ranch Rd to I-95)

Project Number: 1581  
BCC District: CW  
Delivery Method: Florida Power and Light  
Category: S14-Street Lighting  
Status: Construction  
Designer: Florida Power and Light  
Contractor: Florida Power and Light  
Project Manager: May Cheng

#### SCOPE

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Gun Club Road/Bosque to Congress	7/19/2019	7/19/2019
Congress/Okeechobee to Belvedere	8/1/2019	8/1/2019
10th Avenue North/Haverhill to Kirk		
Community/Haverhill to Military	7/31/2019	7/31/2019
Haverhill Road/WPB City to Haverhill City	7/20/2023	7/20/2023
Glades Road/State Road 7 to Boca Rio	12/9/2022	12/9/2022
Boynton Beach Boulevard/Turnpike to Kn	3/31/2023	3/31/2023
Jog Road/Belvedere to State Road 80	5/3/2021	5/3/2021
Forest Hill/Turnpike to Pinehurst & Jog to		
Haverhill/State Road 80 to Lake Worth	7/13/2023	7/13/2023
Congress/Lantana to Hypoluxo & Gun Cl		
Gateway/Military to Windward		
Belvedere Road/RPB City to Haverhill Cit	6/6/2023	6/6/2023

#### PARTICIPATION


##### Consultant

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

##### Contractor

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

#### FUNDING

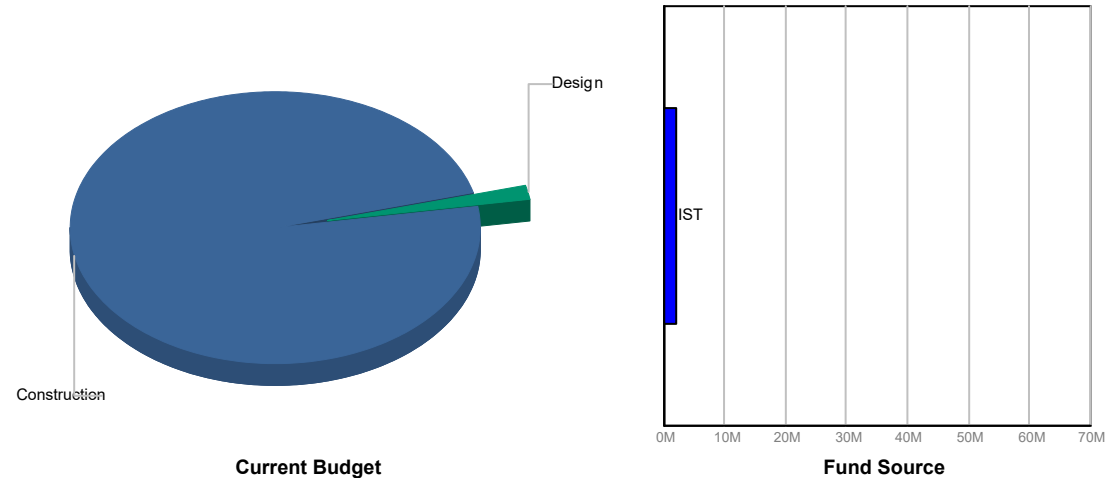

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$30,000	\$35,184	117.28%	\$35,184
Construction	\$1,920,000	\$1,785,737	93.01%	\$1,716,599
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,950,000</b>	<b>\$1,820,922</b>	<b>93.38%</b>	<b>\$1,751,784</b>

#### NOTES

There are 16 street lighting projects (road segments) funded (\$1,950,000) for conversion in FY 2018. All 16 projects have been forwarded to FPL requesting final design and installation. As of 1/18/24, 11 projects have been completed.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Courthouse Electronics System R&R/Command Center

**Project Number:** 16208

**BCC District:** 07

**Delivery Method:** Construction Management

**Category:** J02-Judicial

**Status:** Close Out

**Designer:** TLC Engineering

**Contractor:** Hedrick Brothers Construction Co., Inc.

**Project Manager:** Rich Avery

Security Systems replacement at the Main County Courthouse including the Security Management System, Access Control System, CCTV system, Duress System, Intercom, Elevator Override, and Fire Alarm. The Project will also include addressing the emergency egress procedures for the facility, as well as build-out for the expansion of the 4th floor Command Center.

Total IST, and Ad Valorem funding for this project is \$16,514,475; Total IST funds are \$12,999,700, which are comprised of FY17 IST funds of \$1,300,000 and FY18 IST funds of \$8,699,700 and FY 19 IST funds of \$3,000,000. Ad Valorem funds are \$3,449,845



### SCHEDULE SUMMARY

	Original	Actual
Project Start	2/19/2016	2/19/2016
Design Start	2/15/2017	2/15/2017
Construction - Start	11/26/2018	1/7/2019
Substantial Completion	2/1/2021	5/21/2021
Project Completion	4/1/2021	

### PARTICIPATION

#### Consultant

SBE 13.4%

Local 100%

WBE N/A

MBE N/A

#### Contractor


SBE 25%

Local 100%


WBE N/A

MBE N/A

### FUNDING

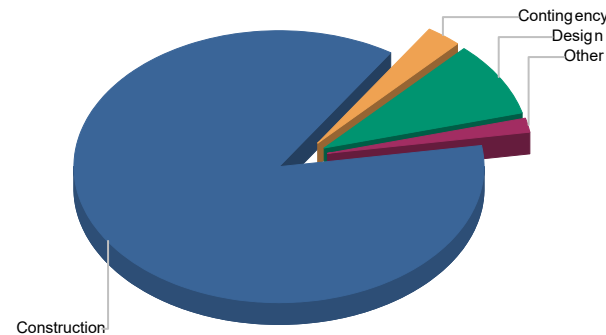

Current Budget

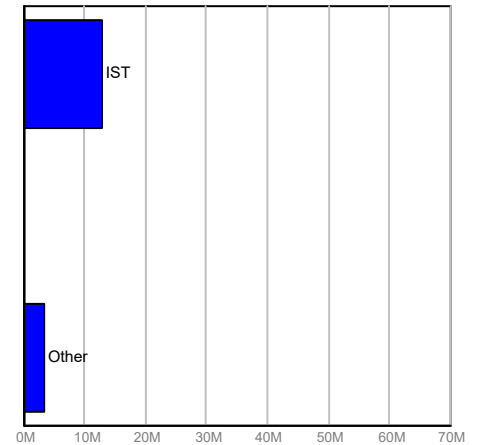

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,456,336	\$1,342,276	92.17%	\$949,155
Construction	\$14,306,620	\$14,281,321	99.82%	\$12,795,750
Furniture, Fixtures & Equipment	(\$142,784)	(\$23,996)	16.81%	\$0
Other	\$285,139	\$116,316	40.79%	\$116,316
Contingency	\$465,300	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$16,370,611</b>	<b>\$15,715,917</b>	<b>96.00%</b>	<b>\$13,861,221</b>

### NOTES

Missing schedule 3 and 4's remain to be provided. CID PM has reminded the CM to provide these documents. Once received and reviewed the final pay application will be ready for submission for approval.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** FY 2019 Street Lighting LED Replacements - Countywide  
**Project Number:** 1627  
**BCC District:** Multiple  
**Delivery Method:** Florida Power and Light  
**Category:** S14-Street Lighting  
**Status:** Construction  
**Designer:** Florida Power and Light  
**Contractor:** Florida Power and Light  
**Project Manager:** May Cheng

#### SCOPE

These projects replace the high pressure sodium lights with LED lights. Many of the street lights along County roads are owned and maintained by FPL with the County paying all the operation and maintenance costs. FPL will be responsible for final design and installation and the County will reimburse FPL.  
IST \$820,000 FY19  
IST \$300,000 FY24

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Melaleuca Lane/Greenacres limits to Kirk		
Linton/Military to Jog		
Jog Rd/SR80 to Forest Hill	7/19/2023	7/19/2023
Jog Rd/Gateway to Woolbright	4/30/2024	4/30/2024
Jog Rd/Lake Ida to Old Clint Moore		
Lantana Rd/Turnpike to High Ridge		

#### PARTICIPATION


##### Consultant

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

##### Contractor

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

#### FUNDING

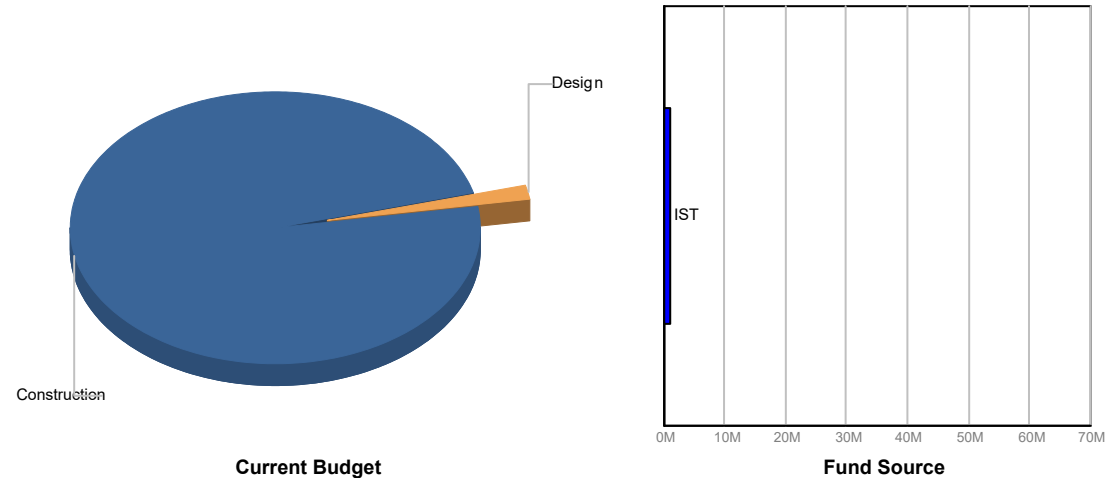

Current Budget

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$20,000	\$107	0.54%	\$107
Construction	\$1,100,000	\$1,044,305	94.94%	\$329,783
<b>TOTAL</b>	<b>\$1,120,000</b>	<b>\$1,044,413</b>	<b>93.25%</b>	<b>\$329,890</b>

#### NOTES

There are 6 street lighting projects (road segments) funded (\$820,000) for conversion in FY 2019. All 6 projects have been forwarded to FPL requesting final design and installation . A Budget Transfer (BT 24-0636) was approved on 6/4/24 that increased the funding by \$300,000. As of 9/1/24, 2 projects have been completed. The result of the lighting conversion to LED will provide a cost savings, better quality illumination and a more desirable environmental light source.





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Corkscrew Blvd. over SFWMD Miami Canal  
**Project Number:** 1656  
**BCC District:** 06  
**Delivery Method:** Design CCNA  
**Category:** B08-Bridge Replacements  
**Status:** Design  
**Designer:** Alan Gerwig & Associates  
**Contractor:** TBD  
**Project Manager:** Carlos Bojorge

#### SCOPE

This project will replace an existing bridge that as built over 70 years ago. The project will improve traffic safety (lane widths, sidewalks, etc.) and improve embankment/slope protection. Note the current bridge is weight restricted.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	8/15/2023	8/15/2023
Consultant Procurement Finish	4/1/2024	4/1/2024
Design Start	7/2/2024	8/20/2024
Design Complete	8/1/2026	
Permit Application	7/1/2025	
Permit Issued	8/1/2026	
Construction Start	4/1/2027	
Construction Complete	9/1/2028	

#### PARTICIPATION


##### Consultant

SBE 18.9%  
Local 100%  
WBE 0%  
MBE 14.8%

##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

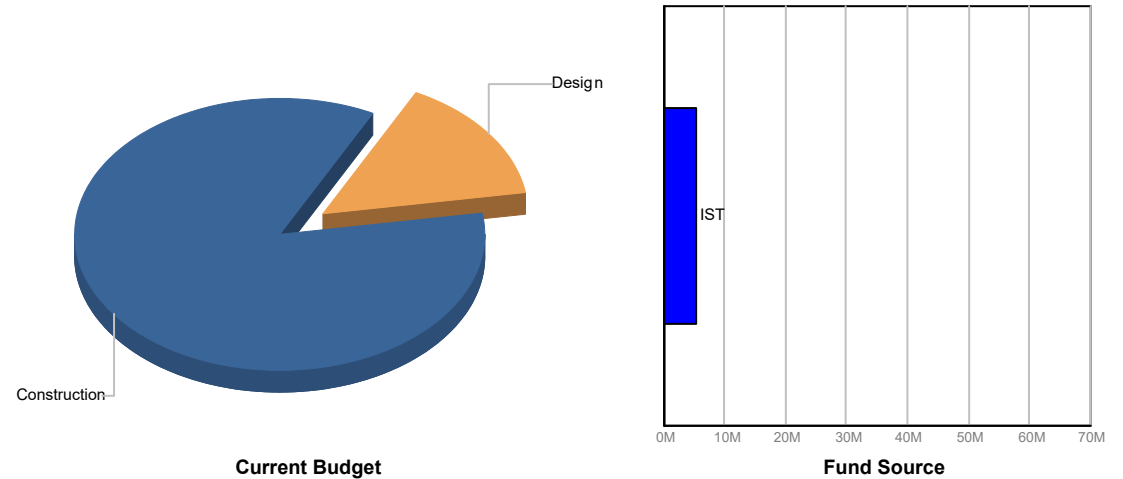

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$800,000	\$1,437	0.18%	\$1,437
Construction	\$4,575,000	\$390,053	8.53%	\$65,141
<b>TOTAL</b>	<b>\$5,375,000</b>	<b>\$391,490</b>	<b>7.28%</b>	<b>\$66,578</b>

#### NOTES

The project is funded for design (\$800k) in FY22 and for construction (\$4.575m) in FY25. Design is ongoing (5% complete).



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Jupiter Beach Rd. over Branch of ICWW

Project Number: 1657  
BCC District: 01  
Delivery Method: Design CCNA  
Category: B08-Bridge Replacements  
Status: Design  
Designer: Alan Gerwig & Associates  
Contractor: TBD  
Project Manager: Maroun Azzi

#### SCOPE

This project will replace an existing bridge that was built over 60 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	4/1/2022	4/13/2022
Consultant Procurement Finish	2/1/2023	1/10/2023
Design Start	5/1/2023	1/23/2023
Design Complete	12/1/2025	
Construction Start	6/1/2026	
Construction Complete	12/1/2027	

#### PARTICIPATION


##### Consultant

SBE 90%  
Local 100%  
WBE 0%  
MBE 0%

##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

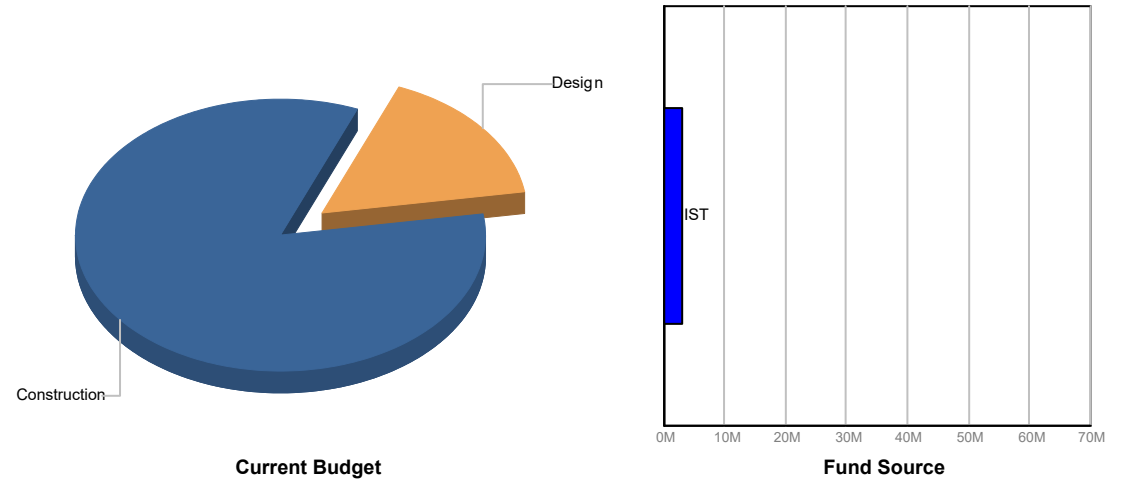

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$303,797	60.76%	\$177,726
Construction	\$2,529,000	\$9,823	0.39%	\$9,823
<b>TOTAL</b>	<b>\$3,029,000</b>	<b>\$313,620</b>	<b>10.35%</b>	<b>\$187,549</b>

#### NOTES

The project is funded for design (\$500k) in FY22 and for construction (\$2.5m) in FY25. Design is ongoing (15% complete)




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Australian Ave. from Banyan St. to 45th St.</p> <p>Project Number: 1658</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: HSQ</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>The project will include drainage improvements (pipd drainage system) and a new paving surface for a wider 4-lane divided section with new pathways on both sides along Australian Avenue from Banyan Blvd. to 45th Street. The work scope may also include replacing the twin bridges over Clear Lake (possible culverts) and replacing the twin bridges over the Carver Canal.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Design Start</td><td>3/1/2022</td><td>4/12/2022</td></tr><tr><td>Design Complete</td><td>6/1/2024</td><td>9/1/2024</td></tr><tr><td>Construction Bid Date</td><td>6/1/2025</td><td></td></tr><tr><td>Construction Start</td><td>10/1/2025</td><td></td></tr><tr><td>Construction Complete</td><td>4/1/2028</td><td></td></tr></table>		Original	Actual	Design Start	3/1/2022	4/12/2022	Design Complete	6/1/2024	9/1/2024	Construction Bid Date	6/1/2025		Construction Start	10/1/2025		Construction Complete	4/1/2028		<p><b>Consultant</b></p> <p>SBE 90.4%</p> <p>Local 100%</p> <p>WBE 0.4%</p> <p>MBE 5.6%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																		
Design Start	3/1/2022	4/12/2022																		
Design Complete	6/1/2024	9/1/2024																		
Construction Bid Date	6/1/2025																			
Construction Start	10/1/2025																			
Construction Complete	4/1/2028																			

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Design is complete. The bid process and preparation is ongoing. The project is funded for design (\$2m) in FY21 and for construction (\$15.8m) in FY24 and FY25. The total cost of the project is estimated at over \$30m. It is anticipated that a Florida Department of Environmental Protection (FDEP) Resiliency grant of \$13.4m will be received for the project. Project was bid on 12/19/24 but only 1 bid was received. Project will be rebid.				
	A	B	C=B/A	D					
Design	\$2,000,000	\$1,792,586	89.63%	\$1,450,052					
Construction	\$15,800,000	\$2,999,644	18.99%	\$534,324					
TOTAL	\$17,800,000	\$4,792,229	26.92%	\$1,984,376					




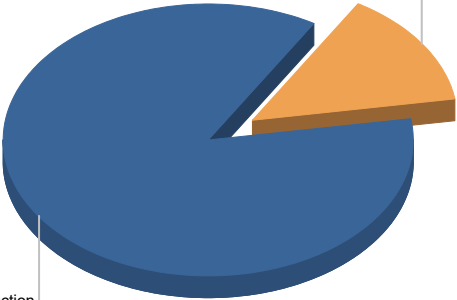

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Belvedere Rd canal piping &amp; sidewalk addition (62nd Dr. N. to Haverhill park)</p> <p>Project Number: 1661</p> <p>BCC District: 02</p> <p>Delivery Method: Design CCNA</p> <p>Category: P04-Pathways</p> <p>Status: Design</p> <p>Designer: Keshavarz</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>This project will add a new sidewalk (SW) on the south side of Belvedere Road from 62nd Dr. N. to the Haverhill park (just east of the E-3 Canal) - connecting to the existing south SW at the park's frontage. The SW may require the piping of Lake Worth Drainage District's (LWDD) L-3 Canal.</p> <p>FY 2021 IST \$500,000</p> <p>FY 2024 IST \$3,100,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Study Complete</td><td>4/20/2025</td><td></td></tr><tr><td>Design Complete</td><td></td><td></td></tr><tr><td>Construction Bid Date</td><td></td><td></td></tr><tr><td>Construction Start</td><td></td><td></td></tr><tr><td>Construction Complete</td><td></td><td></td></tr></table>		Original	Actual	Study Complete	4/20/2025		Design Complete			Construction Bid Date			Construction Start			Construction Complete			<p><b>Consultant</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><p>Design</p><p>Construction</p></div> <div><p>IST</p><p>0M 10M 20M 30M 40M 50M 60M 70M</p></div>
	Original	Actual																		
Study Complete	4/20/2025																			
Design Complete																				
Construction Bid Date																				
Construction Start																				
Construction Complete																				

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Design	\$500,000	\$95,021	19.00%	\$86,100	
Construction	\$3,100,000	\$17,873	0.58%	\$17,873	
TOTAL	\$3,600,000	\$112,894	3.14%	\$103,973	The project is in the study phase to determine a more precise work scope. The project is funded for design (\$500k) in FY21 and for construction (\$3.1M) in FY24.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Congress Ave. from Palm Beach Lakes to 45th St.</p> <p>Project Number: 1664</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Darren Prainito</p>	<p>Resurfacing 2.6 miles (11.4 lane miles) of Congress Avenue from Palm Beach Lakes Boulevard to 45th Street.</p> <p>FY2021 IST \$1,000,000</p> <p>FY2024 IST \$250,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>12/1/2023</td><td>4/24/2024</td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>2/14/2024</td><td>10/11/2024</td></tr><tr><td>Traffic Striping Complete</td><td>1/1/2024</td><td>5/24/2024</td></tr><tr><td>Traffic Loops Complete</td><td>4/1/2024</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	12/1/2023	4/24/2024	ADA (Curb/Cut Ramps) Complete	2/14/2024	10/11/2024	Traffic Striping Complete	1/1/2024	5/24/2024	Traffic Loops Complete	4/1/2024		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div><div>0M10M20M30M40M50M60M70M</div><div>Fund Source</div></div> <div><div>Construction</div><div>Current Budget</div></div>
	Original	Actual															
Milling and Pavement Complete	12/1/2023	4/24/2024															
ADA (Curb/Cut Ramps) Complete	2/14/2024	10/11/2024															
Traffic Striping Complete	1/1/2024	5/24/2024															
Traffic Loops Complete	4/1/2024																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$1,250,000	\$921,793	73.74%	\$921,793	
TOTAL	\$1,250,000	\$921,793	73.74%	\$921,793	






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Garden Rd. from Bee Line Hwy. to Investment Ln.</p> <p>Project Number: 1672</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Hinterland</p> <p>Project Manager: Darren Prainito</p>	<p>Resurfacing 1.9 miles (3.8 lane miles) of Garden Road from Bee Line Hwy. to Investment Lane. There are three existing 60" drainage culverts crossing under Garden Road at the EPB-6 Canal that are in disrepair and need to be lined.</p> <p>FY 2021 IST \$300,000</p> <p>FY 2022 IST \$700,000</p>	

SCHEDULE SUMMARY			PARTICIPATION		FUNDING	
	Original	Actual				
Drainage Repair Complete	12/1/2024	1/31/2025				
Milling and Pavement Complete	6/1/2025					
Traffic Striping Complete	8/1/2025					
Traffic Loops Complete	9/1/2025					
ADA (Curb/Cut Ramps) Complete	9/1/2025					

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.				
	A	B	C=B/A	D					
Construction	\$1,000,000	\$965,608	96.56%	\$697,534					
TOTAL	\$1,000,000	\$965,608	96.56%	\$697,534					



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Countywide Street Lighting FY21 (frmlly Military Trl (L.W. to Clint Moore))

Project Number: 1680

BCC District: CW

Delivery Method: Florida Power and Light

Category: S14-Street Lighting

Status: Construction

Designer: Florida Power & Light

Contractor: Florida Power & Light

Project Manager: May Cheng

#### SCOPE

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Jog/Okeechobee to Belvedere		
Military/Northlake to Leo Lane		
SW 18th/SR7 to Turnpike		
Lake Worth Rd/SR7 to Jog		
Lyons/Clint Moore to Broward County Lin		
Military/Okeechobee to Lake Worth Rd		
Palmetto Park/University to Military		
Military/Lake Worth to Clint Moore		

#### PARTICIPATION

##### Consultant

SBE N/A

Local N/A

WBE N/A

MBE N/A

##### Contractor


SBE N/A

Local N/A


WBE N/A

MBE N/A

#### FUNDING



Current Budget

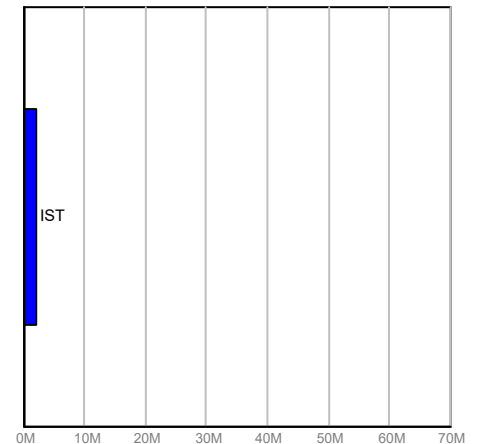

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,180,000	\$537,363	24.65%	\$238,767
<b>TOTAL</b>	<b>\$2,180,000</b>	<b>\$537,363</b>	<b>24.65%</b>	<b>\$238,767</b>

#### NOTES

There are 8 street lighting projects (road segments) funded (\$2,180,000) for conversion in FY 2021. All 8 projects have been forwarded to FPL requesting final design and installation.




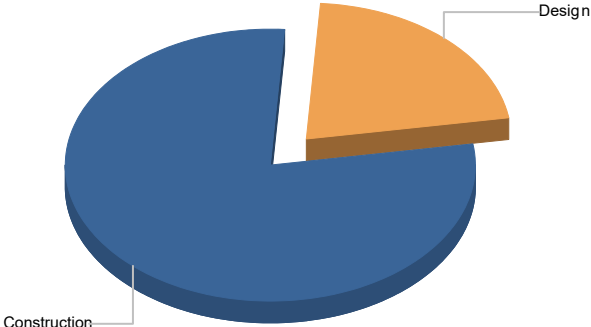
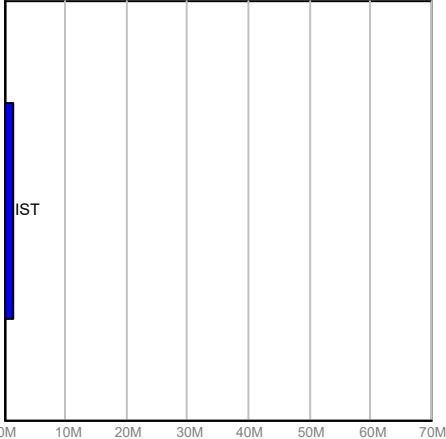
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Belvedere Rd. Canal Piping</p> <p>Project Number: 1690</p> <p>BCC District: 02</p> <p>Delivery Method: Design CCNA</p> <p>Category: B02-Belvedere Rd. Canal Piping</p> <p>Status: Design</p> <p>Designer: Keith</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Maroun Azzi</p>	<p>This project will pipe a portion of a drainage ditch that runs along Belvedere Road and Troy Boulevard - adjacent to Palm Beach International Airport. The embankment area for the ditch is small and difficult to maintain. The undermining of this area continues and compromises the integrity of the sidewalk and road. Piping of the ditch is necessary to properly protect the road and sidewalk.</p> <p>FY2022 IST \$300,000</p> <p>FY2024 IST \$1,100,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Study Complete</td><td>9/1/2023</td><td>12/1/2023</td></tr><tr><td>Design Complete</td><td>6/1/2025</td><td></td></tr><tr><td>Construction Bid Date</td><td></td><td></td></tr><tr><td>Construction Start</td><td></td><td></td></tr><tr><td>Construction Complete</td><td></td><td></td></tr></table>		Original	Actual	Study Complete	9/1/2023	12/1/2023	Design Complete	6/1/2025		Construction Bid Date			Construction Start			Construction Complete			<p><b>Consultant</b></p> <p>SBE 54%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><p>Design</p><p>Construction</p></div> <div><p>IST</p><p>Fund Source</p></div>
	Original	Actual																		
Study Complete	9/1/2023	12/1/2023																		
Design Complete	6/1/2025																			
Construction Bid Date																				
Construction Start																				
Construction Complete																				

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>Design is ongoing (65% complete). The project is funded for design (\$300k) in FY22 and for construction (\$1.1m) in FY24.</p>
	A	B	C=B/A	D	
Design	\$300,000	\$75,370	25.12%	\$69,371	
Construction	\$1,100,000	\$9,866	0.90%	\$13,366	
TOTAL	\$1,400,000	\$85,236	6.09%	\$82,737	



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Barwick Rd. over LWDD Lat. 30 Canal (934455)  
**Project Number:** 1691  
**BCC District:** 04  
**Delivery Method:** Design CCNA  
**Category:** B04-Bridge Modifications  
**Status:** Design  
**Designer:** Alan Gerwig & Associates  
**Contractor:** TBD  
**Project Manager:** Kristine Frazelle-Smith

#### SCOPE

This project will replace an existing bridge that was built over 60 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	7/1/2023	7/1/2023
Consultant Procurement Finish	12/5/2023	12/5/2023
Design Start	12/12/2023	12/12/2023
Design Complete	10/1/2025	
Permit Application	4/1/2025	
Permit Issued	11/1/2025	
Construction Start	5/14/2026	
Construction Complete	5/14/2027	

#### PARTICIPATION


##### Consultant

SBE 98%  
Local 100%  
WBE 0%  
MBE 15%

##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

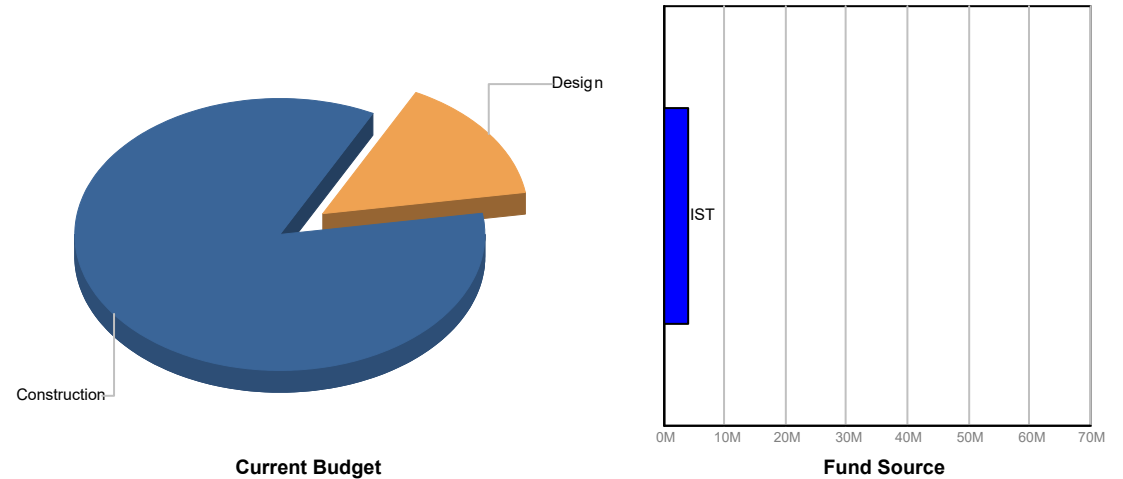

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$268,223	44.70%	\$46,438
Construction	\$3,370,000	\$37,410	1.11%	\$14,823
<b>TOTAL</b>	<b>\$3,970,000</b>	<b>\$305,633</b>	<b>7.70%</b>	<b>\$61,262</b>

#### NOTES

The project is funded for design (\$600k) in FY22 and for construction (\$3.37m) in FY26. Design is ongoing (15% complete).



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Summit Blvd. over C-51 Canal (934201)

Project Number: 1693  
BCC District: 03  
Delivery Method: Design CCNA  
Category: B08-Bridge Replacements  
Status: Design  
Designer: Consor Engineers, LLC  
Contractor: TBD  
Project Manager: Maroun Azzi

#### SCOPE

This project will replace an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection. The project will also add a left turn lane servicing the adjacent school on the NE quadrant.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	3/1/2022	3/1/2022
Consultant Procurement Finish	12/1/2022	12/1/2022
Design Start	4/1/2023	3/14/2023
Design Complete	6/1/2026	
Permit Application	1/1/2025	
Permit Issued	6/1/2026	
Construction Start	12/1/2026	
Construction Complete	1/1/2029	

#### PARTICIPATION


##### Consultant

SBE 40%  
Local 100%  
WBE 0%  
MBE 0%


##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

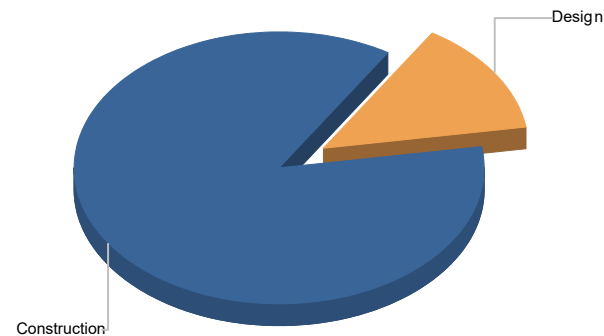

Current Budget

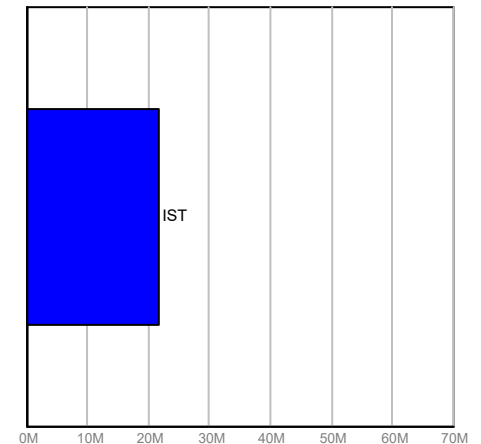

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,000,000	\$802,772	26.76%	\$621,258
Construction	\$18,863,000	\$33,126	0.18%	\$35,190
<b>TOTAL</b>	<b>\$21,863,000</b>	<b>\$835,898</b>	<b>3.82%</b>	<b>\$656,448</b>

#### NOTES

The project is funded for design (\$3m) in FY22 and for construction (\$18.863m) in FY27. Design is ongoing (25% complete).






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Seminole Colony east (Okeechobee/Military)</p> <p>Project Number: 1694</p> <p>BCC District: 07</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: Masse Consulting Services</p> <p>Contractor: TBD</p> <p>Project Manager: Carlos Bojorge</p>	<p>The project will include drainage improvements along Seminole Colony East (Spafford Avenue, Scott Avenue, Indian Road, and Gardenia Street) just north of Okeechobee Boulevard.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Design Start</td><td>4/1/2023</td><td>4/1/2023</td></tr><tr><td>Design Complete</td><td>12/1/2024</td><td></td></tr><tr><td>Construction Bid Date</td><td>3/1/2025</td><td></td></tr><tr><td>Construction Start</td><td>7/1/2025</td><td></td></tr><tr><td>Construction Complete</td><td>7/1/2026</td><td></td></tr></table>		Original	Actual	Design Start	4/1/2023	4/1/2023	Design Complete	12/1/2024		Construction Bid Date	3/1/2025		Construction Start	7/1/2025		Construction Complete	7/1/2026		<p><b>Consultant</b></p> <p>SBE 94.6%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 74.5%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><p>Current Budget</p></div> <div><p>Fund Source</p></div>
	Original	Actual																		
Design Start	4/1/2023	4/1/2023																		
Design Complete	12/1/2024																			
Construction Bid Date	3/1/2025																			
Construction Start	7/1/2025																			
Construction Complete	7/1/2026																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>Design is ongoing (50% complete). The project is funded for design (\$300k) in FY22 and for construction (\$1.2m) in FY24.</p>
	A	B	C=B/A	D	
Design	\$300,000	\$296,217	98.74%	\$239,688	
Construction	\$1,200,000	\$13,355	1.11%	\$13,355	
TOTAL	\$1,500,000	\$309,572	20.64%	\$253,042	



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Seminole Colony west  
(Okeechobee/Military)

Project Number: 1695

BCC District: 07

Delivery Method: Design CCNA

Category: D04-Drainage Improvements

Status: Design

Designer: Mock Roos

Contractor: TBD

Project Manager: Carlos Bojorge

#### SCOPE

The project will include drainage improvements along Seminole Colony West just north of Okeechobee Boulevard and east of Military Trail. The improvement anticipates piping an existing ditch from the south termini (starting around Schall Rd. and Gardenia St. - if both were extended) to the outfall into the PBCID-EPB-E 11-S Canal.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Design Start	10/1/2023	9/1/2023
Design Complete	4/1/2025	
Construction Bid Date	8/1/2025	
Construction Start	11/1/2025	
Construction Complete	12/1/2026	

#### PARTICIPATION

##### Consultant

SBE 23.2%

Local 100%

WBE 0%

MBE 0%

##### Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

#### FUNDING

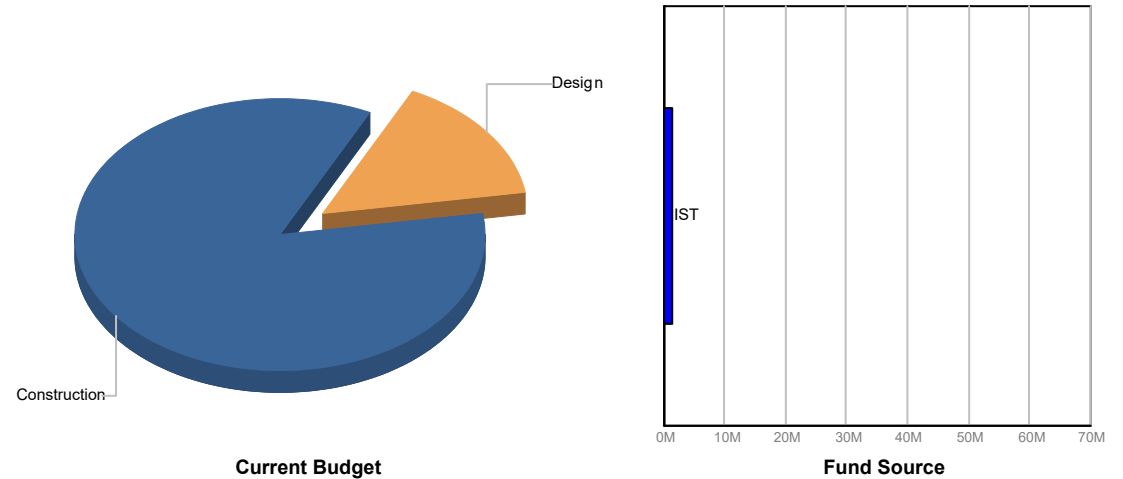

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$200,000	\$148,985	74.49%	\$119,256
Construction	\$1,100,000	\$6,993	0.64%	\$6,993
<b>TOTAL</b>	<b>\$1,300,000</b>	<b>\$155,978</b>	<b>12.00%</b>	<b>\$126,249</b>

#### NOTES

Design is ongoing (15% complete). The project is funded for design (\$200k) in FY22 and for construction (\$1.1m) in FY24.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Palmetto Park Rd. from Glades Rd. to Crawford Blvd.</p> <p>Project Number: 1697</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger Construction Industries, Inc.</p> <p>Project Manager: Thomas Coppini</p>	<p>Resurfacing 10 miles (51.8 lane miles) of Palmetto Park Road from Glades Road to Crawford Boulevard (SW 3rd Ave.)</p> <p>FY 2022 IST \$4,800,000.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>9/1/2022</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>12/1/2022</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>12/1/2022</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>3/1/2023</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	9/1/2022		ADA (Curb/Cut Ramps) Complete	12/1/2022		Traffic Striping Complete	12/1/2022		Traffic Loops Complete	3/1/2023		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	9/1/2022																
ADA (Curb/Cut Ramps) Complete	12/1/2022																
Traffic Striping Complete	12/1/2022																
Traffic Loops Complete	3/1/2023																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>All of the resurfacing work west of I-95 is complete. There is an ongoing 5 Yr. Road Program project to replace the bridge over the E-4 (El Rio) Canal (with scheduled completion date in 2024). After completion of the bridge replacement, resurfacing work will continue east of I-95 to Crawford.</p>
	A	B	C=B/A	D	
Construction	\$4,800,000	\$4,785,712	99.70%	\$4,139,239	
TOTAL	\$4,800,000	\$4,785,712	99.70%	\$4,139,239	




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lantana Road &amp; Congress Avenue</p> <p>Project Number: 1714</p> <p>BCC District: Multiple</p> <p>Delivery Method: Design CCNA</p> <p>Category: S08-Signals and Signal Systems</p> <p>Status: Design</p> <p>Designer: Propel Engineering, Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: Fattoush Jafar</p>	<p>This project will replace the existing span-wire signal system with a mast arm signal system.</p> <p>FY 2022 IST \$150,000</p> <p>FY 2023 IST \$500,000</p> <p>FY 2025 IST \$400,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Design NTP Issued</td><td>12/15/2021</td><td>12/15/2021</td></tr><tr><td>Design Complete</td><td>6/21/2025</td><td></td></tr><tr><td>Construction Start</td><td>11/1/2025</td><td></td></tr><tr><td>Construction Complete</td><td>11/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Design NTP Issued	12/15/2021	12/15/2021	Design Complete	6/21/2025		Construction Start	11/1/2025		Construction Complete	11/1/2026		<p><b>Consultant</b></p> <p>SBE 92%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><div></div><div>IST</div><div>0M10M20M30M40M50M60M70M</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Design NTP Issued	12/15/2021	12/15/2021															
Design Complete	6/21/2025																
Construction Start	11/1/2025																
Construction Complete	11/1/2026																

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,050,000	\$151,775	14.45%	\$102,071
TOTAL	\$1,050,000	\$151,775	14.45%	\$102,071

NOTES
Design is ongoing (95% complete). A Budget Transfer (BT 25-0387) was approved on 3/11/25 that increased the funding by \$400,000.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Lake Lytal Aquatic Center Replace Public Aquatic Facility

**Project Number:** 17218

**BCC District:** 03

**Delivery Method:** Construction Management at Risk

**Category:** A02-Aquatic Facility Repair and Replacement

**Status:** Design

**Designer:** Harvard Jolly, Inc.

**Contractor:** Kauffman Lynn/ Hedrick Brothers

**Project Manager:** Rich Carlton

#### SCOPE

The project entails constructing a new multi-phase Aquatic Complex mainly on undeveloped land along Kirk Rd. within Lake Lytal Park. The existing Pool Facility is to be demolished once the new aquatic center is opened to the public. The major components of the new Aquatic Complex will be a 70 Meter competition pool with dive well, a family water play area, 6-lane warm-up pool, flow riders, slides and building amenities such as restrooms, lockers, concession stand.

FY 2017 IST - \$4,000,000  
FY 2018 IST - \$2,000,000  
FY 2023 IST - \$6,152,500  
FY 2024 IST - \$18,393,368

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	4/19/2018	4/19/2018
Design Start (Master Plan)	7/10/2018	7/10/2018
Design Start (Aquatic Center)	11/20/2018	5/1/2023
Construction Start	7/1/2019	3/25/2024
Substantial Completion	7/1/2020	
Project Completion	9/1/2020	

#### PARTICIPATION

##### Consultant

SBE 30%

Local 100%

WBE N/A

MBE N/A

##### Contractor


SBE 24.66%

Local N/A


WBE N/A

MBE N/A

#### FUNDING

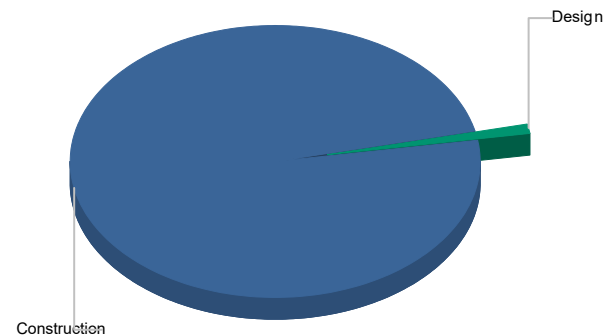

Current Budget

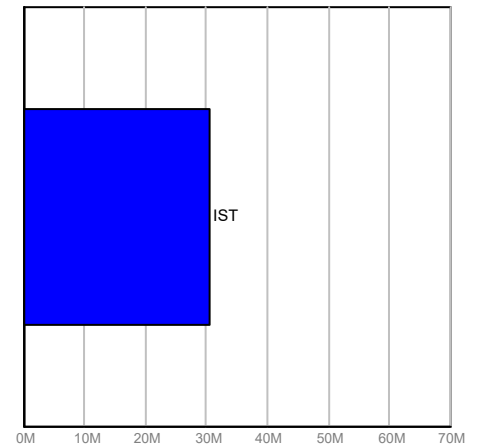

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$373,498	\$590,036	157.98%	\$254,103
Construction	\$30,199,635	\$11,661,465	38.61%	\$10,114,153
Furniture, Fixtures & Equipment	\$0	\$282	0.00%	\$282
Other	\$0	\$37,316	0.00%	\$37,316
Contingency	\$0	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$30,573,133</b>	<b>\$12,289,099</b>	<b>40.20%</b>	<b>\$10,405,853</b>

#### NOTES

Phase 1 (site preparation): construction complete. Phase 2 (site infrastructure): construction continues, including YMCA site utilities (water/sewer), with an anticipated substantial completion date of 5/31/2025, at which time a punchlist walk-through will be scheduled. Phase 3 (balance of improvements): 95% construction documents are complete; GMP being developed by the construction manager and initial draft is due to PBC on 5/7/2025; additional funding is expected to be required to fulfill the project costs through all (3) phases and development of a funding plan is in progress.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> East Ocean Ave. (C-812) over Hypoluxo Island Lagoon (934347)</p> <p>Project Number: 1728</p> <p>BCC District: 04</p> <p>Delivery Method: Design CCNA</p> <p>Category: B04-Bridge Modifications</p> <p>Status: Design</p> <p>Designer: Scalar</p> <p>Contractor: TBD</p> <p>Project Manager: Kristine Frazelle-Smith</p>	<p>This project will replace an existing bridge that was built over 35 years ago. The project will improve traffic safety (lane widths, bike lanes, sidewalks, etc.) and improve drainage and embankment/slope protection.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Project Start</td><td>9/1/2023</td><td>9/1/2023</td></tr><tr><td>Consultant Procurement Finish</td><td>1/23/2024</td><td>1/23/2024</td></tr><tr><td>Design Start</td><td>2/1/2024</td><td>2/1/2024</td></tr><tr><td>Design Complete</td><td>6/1/2026</td><td></td></tr><tr><td>Permit Application</td><td>4/1/2025</td><td></td></tr><tr><td>Permit Issued</td><td>6/1/2026</td><td></td></tr><tr><td>Construction Start</td><td>12/1/2026</td><td></td></tr><tr><td>Construction Complete</td><td>2/1/2028</td><td></td></tr></tbody></table>		Original	Actual	Project Start	9/1/2023	9/1/2023	Consultant Procurement Finish	1/23/2024	1/23/2024	Design Start	2/1/2024	2/1/2024	Design Complete	6/1/2026		Permit Application	4/1/2025		Permit Issued	6/1/2026		Construction Start	12/1/2026		Construction Complete	2/1/2028		<p><b>Consultant</b></p> <p>SBE 12.4%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><p>Design</p><p>Construction</p></div> <div><p>IST</p></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																											
Project Start	9/1/2023	9/1/2023																											
Consultant Procurement Finish	1/23/2024	1/23/2024																											
Design Start	2/1/2024	2/1/2024																											
Design Complete	6/1/2026																												
Permit Application	4/1/2025																												
Permit Issued	6/1/2026																												
Construction Start	12/1/2026																												
Construction Complete	2/1/2028																												

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>The project is funded for design (\$800k) in FY23 and for construction (\$4.582m) in FY26. Design is ongoing (5% complete).</p>
	A	B	C=B/A	D	
Design	\$800,000	\$555	0.07%	\$555	
Construction	\$4,582,000	\$478,936	10.45%	\$191,356	
TOTAL	\$5,382,000	\$479,491	8.91%	\$191,911	




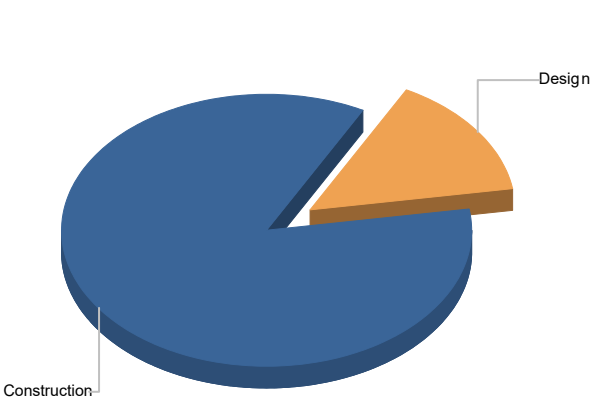
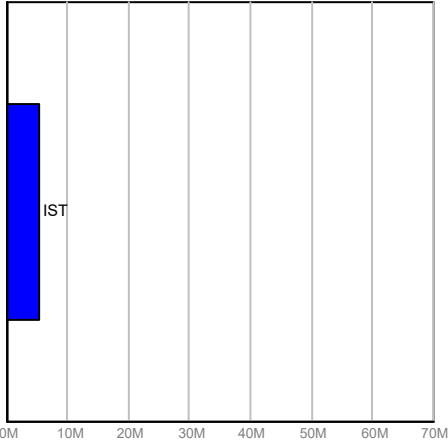
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Duda Rd. over SFWMD Lat. 14 Canal (Hillsboro Canal) (934519)</p> <p>Project Number: 1729</p> <p>BCC District: 06</p> <p>Delivery Method: Design CCNA</p> <p>Category: B08-Bridge Replacements</p> <p>Status: Design</p> <p>Designer: R.J. Behar</p> <p>Contractor: TBD</p> <p>Project Manager: Carlos Bojorge</p>	<p>This project will replace an existing bridge that was built over 70 years ago. The project will improve traffic safety (lane widths, sidewalks, etc.) and improve embankment/slope protection.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Project Start</td><td>11/1/2022</td><td>11/1/2022</td></tr><tr><td>Consultant Procurement Finish</td><td>4/1/2024</td><td>4/1/2024</td></tr><tr><td>Design Start</td><td>6/11/2024</td><td>6/11/2024</td></tr><tr><td>Design Complete</td><td>12/1/2026</td><td></td></tr><tr><td>Permit Application</td><td>12/1/2025</td><td></td></tr><tr><td>Permit Issued</td><td>12/1/2026</td><td></td></tr><tr><td>Construction Start</td><td>6/1/2027</td><td></td></tr><tr><td>Construction Complete</td><td>4/1/2029</td><td></td></tr></tbody></table>		Original	Actual	Project Start	11/1/2022	11/1/2022	Consultant Procurement Finish	4/1/2024	4/1/2024	Design Start	6/11/2024	6/11/2024	Design Complete	12/1/2026		Permit Application	12/1/2025		Permit Issued	12/1/2026		Construction Start	6/1/2027		Construction Complete	4/1/2029		<p><b>Consultant</b></p> <p>SBE 23%</p> <p>Local 100%</p> <p>WBE 23%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 
	Original	Actual																											
Project Start	11/1/2022	11/1/2022																											
Consultant Procurement Finish	4/1/2024	4/1/2024																											
Design Start	6/11/2024	6/11/2024																											
Design Complete	12/1/2026																												
Permit Application	12/1/2025																												
Permit Issued	12/1/2026																												
Construction Start	6/1/2027																												
Construction Complete	4/1/2029																												

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	The project is funded for design (\$800k) in FY23 and for construction (\$4.667m) in FY27. Design is ongoing (10% complete).				
	A	B	C=B/A	D					
Design	\$800,000	\$0	0.00%	\$0					
Construction	\$4,667,000	\$486,278	10.42%	\$67,422					
TOTAL	\$5,467,000	\$486,278	8.89%	\$67,422					






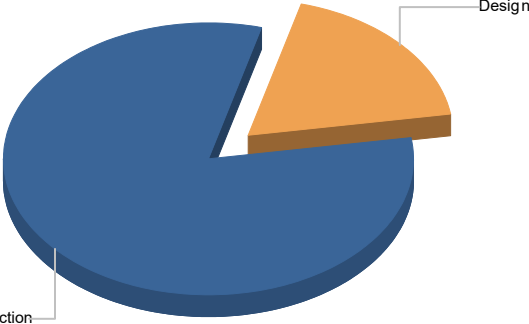
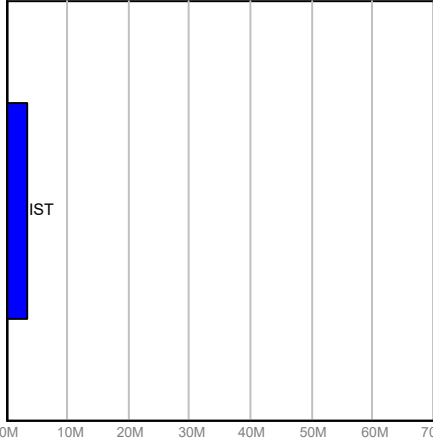
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lantana Rd. from Hagen Ranch Rd. to I-95</p> <p>Project Number: 1731</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Design</p> <p>Designer: Mock, Roos &amp; Associates</p> <p>Contractor: TBD</p> <p>Project Manager: Chase Miller</p>	<p>Resurfacing 5.5 miles (33 lane miles) of Lantana Road from Hagen Ranch Road to I-95. The road exhibits deteriorating surface conditions caused by issues with the underground closed drainage system.</p> <p>FY2022 IST \$3,280,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Drainage Repairs Complete</td><td>12/1/2025</td><td></td></tr><tr><td>Milling and Pavement Complete</td><td>6/1/2026</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>9/1/2026</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>8/1/2026</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>12/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Drainage Repairs Complete	12/1/2025		Milling and Pavement Complete	6/1/2026		ADA (Curb/Cut Ramps) Complete	9/1/2026		Traffic Striping Complete	8/1/2026		Traffic Loops Complete	12/1/2026		<p><b>Consultant</b></p> <p>SBE 0%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><p>Design</p><p>Construction</p></div> <div><p>IST</p><p>0M 10M 20M 30M 40M 50M 60M 70M</p><p>Fund Source</p></div> <p>Current Budget</p>
	Original	Actual																		
Drainage Repairs Complete	12/1/2025																			
Milling and Pavement Complete	6/1/2026																			
ADA (Curb/Cut Ramps) Complete	9/1/2026																			
Traffic Striping Complete	8/1/2026																			
Traffic Loops Complete	12/1/2026																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Design	\$600,000	\$0	0.00%	\$0	
Construction	\$2,680,000	\$6,070	0.23%	\$6,070	
TOTAL	\$3,280,000	\$6,070	0.19%	\$6,070	Drainage infrastructure study underway to determine scope of drainage repairs. Outstanding work includes drainage repairs, milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Countywide Street Lighting FY23 (frmly Lyons Rd (Lantana to Boynton Bch Blvd)

Project Number: 1760

BCC District: CW

Delivery Method: Florida Power and Light

Category: S14-Street Lighting

Status: Construction

Designer: Florida Power & Light

Contractor: Florida Power & Light

Project Manager: May Cheng

#### SCOPE

These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Gateway/Lawrence to Savannah Lakes		
Gun Club/Kirk to Congress		
Military/Camino Real to SW 18th		
Lawrence/Gateway to Boynton Beach		
Lake Worth/Wellington City Limits to SR 7		
Lawrence/Hypoluxo to Miner		
Jog/Hypoluxo to Joe de Long		
Hagen Ranch/Boynton Beach to W. Atlan		
Clint Moore/SR 7 to Turpike		
Hypoluxo/SR 7 to Hagen Ranch		
Okeechobee/SR 7 to Turpike		
Jog/Woolbright to Lake Ida		
Military/Waditika Wy to Okeechobee		

#### PARTICIPATION

##### Consultant

SBE N/A

Local N/A

WBE N/A

MBE N/A

##### Contractor


SBE N/A

Local N/A

WBE N/A

MBE N/A

#### FUNDING

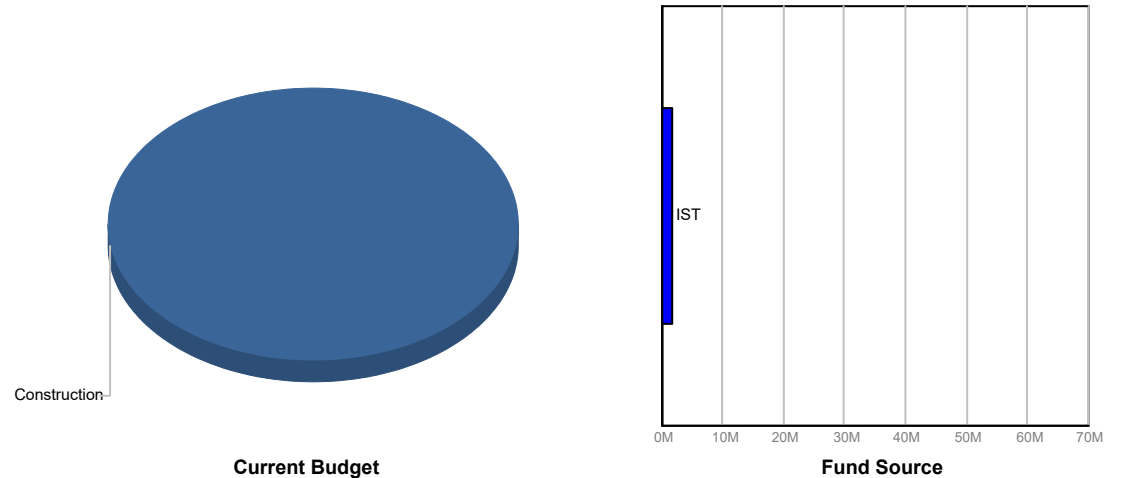

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,830,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,830,000</b>	<b>\$0</b>	<b>0.00%</b>	<b>\$0</b>

#### NOTES

There are 15 street lighting projects (road segments) funded (\$1,830,000) for conversion in FY 2023.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Congress Ave. from Clint Moore Rd. to Lake Ida Rd.</p> <p>Project Number: 1779</p> <p>BCC District: Multiple</p> <p>Delivery Method:</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Chase Miller</p>	<p>Resurfacing 4.7 miles (28.2 lane miles) of Congress Avenue from Clint Moore Road to Lake Ida Road.</p> <p>IST FY2024 \$3,300,000.00</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>12/1/2025</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>3/1/2026</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>1/1/2026</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>9/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	12/1/2025		ADA (Curb/Cut Ramps) Complete	3/1/2026		Traffic Striping Complete	1/1/2026		Traffic Loops Complete	9/1/2026		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div><div>0M10M20M30M40M50M60M70M</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	12/1/2025																
ADA (Curb/Cut Ramps) Complete	3/1/2026																
Traffic Striping Complete	1/1/2026																
Traffic Loops Complete	9/1/2026																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$3,300,000	\$11,200	0.34%	\$11,200	
TOTAL	\$3,300,000	\$11,200	0.34%	\$11,200	




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> S.W. 18th St. from Boca Rio Rd. to Military Trail</p> <p>Project Number: 1782</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Ranger</p> <p>Project Manager: Chase Miller</p>	<p>Resurfacing 2.5 miles (10.8 lane miles) of SW 18th Street from Boca Rio Road to Military Trail.</p> <p>IST FY2024 \$1,300,000.00</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>10/1/2025</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>2/1/2026</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>12/1/2025</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>4/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	10/1/2025		ADA (Curb/Cut Ramps) Complete	2/1/2026		Traffic Striping Complete	12/1/2025		Traffic Loops Complete	4/1/2026		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 15%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div><div>0M10M20M30M40M50M60M70M</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	10/1/2025																
ADA (Curb/Cut Ramps) Complete	2/1/2026																
Traffic Striping Complete	12/1/2025																
Traffic Loops Complete	4/1/2026																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$1,300,000	\$156,167	12.01%	\$53,167	
TOTAL	\$1,300,000	\$156,167	12.01%	\$53,167	




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Lake Ida Rd. from Hagen Ranch Rd. to Congress Ave.</p> <p>Project Number: 1813</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&amp;M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	Resurfacing 4.5 miles (14.4 lane miles) of Lake Ida Road from Hagan Ranch Road to Congress Avenue.	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>8/1/2025</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>10/1/2025</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>10/1/2025</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>1/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	8/1/2025		ADA (Curb/Cut Ramps) Complete	10/1/2025		Traffic Striping Complete	10/1/2025		Traffic Loops Complete	1/1/2026		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 10%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	8/1/2025																
ADA (Curb/Cut Ramps) Complete	10/1/2025																
Traffic Striping Complete	10/1/2025																
Traffic Loops Complete	1/1/2026																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$1,850,000	\$238,224	12.88%	\$238,224	
TOTAL	\$1,850,000	\$238,224	12.88%	\$238,224	





Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Old Dixie Hwy. from South County Line to Spanish River Blvd.</p> <p>Project Number: 1814</p> <p>BCC District: 04</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&amp;M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	<p>Resurfacing 4.6 miles (18.4 lane miles) of Old Dixie Hwy. from S. County line to Spanish River.</p>	

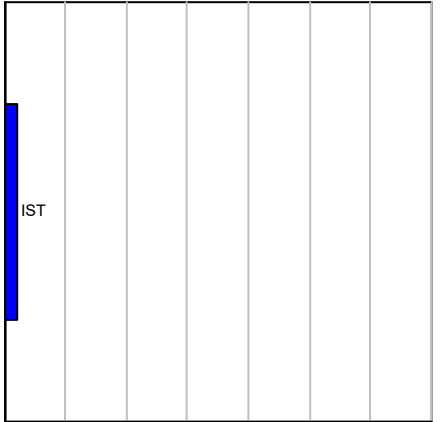SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>12/1/2025</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>10/1/2025</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>2/1/2026</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>6/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	12/1/2025		ADA (Curb/Cut Ramps) Complete	10/1/2025		Traffic Striping Complete	2/1/2026		Traffic Loops Complete	6/1/2026		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 10%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>Construction</div></div>   <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	12/1/2025																
ADA (Curb/Cut Ramps) Complete	10/1/2025																
Traffic Striping Complete	2/1/2026																
Traffic Loops Complete	6/1/2026																

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.				
	A	B	C=B/A	D					
Construction	\$2,170,000	\$50,510	2.33%	\$2,910					
TOTAL	\$2,170,000	\$50,510	2.33%	\$2,910					




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> El Clair Ranch Rd. from Atlantic Ave. to Boynton Beach Blvd.</p> <p>Project Number: 1816</p> <p>BCC District: 05</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&amp;M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	Resurfacing 5.2 miles (10.4 lane miles) of El Clair Ranch Road from Atlantic Avenue to Boynton Beach Boulevard.	

SCHEDULE SUMMARY			PARTICIPATION		FUNDING	
	Original	Actual				
Milling and Pavement Complete	12/1/2025					
ADA (Curb/Cut Ramps) Complete	10/1/2025					
Traffic Striping Complete	2/1/2026					
Traffic Loops Complete	5/1/2026					
			<b>Consultant</b>			
			SBE	N/A		
			Local	N/A		
			WBE	N/A		
			MBE	N/A		
			<b>Contractor</b>			
			SBE	10%		
			Local	100%		
			WBE	0%		
			MBE	0%		

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$1,360,000	\$85,071	6.26%	\$1,824	
TOTAL	\$1,360,000	\$85,071	6.26%	\$1,824	







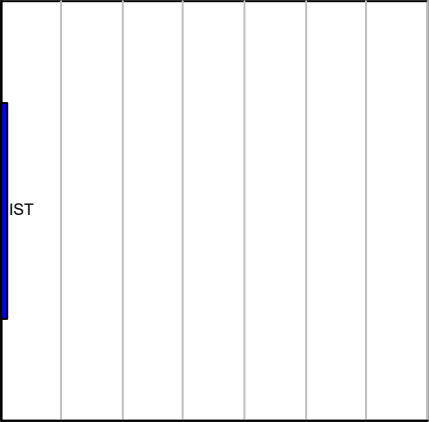
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Judge Winnikoff Rd. from State Rd. 7 to Glades Rd.</p> <p>Project Number: 1820</p> <p>BCC District: 05</p> <p>Delivery Method: Annual Construction Contract</p> <p>Category: R04-Resurfacing</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: M&amp;M Asphalt Maintenance</p> <p>Project Manager: Chase Miller</p>	Resurfacing 3.9 miles (10.0 lane miles) of Judge Winnikoff Road from Glades Road to SR 7.	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Milling and Pavement Complete</td><td>9/1/2025</td><td></td></tr><tr><td>ADA (Curb/Cut Ramps) Complete</td><td>12/1/2025</td><td></td></tr><tr><td>Traffic Striping Complete</td><td>11/1/2025</td><td></td></tr><tr><td>Traffic Loops Complete</td><td>2/1/2026</td><td></td></tr></tbody></table>		Original	Actual	Milling and Pavement Complete	9/1/2025		ADA (Curb/Cut Ramps) Complete	12/1/2025		Traffic Striping Complete	11/1/2025		Traffic Loops Complete	2/1/2026		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 10%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>Construction</div></div>  <div>IST</div>  <p>0M 10M 20M 30M 40M 50M 60M 70M</p> <p>Current Budget Fund Source</p>
	Original	Actual															
Milling and Pavement Complete	9/1/2025																
ADA (Curb/Cut Ramps) Complete	12/1/2025																
Traffic Striping Complete	11/1/2025																
Traffic Loops Complete	2/1/2026																

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Outstanding work includes milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.
	A	B	C=B/A	D	
Construction	\$1,030,000	\$60,892	5.91%	\$60,892	
TOTAL	\$1,030,000	\$60,892	5.91%	\$60,892	



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Courthouse Buildout and Renovations

Project Number: B592  
BCC District: CW  
Delivery Method: CMAR  
Category: J02-Judicial  
Status: Design  
Designer: Leo A. Daly  
Contractor: The Weitz Company LLC  
Project Manager: Rich Avery

#### SCOPE

Improvement of approximately 100,000 square feet of unfinished interior space upon floors one, seven and eight of the Judge Daniel T.K. Hurley Courthouse in downtown West Palm Beach, as well as other incidental interior improvements. All improvements will implement the Palm Beach County Judicial Facilities Master Plan Update.

IST funding consists of:  
\$8,000,000 in FY 2022,  
\$24,500,000 in FY 2023  
\$35,136,943 in FY 2024,  
\$3,000,000 Impact Fees  
Total of \$70,636,943.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Design Contract Issued	6/7/2022	6/7/2022
Design Commencement	6/17/2022	6/17/2022
Design Completion 1st, 7th, & 8th floors	5/18/2023	

#### PARTICIPATION



##### Consultant

SBE 25%  
Local 100%  
WBE 100%  
MBE 100%

##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

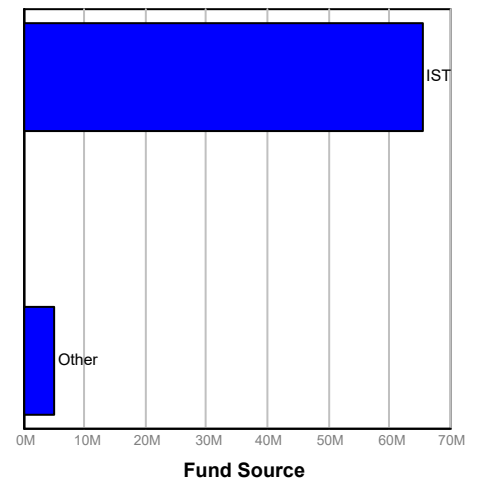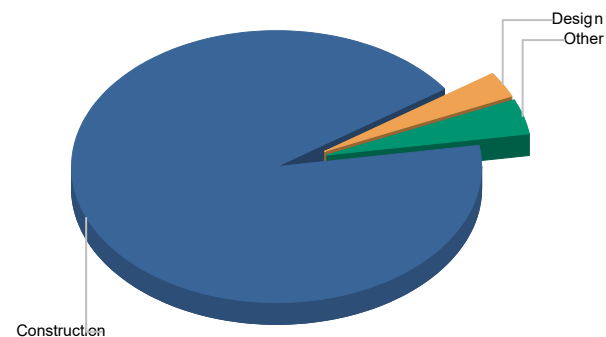

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,026,992	\$2,088,213	103.02%	\$426,598
Construction	\$65,519,822	\$2,998,310	4.58%	\$2,162,142
Other	\$3,000,000	\$143,484	4.78%	\$12,773
<b>TOTAL</b>	<b>\$70,546,814</b>	<b>\$5,230,007</b>	<b>7.41%</b>	<b>\$2,601,513</b>

#### NOTES

OAC meetings are scheduled for every two weeks and are ongoing. Design work is continuing for the first floor and the Schematic Design submission is forthcoming. The intent is to ultimately catch the 1st floor design up with the 7th and 8th floors design, which are at 100% Design Development. The CM is working on finalizing the 100% DD construction cost estimate, schedule and phases of work for review with the county.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Lake Worth West Substation

Project Number: B607  
BCC District: Multiple  
Delivery Method: Construction Manager at Risk  
Category: S06-Sheriff - FDO  
Status: Construction  
Designer: Ohlson Lavoie Collaborative  
Contractor: D Stephenson  
Project Manager: Sunil Jagoo

#### SCOPE

Provide dedicated office(s) within the HRC2 building (project-19220) for PBSO field personnel's use. Additional interior improvements include a multipurpose room for PBSO training purposes and HRC/community programming, as well as restrooms, circulation area, and other incidental improvements.

FY 2019 IST \$1,213,460

#### PHOTO



#### SCHEDULE SUMMARY

Original

Actual

Please Refer to Central County Resource

#### PARTICIPATION

##### Consultant

SBE TBD

Local TBD

WBE TBD

MBE TBD

##### Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

#### FUNDING

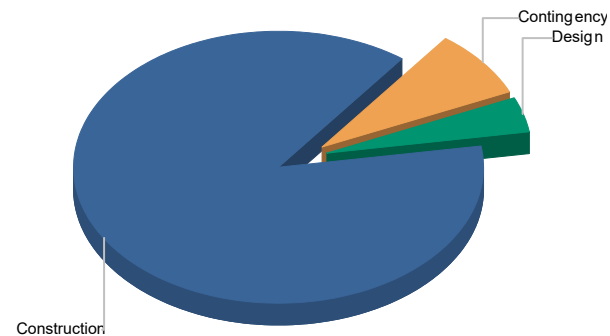

Current Budget

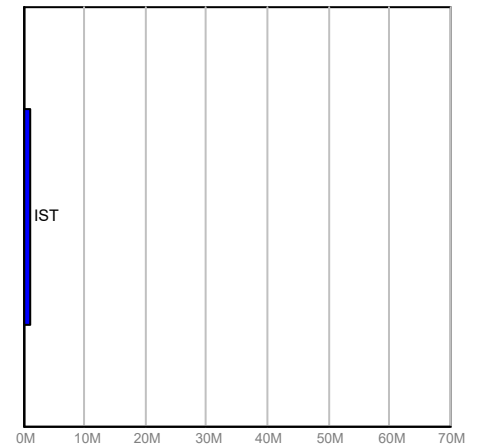

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$2,227	4.45%	\$2,227
Construction	\$1,063,460	\$1,085,373	102.06%	\$1,085,374
Contingency	\$100,000	\$0	0.00%	\$0
<b>TOTAL</b>	<b>\$1,213,460</b>	<b>\$1,087,601</b>	<b>89.63%</b>	<b>\$1,087,601</b>

#### NOTES

Please refer to the Central County Resource Center report for current status and material project updates.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** PBSO District 1 Substation and Marine Unit  
**Project Number:** B665  
**BCC District:** 02  
**Delivery Method:** CMAR  
**Category:** S06-Sheriff - FDO  
**Status:** Construction  
**Designer:** Song & Associates  
**Contractor:** Kaufman Lynn  
**Project Manager:** Henry Madriz

#### SCOPE

Construction of an approximately 28,000 square foot facility and site improvements to accommodate the relocation of PBSO District 1 from PBSO Headquarters as well as the relocation of the PBSO Marine Unit from the County's Cherry Road Complex property. The subject site is approximately 5.75 acres and located on the west side of Jog Road approximately 1,000 feet south of Belvedere Road.  
Funding Sources: IST\$1,000,000,Ad-valorem \$2,076,000, and Impact Fees \$ 22,516,895

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Submit DRO Application	8/3/2020	8/3/2020
Submit for Permits	3/18/2022	5/6/2022
Construction Complete	10/31/2023	6/16/2025
PBSO Turn Over	3/21/2025	

#### PARTICIPATION


##### Consultant

SBE 77.4%  
Local 100%  
WBE 77.4%  
MBE 77.4%

##### Contractor

SBE 27.06%  
Local 100%  
WBE 0%  
MBE 6.40%

#### FUNDING

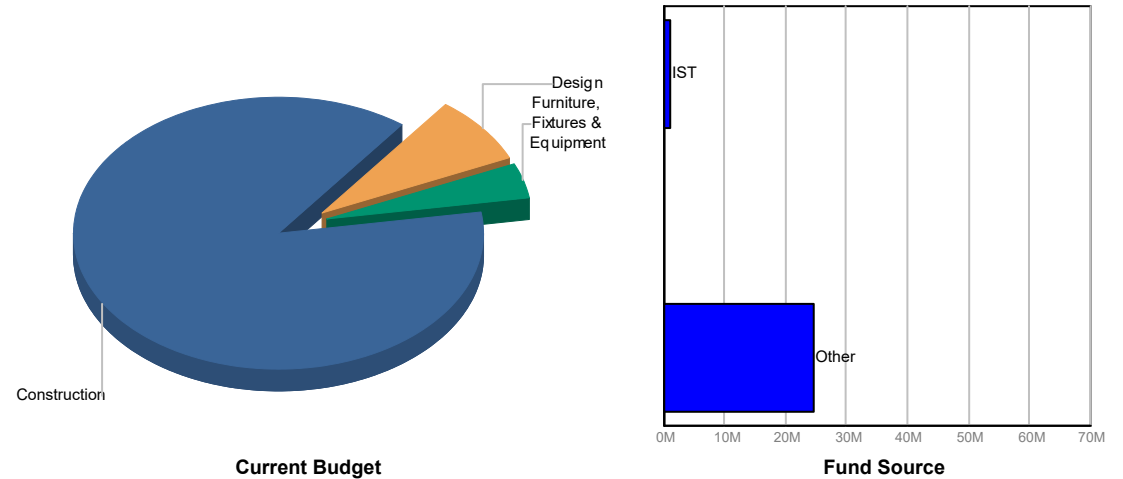

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,076,000	\$840,021	40.46%	\$840,021
Construction	\$22,440,895	\$21,894,799	97.57%	\$17,015,700
Furniture, Fixtures & Equipment	\$1,076,000	\$854,251	79.39%	\$854,251
<b>TOTAL</b>	<b>\$25,592,895</b>	<b>\$23,589,071</b>	<b>92.17%</b>	<b>\$18,709,971</b>

#### NOTES

Final Inspections for TCO are in progress. Furnishings are being installed. A ribbon cutting date is being established. Punchlist and user requested modifications are forthcoming.





Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Gramercy Park Expansion (aka Mack Bernard Park)</p> <p>Project Number: P945</p> <p>BCC District: 07</p> <p>Delivery Method: Annual Contract</p> <p>Category: E02-Existing Park Redevelopment or Expansion</p> <p>Status: Construction</p> <p>Designer: Colome' &amp; Associates, Inc.</p> <p>Contractor: Hatcher Construction &amp; Development</p> <p>Project Manager: David Polson</p>	<p>Gramercy: Construction of a +/- 11,000 sq. ft. neighborhood center and passive park for underserved Countywide Community Revitalization Team (CCRT) areas.</p> <p>FY 2024 IST: \$4,000,000</p> <p>Other funding is captured in another report, T004.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Construction NTP Issued</td><td>1/30/2024</td><td>1/30/2024</td></tr><tr><td>Construction Commencement</td><td>2/5/2024</td><td>2/5/2024</td></tr><tr><td>Permits Issued</td><td>1/24/2024</td><td>1/24/2024</td></tr><tr><td>Ground Breaking Ceremony</td><td>3/14/2024</td><td>3/14/2024</td></tr><tr><td>Project Completion</td><td>3/3/2025</td><td></td></tr></tbody></table>		Original	Actual	Construction NTP Issued	1/30/2024	1/30/2024	Construction Commencement	2/5/2024	2/5/2024	Permits Issued	1/24/2024	1/24/2024	Ground Breaking Ceremony	3/14/2024	3/14/2024	Project Completion	3/3/2025		<p><b>Consultant</b></p> <p>SBE 88.63%</p> <p>Local 100%</p> <p>WBE 6.27%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<div><div></div><div>IST</div><div>Other</div></div>  <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																		
Construction NTP Issued	1/30/2024	1/30/2024																		
Construction Commencement	2/5/2024	2/5/2024																		
Permits Issued	1/24/2024	1/24/2024																		
Ground Breaking Ceremony	3/14/2024	3/14/2024																		
Project Completion	3/3/2025																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>OAC meetings being held 1st &amp; 3rd Thursdays of each month. Anticipated substantial complete date is 5/23/2025. Application of wood trim at porch column is ongoing, placement of floor tile in restrooms complete, installation of quarry tile is ongoing in the kitchen, interior painting has started, ceiling grid installation is ongoing, light fixture installation is ongoing, planting of palm and oak trees is ongoing in the pigtail area and fire extinguisher cabinets have been installed.</p>
	A	B	C=B/A	D	
Design	\$0	\$0	0.00%	\$0	
Construction	\$4,026,663	\$2,824,521	70.15%	\$1,281,811	
<b>TOTAL</b>	<b>\$4,026,663</b>	<b>\$2,824,521</b>	<b>70.15%</b>	<b>\$1,281,811</b>	





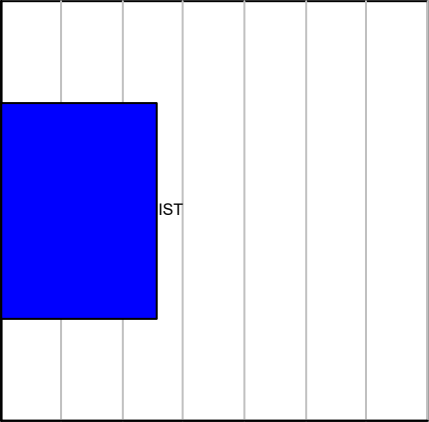
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Housing Units for Homeless, Extremely Low Income, &amp; Low Income</p> <p>Project Number: Q001</p> <p>BCC District: CW</p> <p>Delivery Method: TBD</p> <p>Category: H02-Housing</p> <p>Status: Varies</p> <p>Designer: Varies</p> <p>Contractor: Varies</p> <p>Project Manager: Varies</p>	<p>This project involves the delivery of housing units for use as temporary or longer term affordable housing for homeless and special populations.</p> <p>This Project is funded in: FY 2017 - FY 2026 for \$2,550,000 each year for a total of \$25,500,000.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Project Start</td><td>9/1/2017</td><td>9/1/2017</td></tr><tr><td> </td><td> </td><td> </td></tr><tr><td> </td><td> </td><td> </td></tr><tr><td> </td><td> </td><td> </td></tr><tr><td>Project Completion</td><td> </td><td> </td></tr><tr><td> </td><td> </td><td> </td></tr><tr><td> </td><td> </td><td> </td></tr></tbody></table>		Original	Actual	Project Start	9/1/2017	9/1/2017										Project Completion									<p><b>Consultant</b></p> <p>SBE VARIES</p> <p>Local VARIES</p> <p>WBE VARIES</p> <p>MBE VARIES</p> <p><b>Contractor</b></p> <p>SBE VARIES</p> <p>Local VARIES</p> <p>WBE VARIES</p> <p>MBE VARIES</p>	<div><div></div><div>Construction</div></div>  
	Original	Actual																								
Project Start	9/1/2017	9/1/2017																								
Project Completion																										

FINANCIAL SUMMARY					NOTES	
	Project Budget	Committed	% Committed	Paid To Date	<p>This project supports multiple initiatives over a 10-year period, focusing on housing and shelter improvements. The Cottage Homes pilot project by the WPB Housing Authority received \$6.07 million, with its ribbon-cutting held on October 30, 2024, and reconciliation underway. The BCC allocated \$1 million for a non-congregate shelter in Pahokee, with \$621,000 expended since September 15, 2020. A \$2.5 million investment was approved on November 1, 2022, to enhance 534 Belle Glade housing units, with ongoing work. Additionally, \$13 million was committed on March 18, 2025, for acquiring a 114-room senior housing hotel, currently progressing toward operational launch.</p>	
	A	B	C=B/A	D		
Design	\$0	\$15,459	0.00%	\$15,459		
Construction	\$25,500,000	\$9,215,222	36.14%	\$6,429,916		
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0		
Other	\$0	\$51,039	0.00%	\$50,674		
Contingency	\$0	\$0	0.00%	\$0		
<b>TOTAL</b>	<b>\$25,500,000</b>	<b>\$9,281,720</b>	<b>36.40%</b>	<b>\$6,496,049</b>		




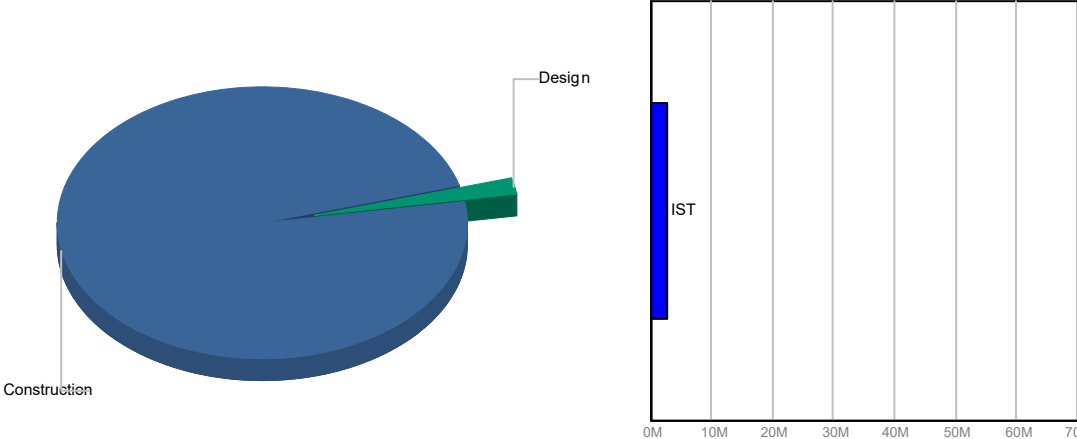
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Countywide ADA Renovations</p> <p>Project Number: Q002</p> <p>BCC District: CW</p> <p>Delivery Method: Annual Contract</p> <p>Category: G02-General Government Facilities</p> <p>Status: Varies</p> <p>Designer: Varies</p> <p>Contractor: Varies</p> <p>Project Manager: Varies</p>	<p>Renovate multiple public facility restrooms to meet ADA requirements. The following locations are planned for renovation:</p> <p>Delray Health Clinic ADA Restrooms @ \$250K FY2017</p> <p>Lantana Health Clinic ADA Restrooms @ \$275K FY2022</p> <p>Lantana Health Clinic ADA Service Counter @ \$16K FY2022</p> <p>Jupiter Health Clinic ADA Restrooms @ \$64K FY2022</p> <p>West County Administration Building (aka Glades Office Building) ADA Improvements @ \$245K FY2022 and \$450K FY2023</p> <p>This Project is funded in:</p> <p>FY 2017 \$250,000    FY 2024 \$1,009,758</p> <p>FY 2022 \$600,000    FY 2025 \$539,000</p> <p>FY 2023 \$450,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Delray Health Start</td><td>7/27/2017</td><td>7/27/2017</td></tr><tr><td>Delray Health Finish</td><td>12/21/2018</td><td>10/24/2022</td></tr><tr><td>Lantana Health Start</td><td>7/7/2017</td><td>7/7/2017</td></tr><tr><td>Lantana Health Finish</td><td>4/8/2018</td><td></td></tr><tr><td>Lantana Health (Counters) Start</td><td>11/24/2020</td><td>11/24/2020</td></tr><tr><td>Lantana Health (Counters) Finish</td><td>10/1/2024</td><td>10/1/2024</td></tr><tr><td>Jupiter Health Start</td><td>12/22/2020</td><td>12/22/2020</td></tr><tr><td>Jupiter Health Finish</td><td>11/1/2024</td><td>11/1/2024</td></tr><tr><td>West County Admin Start</td><td>6/22/2022</td><td>6/1/2023</td></tr><tr><td>West County Admin Finish</td><td></td><td></td></tr></tbody></table>		Original	Actual	Delray Health Start	7/27/2017	7/27/2017	Delray Health Finish	12/21/2018	10/24/2022	Lantana Health Start	7/7/2017	7/7/2017	Lantana Health Finish	4/8/2018		Lantana Health (Counters) Start	11/24/2020	11/24/2020	Lantana Health (Counters) Finish	10/1/2024	10/1/2024	Jupiter Health Start	12/22/2020	12/22/2020	Jupiter Health Finish	11/1/2024	11/1/2024	West County Admin Start	6/22/2022	6/1/2023	West County Admin Finish			<p><b>Consultant</b></p> <p>SBE Varies</p> <p>Local Varies</p> <p>WBE Varies</p> <p>MBE Varies</p> <p><b>Contractor</b></p> <p>SBE Varies</p> <p>Local Varies</p> <p>WBE Varies</p> <p>MBE Varies</p>	 <p>Design</p> <p>Construction</p> <p>IST</p> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																																	
Delray Health Start	7/27/2017	7/27/2017																																	
Delray Health Finish	12/21/2018	10/24/2022																																	
Lantana Health Start	7/7/2017	7/7/2017																																	
Lantana Health Finish	4/8/2018																																		
Lantana Health (Counters) Start	11/24/2020	11/24/2020																																	
Lantana Health (Counters) Finish	10/1/2024	10/1/2024																																	
Jupiter Health Start	12/22/2020	12/22/2020																																	
Jupiter Health Finish	11/1/2024	11/1/2024																																	
West County Admin Start	6/22/2022	6/1/2023																																	
West County Admin Finish																																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Design	\$52,353	\$285,482	545.30%	\$265,174	
Construction	\$2,796,405	\$826,553	29.56%	\$731,962	
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0	
Other	\$0	\$1,339	0.00%	\$1,339	
Contingency	\$0	\$0	0.00%	\$0	
<b>TOTAL</b>	<b>\$2,848,758</b>	<b>\$1,113,373</b>	<b>39.08%</b>	<b>\$998,475</b>	<p>Delray Health: Closed. Lantana Health: Project completed. Final reconciliation change order underway.</p> <p>Jupiter Health: Facility in use by Health Department. Project in closeout. West County Administration Building: Design Development drawings received and are currently under review.</p>





# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

**Project Title:** Animal Care & Control

Project Number: Q008  
 BCC District: 02  
 Delivery Method: Construction Manager at Risk  
 Category: G02-General Government Facilities  
 Status: Design  
 Designer: PGAL  
 Contractor: Wharton-Smith  
 Project Manager: Rich Avery

### SCOPE

The Animal Care & Control Renovation & Expansion project for the Belvedere Rd. campus includes: renovations to existing buildings for improved functionality; possible replacement of non-air conditioned kennel buildings with air-conditioned kennel buildings pending evaluation, pricing and approval; and the creation of new spaces necessary to facilitate current and future projected operational needs. The cost of the project includes cost-estimating services necessary in order to validate the project scope, which was derived jointly by FDO & the ACC Division via a needs assessment and programming document, as well as interim arrangements to sustain continuous operations during construction. Funding: FY 2019 IST now only \$6,000,000 and FY 2020 IST \$7,000,000. The balance will be bond (+/- \$60M).

### PHOTO



### SCHEDULE SUMMARY

	Original	Actual
PROGRAMMING	10/1/2018	10/1/2018
Commence Design Comparative Study	7/24/2019	7/24/2019
Design Start	2/3/2020	12/2/2020
Construction Start	12/1/2020	
Substantial Completion	7/3/2023	

### PARTICIPATION


#### Consultant

SBE 20%  
 Local 100%  
 WBE N/A  
 MBE N/A


#### Contractor

SBE 13.04%  
 Local 13.04%  
 WBE 13.04%  
 MBE 13.04%

### FUNDING

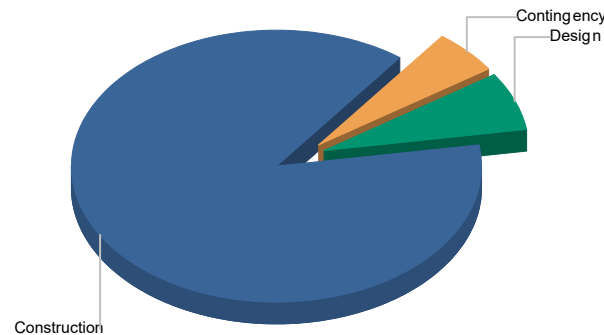

Current Budget

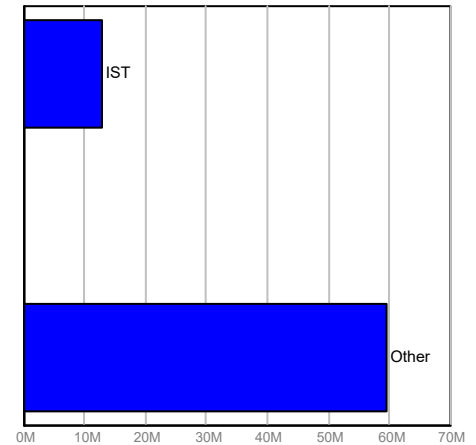

Fund Source

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$5,059,495	\$3,842,208	75.94%	\$1,190,779
Construction	\$63,820,000	\$957,722	1.50%	\$752,379
Contingency	\$3,780,000	\$119,779	3.17%	\$99,639
<b>TOTAL</b>	<b>\$72,659,495</b>	<b>\$4,919,709</b>	<b>6.77%</b>	<b>\$2,042,797</b>

### NOTES

The CID PM met with the consultant to review the plan review comments, as previously indicated. The consultant is making the necessary adjustments. The 50% Construction Documents construction cost estimate has been received from the CM and is currently under review. Both the CM and the consultant are preparing for a presentation meeting with FDO Administration to discuss the plan estimate and construction phasing per the county's request. The meeting is expected to be scheduled within the next two weeks.



# Monthly Infrastructure Sales Tax Project Report

## Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

### DESCRIPTION/TEAM

### SCOPE

### PHOTO

**Project Title:** Central County Housing Resource Center

**Project Number:** Q009

**BCC District:** 03

**Delivery Method:** Construction Manager at Risk

**Category:** H02-Housing

**Status:** Close Out

**Designer:** Ohlson Lavoie Collaborative

**Contractor:** D Stephenson

**Project Manager:** Sunil Jagoo

The Homeless Resource Center 2 (HRC 2) is to provide an effective Crisis Response System that provides immediate and easy access to safe and decent temporary shelter to County residents that need it and aims to re-house people as quickly as possible while receiving wrap-around social services. The facility will compliment the County's existing Senator Philip D. Lewis Center in West Palm Beach and will consist of approximately 19,000 square feet to support 74 client beds, dining and service delivery/office areas, restrooms, laundry facilities, an intake lobby, and other incidental interior and exterior improvements. Co-located within the facility will be the improvements identified in the IST Project Plan titled PBSO Lake Worth West Substation. FY 2019 IST \$5,700,000 FY 2022 IST \$9,243,697



### SCHEDULE SUMMARY

	Original	Actual
Program Development	11/1/2017	11/1/2017
Public Outreach	2/1/2019	2/1/2019
Design Team Solicitation	5/1/2019	9/30/2020
CM Solicitation	9/1/2019	11/26/2019
Schematic Design	11/11/2019	1/31/2020
Design Development	5/1/2020	9/28/2020
Construction Documents	10/1/2020	2/23/2021
Permitting	1/1/2021	11/1/2021
Construction Commencement	6/1/2021	5/10/2022
CO/Substantial Completion	9/1/2022	5/17/2023
Occupancy	10/3/2022	1/30/2024

### PARTICIPATION

#### Consultant

SBE 0%

Local 25%

WBE 0%

MBE 0%

#### Contractor


SBE N/A

Local 100%

WBE 6.9%

MBE 22.4%

### FUNDING

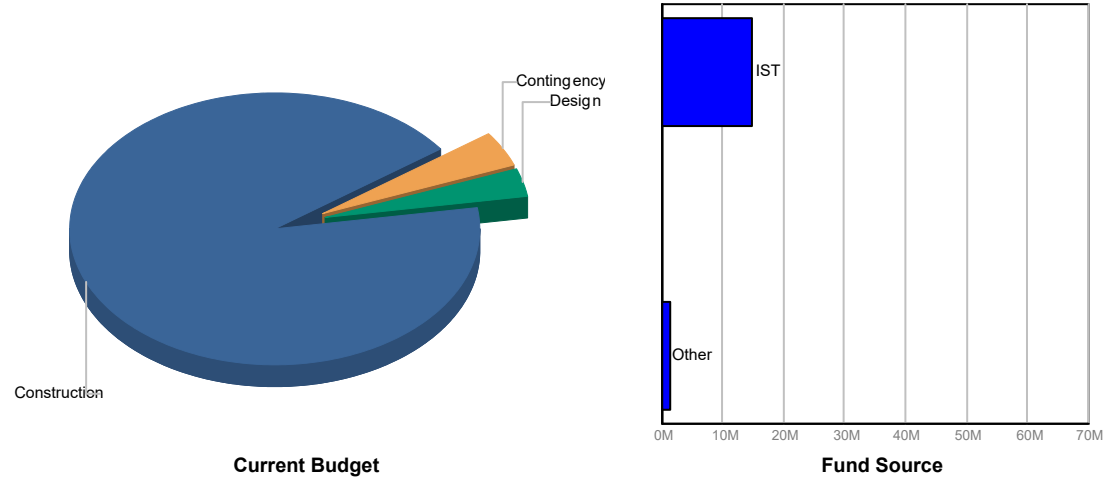

### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$547,999	\$157,227	28.69%	\$157,227
Construction	\$15,117,852	\$14,910,311	98.63%	\$14,170,104
Contingency	\$700,000	\$5,300	0.76%	\$5,300
<b>TOTAL</b>	<b>\$16,365,851</b>	<b>\$15,072,838</b>	<b>92.10%</b>	<b>\$14,332,631</b>

### NOTES

CID PM is currently working with the contractor on the change order and close out packages.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** South County Administrative Complex

Project Number: Q010  
BCC District: 07  
Delivery Method: Varies  
Category: G02-General Government Facilities  
Status: Design  
Designer: Zyscovich, LLC  
Contractor: TBD  
Project Manager: Michael Jenner

#### SCOPE

This project funds essential Renewal and Replacement (R&R) needs to sustain the continuous operation of this 40+ year old complex prior to its future redevelopment. As such there is no defined scope of work. Any funds remaining at such time that redevelopment is funded would be utilized toward professional design services for the redevelopment. Funding includes \$3M each in FY 2020 and FY 2021, for a total of \$6M.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Redevelopment Planning	10/29/2019	10/29/2019
Programming	12/6/2022	12/6/2022
Master Plan	8/29/2023	8/29/2023
Design Commencement	12/3/2024	

#### PARTICIPATION


##### Consultant

SBE Varies  
Local Varies  
WBE Varies  
MBE Varies

##### Contractor

SBE Varies  
Local Varies  
WBE Varies  
MBE Varies

#### FUNDING

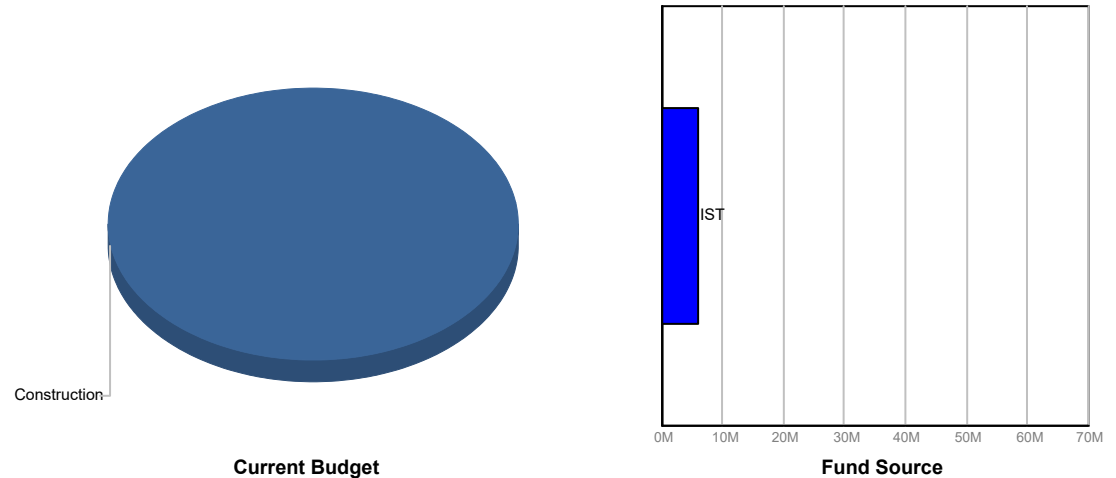

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$1,360,162	22.67%	\$1,260,530
Other	\$0	\$27,977	0.00%	\$22,503
<b>TOTAL</b>	<b>\$6,000,000</b>	<b>\$1,388,139</b>	<b>23.14%</b>	<b>\$1,283,034</b>

#### NOTES

R&R work is occurring on an as needed basis to sustain operations. Proposal for Phase 2 Design services negotiated and agreed upon for the Amount of \$11,489,524.64. There is currently \$4,500,000.00 of IST funding for this project and the remaining balance will be provided in the form of a bond issuance and/or other allocations. The design services proposal is expected to be presented at the BCC meeting on 5/20/25. Procurement of a Construction Manager at Risk(CMAR) is in progress.






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Government Center Renewal/Replacement</p> <p>Project Number: Q011</p> <p>BCC District: 02</p> <p>Delivery Method: Construction Manager at Risk</p> <p>Category: G02-General Government Facilities</p> <p>Status: Design</p> <p>Designer: Netta Architects</p> <p>Contractor: The Weitz Company LLC</p> <p>Project Manager: Jeffrey Halverson</p>	<p>This project includes but is not limited to upgrades and replacement of select building finishes and systems including security, HVAC, plumbing, fire alarm, fire sprinkler, electrical, low voltage, lighting, flooring and paint. The scope of the project will additionally include a building conditions assessment, program evaluation study, interior space planning and layout improvements. The proposed renovations to the Robert Weisman Governmental Center are designed to increase the functionality of key areas within the facility and bring the building up to current County standards.</p> <p>FY2022 IST \$8,000,000 FY2023 IST \$14,000,000 FY2024 IST \$43,740,800 FY2025 \$11,000,000</p> <p>FY2026 IST \$15,000,000 FY2027 IST \$11,500,000</p>	 <p>PBC Governmental Center</p>

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>CM RFP Proposals Due</td><td>12/2/2021</td><td>12/2/2021</td></tr><tr><td>CM Shortlist Meeting</td><td>1/19/2022</td><td>3/15/2022</td></tr><tr><td>Design RFP Final Selection</td><td>11/8/2021</td><td>9/30/2021</td></tr><tr><td>Structural Assessment</td><td>1/31/2023</td><td>3/17/2023</td></tr><tr><td>Building Construction Assessment</td><td>6/1/2023</td><td>12/20/2024</td></tr><tr><td>Life Cycle Analysis</td><td>11/1/2023</td><td>1/20/2024</td></tr><tr><td>Programming</td><td>9/9/2024</td><td>9/9/2024</td></tr></tbody></table>		Original	Actual	CM RFP Proposals Due	12/2/2021	12/2/2021	CM Shortlist Meeting	1/19/2022	3/15/2022	Design RFP Final Selection	11/8/2021	9/30/2021	Structural Assessment	1/31/2023	3/17/2023	Building Construction Assessment	6/1/2023	12/20/2024	Life Cycle Analysis	11/1/2023	1/20/2024	Programming	9/9/2024	9/9/2024	<p><b>Consultant</b></p> <p>SBE 33%</p> <p>Local 100%</p> <p>WBE 100%</p> <p>MBE 100%</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p>Construction</p>  <p>IST</p> <p>0M 10M 20M 30M 40M 50M 60M 70M</p> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																								
CM RFP Proposals Due	12/2/2021	12/2/2021																								
CM Shortlist Meeting	1/19/2022	3/15/2022																								
Design RFP Final Selection	11/8/2021	9/30/2021																								
Structural Assessment	1/31/2023	3/17/2023																								
Building Construction Assessment	6/1/2023	12/20/2024																								
Life Cycle Analysis	11/1/2023	1/20/2024																								
Programming	9/9/2024	9/9/2024																								

FINANCIAL SUMMARY					NOTES	
	Project Budget	Committed	% Committed	Paid To Date	<p>The Phase 1 design proposal (CSA #4) is being scheduled for BCC consideration. Phase I calls for the interior design of floors 10, 11 and 12 along with supporting infrastructure (electrical, HVAC, data and plumbing), elevator upgrades, and the exterior items such as impact glazing, up-lighting, façade improvements and reroofing the seven roofs of the facility. The design work is anticipated to take a year. We are initiating a CSA #5 to address space modifications under the Parking Garage to provide transitional space for a smaller department within the Phase I work. This work may require updating the Heat Pump HVAC and Cooling Tower.</p>	
	A	B	C=B/A	D		
Construction	\$103,240,800	\$800,484	0.78%	\$647,481		
<b>TOTAL</b>	<b>\$103,240,800</b>	<b>\$800,484</b>	<b>0.78%</b>	<b>\$647,481</b>		





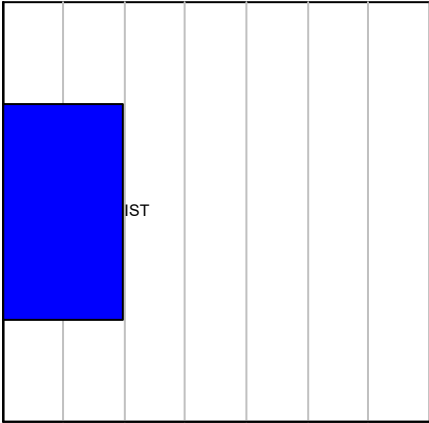
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Countywide Buildings Renewal/Replacement</p> <p>Project Number: Q014</p> <p>BCC District: CW</p> <p>Delivery Method: Varies</p> <p>Category: G02-General Government Facilities</p> <p>Status: Varies</p> <p>Designer: Varies</p> <p>Contractor: Varies</p> <p>Project Manager: Varies</p>	<p>This project addresses backlogged building system renewal and replacement, ranging from envelope components (roofs, walls, structural elements, window and weatherproofing), HVAC, plumbing, electrical, ceiling and lighting, back-up power, flooring and painting.</p> <p>FY23 IST \$4,015,800, FY24 IST \$6,154,093, FY25 IST \$4,015,800, FY26 IST \$4,015,800, and FY27 IST \$1,463,792.</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Projects Commencement</td><td>1/2/2023</td><td>5/17/2023</td></tr><tr><td>Projects Completion</td><td></td><td></td></tr></table>		Original	Actual	Projects Commencement	1/2/2023	5/17/2023	Projects Completion			<p><b>Consultant</b></p> <p>SBE Varies</p> <p>Local Varies</p> <p>WBE Varies</p> <p>MBE Varies</p> <p><b>Contractor</b></p> <p>SBE Varies</p> <p>Local Varies</p> <p>WBE Varies</p> <p>MBE Varies</p>	<div><div></div><div>Construction</div></div>   <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual									
Projects Commencement	1/2/2023	5/17/2023									
Projects Completion											

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Construction	\$19,674,325	\$747,631	3.80%	\$690,989	FDO will target single scope of work projects commanding high dollar values or combined scopes of work at single buildings/facilities for this funding to simplify tracking and reporting. Mid-County Senior Center: The reroofing project is complete; however, final payment is pending until the carport damage has been repaired. Highridge Family Center Roof Replacement: CID has provided the final set of scopes for the roof replacement. An intial plan for additional work using Q014 funds over the coming years has been developed.
TOTAL	\$19,674,325	\$747,631	3.80%	\$690,989	






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Public Safety Equipment</p> <p>Project Number: Q015</p> <p>BCC District: CW</p> <p>Delivery Method: Direct Purchase</p> <p>Category: S04-Sheriff</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: N/A</p> <p>Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the replacement of PBSO public safety vehicles and related equipment (other than radios), tools and/or services.</p> <p>FY 2022 \$11,182,970.00 IST</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Project Start</td><td>4/3/2024</td><td>4/3/2024</td></tr><tr><td>Project Completion TBD</td><td></td><td></td></tr></table>		Original	Actual	Project Start	4/3/2024	4/3/2024	Project Completion TBD			<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<div><div></div><div>Construction</div></div>   <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual									
Project Start	4/3/2024	4/3/2024									
Project Completion TBD											

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County .				
	A	B	C=B/A	D					
Construction	\$11,182,970	\$0	0.00%	\$0					
Furniture, Fixtures & Equipment	\$0	\$8,419,560	0.00%	\$8,419,560					
TOTAL	\$11,182,970	\$8,419,560	75.29%	\$8,419,560					





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM


**Project Title:** 810 Datura Building Replacement

Project Number: Q018  
BCC District: 07  
Delivery Method: CMAR  
Category: G02-General Government Facilities  
Status: Design  
Designer: Alfonso Hernandez Architect, LLC  
Contractor: D. Stephenson  
Project Manager: Terri Wolfe

#### SCOPE

This project relocates the Community Services Department from 810 Datura Street to the County's 45th Street Complex. The result will be a modern office building to replace the existing facility which is 50+ years old, providing adequate space for services and programs into the future.  
FY 2023 - \$2,600,000  
FY 2024 - \$1,575,600  
FY 2025 - \$5,000,000  
FY 2026 - \$18,660,000

#### PHOTO

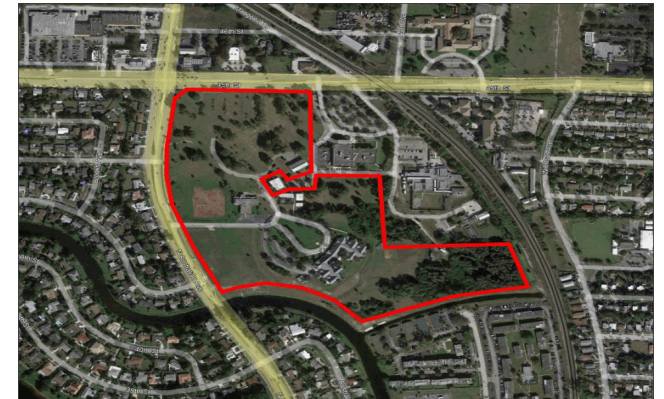

#### SCHEDULE SUMMARY

	Original	Actual
Project Start	10/1/2024	2/9/2022
Programming	5/12/2023	5/12/2023
Design	8/1/2023	8/1/2023
Construction Commencement	1/1/2026	
Construction Completion	6/7/2027	
Substantial Completion	4/5/2027	

#### PARTICIPATION


##### Consultant

SBE 82%  
Local 82%  
WBE 0%  
MBE 15%


##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

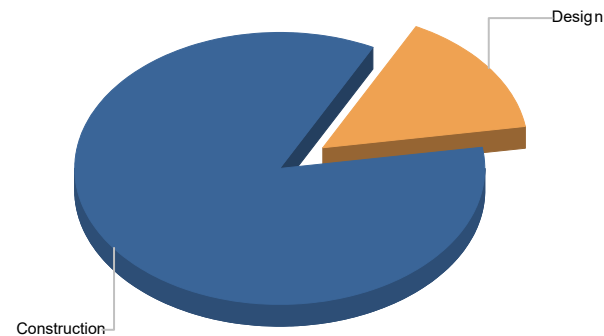

Current Budget

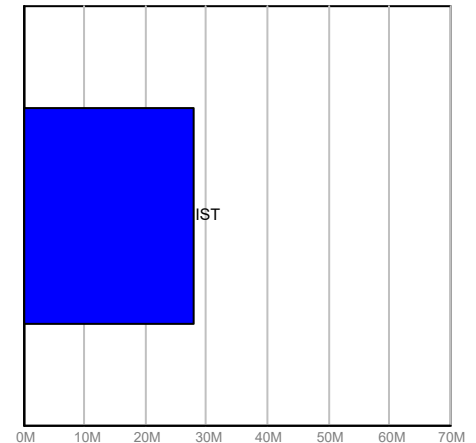

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$4,175,600	\$79,205	1.90%	\$79,205
Construction	\$23,660,000	\$2,570,180	10.86%	\$1,404,224
Other	\$0	\$76,188	0.00%	\$17,138
<b>TOTAL</b>	<b>\$27,835,600</b>	<b>\$2,725,573</b>	<b>9.79%</b>	<b>\$1,500,567</b>

#### NOTES

The drawings are 95% complete, with PPRC review resulting in conditional approval. The lift station size has been reduced to meet the immediate needs of the new facility. CID will meet with Roadway in mid-April to get a progress update on their re-bid process. A temporary signal may become an option to align work efforts. The 100% drawings will be created after value engineering and minor plan adjustments, assuming the tilt-wall option is adopted. A projected funding shortfall is expected to be addressed as part of a bond issuance. The project team is aiming for substantial completion by spring 2027 to allow for FF&E installation.





Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Detention Center Facilities R/R (Phases 3-5)</p> <p>Project Number: Q019</p> <p>BCC District: 03</p> <p>Delivery Method: Construction Management</p> <p>Category: S06-Sheriff - FDO</p> <p>Status: Construction</p> <p>Designer: Leo A. Daly</p> <p>Contractor: Hedrick Brothers Construction</p> <p>Project Manager: Jeffrey Halverson</p>	<p>Phases 3-5 consist of the East Tower and West Tower which are located at the Main Detention Center. The West Detention Center is located in Belle Glade. The design for both towers and the West Detention Center will require repairing and replacing MEP, Fire Sprinkler System, Low Voltage Systems and interior finishes.</p> <p>Detention Center Facilities R/R (Phases 3-5)</p> <p>FY 2018 IST \$8,500,000, FY 2019 IST \$14,700,000, FY 2020 IST \$9,800,000, FY 2022 IST \$10,000,000, FY 2024 IST \$4,802,000 FY 2025 IST \$23,023,759</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>East Tower Design Start</td><td>11/12/2018</td><td>7/11/2019</td></tr><tr><td>East Tower Construction Start-Phase 3</td><td>10/14/2019</td><td>11/18/2020</td></tr><tr><td>East Tower Substantial Completion</td><td>5/11/2022</td><td>12/11/2023</td></tr><tr><td>West Tower Design Start-Phase 4</td><td>3/8/2022</td><td>6/10/2024</td></tr><tr><td>West Tower Construction Start-Phase 4</td><td>1/2/2024</td><td>9/9/2024</td></tr></tbody></table>		Original	Actual	East Tower Design Start	11/12/2018	7/11/2019	East Tower Construction Start-Phase 3	10/14/2019	11/18/2020	East Tower Substantial Completion	5/11/2022	12/11/2023	West Tower Design Start-Phase 4	3/8/2022	6/10/2024	West Tower Construction Start-Phase 4	1/2/2024	9/9/2024	<p><b>Consultant</b></p> <p>SBE 19.88%</p> <p>Local 67%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 63%</p> <p>Local 84%</p> <p>WBE N/A</p> <p>MBE N/A</p>	<p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																		
East Tower Design Start	11/12/2018	7/11/2019																		
East Tower Construction Start-Phase 3	10/14/2019	11/18/2020																		
East Tower Substantial Completion	5/11/2022	12/11/2023																		
West Tower Design Start-Phase 4	3/8/2022	6/10/2024																		
West Tower Construction Start-Phase 4	1/2/2024	9/9/2024																		

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	The Notice to Proceed has been issued, and the permits have been approved. Inmates have been relocated to the East Tower. A preliminary survey of the conditions of doors , locks, lighting, etc., as well as T&B of HVAC, is underway.				
	A	B	C=B/A	D					
Design	\$2,142,334	\$2,951,929	137.79%	\$2,216,231					
Construction	\$42,383,760	\$27,676,961	65.30%	\$25,958,961					
Other	\$23,048,067	\$1,328,794	5.77%	\$952,935					
Contingency	\$4,802,000	\$2,300,000	47.90%	\$2,213,195					
TOTAL	\$72,376,161	\$34,257,684	47.33%	\$31,341,322					




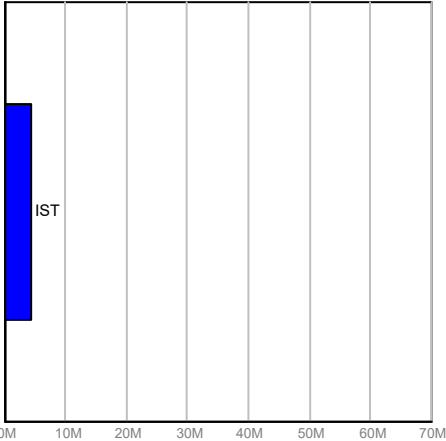
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> West Boynton Park Athletic Field Renovations Sports Turf</p> <p>Project Number: T002</p> <p>BCC District: 02</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 &amp; 2.</p> <p>Funded:</p> <p>FY 2017 \$2,000,000</p> <p>FY 2018 (\$1,011,658)</p> <p>FY 2022 \$1,196,658</p> <p>FY 2024 \$2,202,067</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>3/9/2020</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>10/16/2020</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/23/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>6/6/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	3/9/2020	Finalization of Existing Site Surveys	8/30/2020	10/16/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/23/2023	Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023	Turf Contract GMP Executed	9/17/2024	9/17/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	 <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	3/9/2020																																	
Finalization of Existing Site Surveys	8/30/2020	10/16/2020																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/23/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023																																	
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	<p>The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.</p>				
	A	B	C=B/A	D					
Design	\$1,000,000	\$223,724	22.37%	\$183,103					
Construction	\$3,387,067	\$3,625,200	107.03%	\$51,890					
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0					
Other	\$0	\$459	0.00%	\$459					
Contingency	\$0	\$0	0.00%	\$0					
<b>TOTAL</b>	<b>\$4,387,067</b>	<b>\$3,849,383</b>	<b>87.74%</b>	<b>\$235,452</b>					





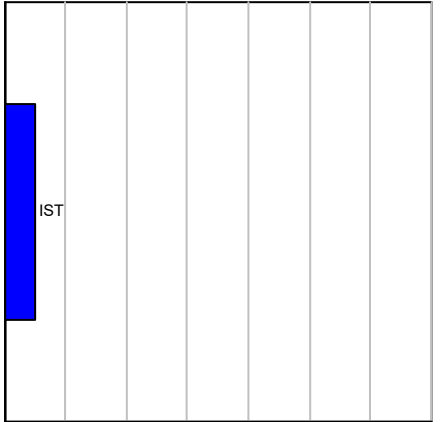
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Buttonwood Park</p> <p>Project Number: T003</p> <p>BCC District: 03</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 2 &amp; 3</p> <p>Funded:</p> <p>FY 2017 \$1,500,000</p> <p>FY 2018 (\$1,488,342)</p> <p>FY 2021 \$900,000</p> <p>FY 2022 \$1,963,342</p> <p>FY 2024 \$2,193,828</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>8/30/2020</td><td>5/18/2021</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>8/23/2021</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/23/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>6/6/2023</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr></tbody></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	8/30/2020	5/18/2021	Finalization of Existing Site Surveys	8/30/2020	8/23/2021	Design RFP Proposals Due	9/4/2020	9/10/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/23/2023	Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023	Turf Contract Substantial Completion	1/30/2026		Turf Contract GMP Executed	9/17/2024	9/17/2024	Design RFP Final Selection	10/29/2020	10/29/2020	<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<p><b>Current Budget</b></p> <p>Construction</p>  <p><b>Fund Source</b></p> 
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	8/30/2020	5/18/2021																																	
Finalization of Existing Site Surveys	8/30/2020	8/23/2021																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/23/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023																																	
Turf Contract Substantial Completion	1/30/2026																																		
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date					
	A	B	C=B/A	D					
Design	\$0	\$251,666	0.00%	\$211,152					
Construction	\$5,068,828	\$4,241,822	83.68%	\$85,784					
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0					
Other	\$0	\$12,458	0.00%	\$12,458					
Contingency	\$0	\$0	0.00%	\$0					
<b>TOTAL</b>	<b>\$5,068,828</b>	<b>\$4,505,947</b>	<b>88.90%</b>	<b>\$309,394</b>					

GMP package submitted 7/30/2024 for 9/17/2024 BCC meeting. Project funding shortfall rectification complete. Building permit submission made May 2024; issuance expected to be prior to construction NTP. Pre-construction kick off meeting held 9/25/2024. OAC meetings held 1st and 3rd Wednesday at 10:00 AM, Notice to Proceed was issued October 21, 2024. Field drainage is underway, scoreboard relocation (2) complete, irrigation system to be reconfigured to accommodate the new fields. Parks & Recreation will be renovating the grass field at the same time the turf installation is underway. All fields will be down an anticipated 3 months.




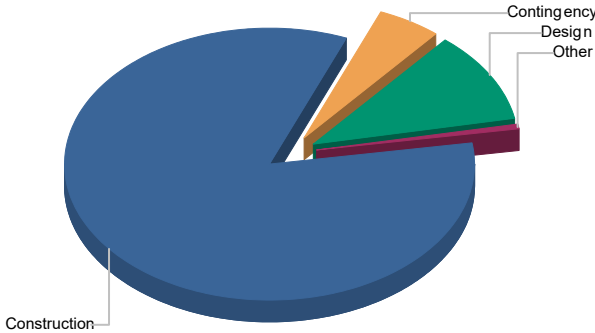
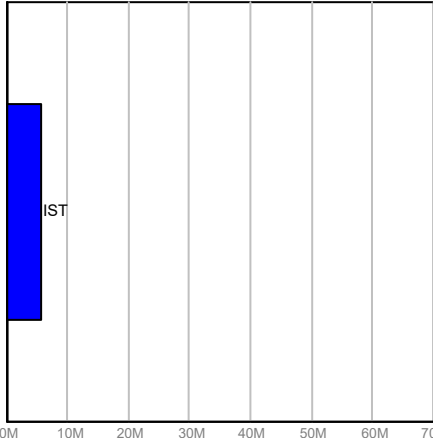
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Community Park - New Development</p> <p>Project Number: T004</p> <p>BCC District: Multiple</p> <p>Delivery Method: Varies</p> <p>Category: N02-New Park Development</p> <p>Status: Varies</p> <p>Designer: Varies</p> <p>Contractor: Varies</p> <p>Project Manager: Varies</p>	<p>Construction of neighborhood park facilities for under served Countywide Community Revitalization Team (CCRT) areas.</p> <p>FY 2017 IST: \$1,000,000</p> <p>FY 2021 IST: \$4,900,000</p> <p>FY 2022 IST: (\$3,900,000)</p> <p>FY 2024 IST: \$3,610,000</p>	

SCHEDULE SUMMARY		PARTICIPATION	FUNDING	
Original	Actual			
Varies by location. Work ongoing		<b>Consultant</b>	 	
		SBE Varies		
		Local Varies		
		WBE Varies		
		MBE Varies		
		<b>Contractor</b>		
		SBE Varies		
		Local Varies		
		WBE Varies		
		MBE Varies		

FINANCIAL SUMMARY					NOTES	
	Project Budget	Committed	% Committed	Paid To Date	<p>Bridgeman; Construction of a .32 acre neighborhood park on a WUD parcel to serve the Belvedere Heights CCRT neighborhood within the Westgate CRA. Completed in 5/2020 with \$32,415 of IST funds. Paulette Burdick; Supplemental #4 NTP was issued on April 3, 2025. The Supplemental #5 proposal for the relocation of the boundary line redesign was submitted, reviewed, and returned to the consultant for resubmittal Gramercy; See P945 for reporting.</p>	
	A	B	C=B/A	D		
Design	\$599,983	\$837,418	139.57%	\$791,118		
Construction	\$4,692,035	\$291,998	6.22%	\$264,671		
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0		
Other	\$32,965	\$33,190	100.68%	\$33,190		
Contingency	\$295,000	\$0	0.00%	\$0		
<b>TOTAL</b>	<b>\$5,619,983</b>	<b>\$1,162,606</b>	<b>20.69%</b>	<b>\$1,088,979</b>		



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** FY 2018 Playground Replacements-Countywide  
**Project Number:** T026  
**BCC District:** Multiple  
**Delivery Method:** Minor Construction Annual Contract  
**Category:** P06-Playground Replacement  
**Status:** Construction  
**Designer:** Varies  
**Contractor:** DW Recreation  
**Project Manager:** Javier Torres

#### SCOPE

Replacement of Playgrounds: Okeeheelee (Alligator Playground), Loggerhead Picnic Area, Glades Pioneer Park, Jupiter Farms, Buttonwood, Morikami Biwa Pavilion, Ocean Cay, Seminole Palms, Dubois, Carlin (W. Gumbo Limbo Playground & W. Playground), JPP. FY 2018 \$812,000, FY 2019 \$1,589,750, and FY2024 \$293,014.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Design Start	7/1/2020	7/1/2020
Phase I Substantial Completion	12/19/2022	11/10/2023
Phase II Construction Start	6/12/2023	
Phase I Completion	12/8/2023	12/8/2023
Phase III Start	3/8/2024	

#### PARTICIPATION


##### Consultant

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

##### Contractor

SBE 95.5%  
Local 95.5%  
WBE N/A  
MBE N/A

#### FUNDING

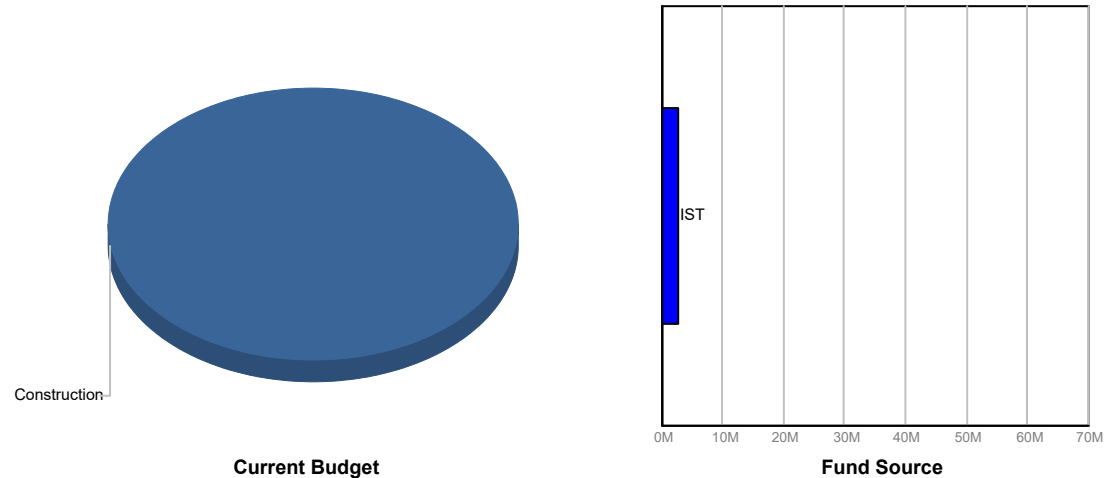

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$1,102,988	0.00%	\$1,102,988
Construction	\$2,694,764	\$73,852	2.74%	\$73,852
<b>TOTAL</b>	<b>\$2,694,764</b>	<b>\$1,176,841</b>	<b>43.67%</b>	<b>\$1,176,841</b>

#### NOTES

Phase I: Carlin/Jupiter Farms/Ocean Cay/& Dubois are complete. Phase II Projects: Loggerhead & Glades Pioneer: Engineering services proposal was sent back to the consultants for revision. Phase III: Buttonwood, Morikami, Seminole Palms, and JPP; No activity.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Bert Winters Park Redevelopment

Project Number: T041  
BCC District: 01  
Delivery Method: Annual Contract  
Category: E02-Existing Park Redevelopment or Expansion  
Status: Permitting  
Designer: Architecture Green  
Contractor: TBD  
Project Manager: Sunil Jagoo

#### SCOPE

Demolish former PBMI building, tennis courts, and playground. Remove lights and poles servicing Field 2. Renovate Baseball Field 1. Construct new regulation 220' x 360' multipurpose field. Construct new 30' x 60' rental pavilion. Construct new playground area. Renovate existing day use dock for public use. Construct new paved parking, curbing, landscaping, sidewalks and picnic areas. Install new underground infrastructure and site lighting. FY2019 IST \$200,000, FY2021 IST \$1,500,000, and FY2024 IST \$207,400  
\$220K FIND Phase II Planning, Design and Permitting Costs  
\$800K FIND Phase II Redevelopment (Construction) – Grant Contract Executed.

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	8/22/2019	8/22/2019
Asbestos Report Initiated	8/23/2019	8/23/2019
Asbestos Report Completion	10/1/2019	10/1/2019
Demolition Start	11/12/2019	4/16/2020
Demolition Completion	12/5/2019	8/17/2020
Design Completion	7/1/2020	11/16/2022
Permitting Start(Dock)	7/15/2020	11/30/2022
Permitting Completion(Dock)	12/31/2020	3/29/2023
Permitting Start(Site)	4/9/2024	4/9/2024
IFQ Advertise	11/5/2024	11/5/2024
Addendum 2	12/3/2024	12/3/2024
Bid Due Extended	12/19/2024	

#### PARTICIPATION


##### Consultant

SBE 89.28%  
Local 100%  
WBE N/A  
MBE N/A


##### Contractor

SBE TBD  
Local TBD  
WBE TBD  
MBE TBD

#### FUNDING

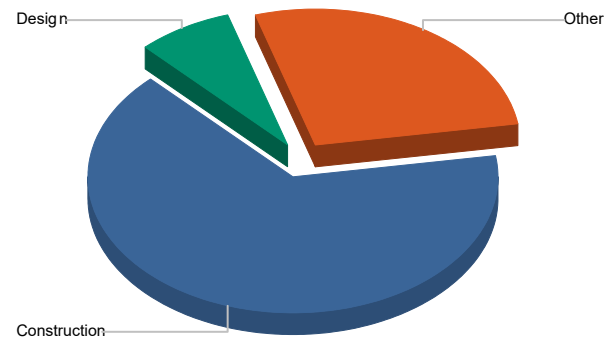

Current Budget

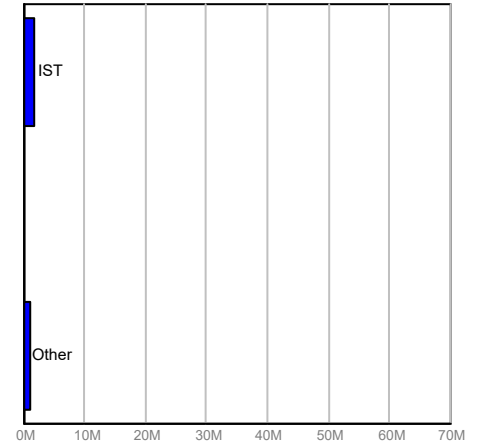

Fund Source

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$220,000	\$0	0.00%	\$0
Construction	\$1,907,400	\$654,627	34.32%	\$255,738
Other	\$800,000	\$15,345	1.92%	\$15,345
Contingency	\$0	\$841	0.00%	\$841
<b>TOTAL</b>	<b>\$2,927,400</b>	<b>\$670,813</b>	<b>22.91%</b>	<b>\$271,924</b>

#### NOTES

The winning bidder's package is under review by Facilities Business Operations and OEBO to determine whether an error on OEBO Schedule 2 is considered minor or renders the bid non-responsive. The building permit is ready for pickup once a contractor has been selected.






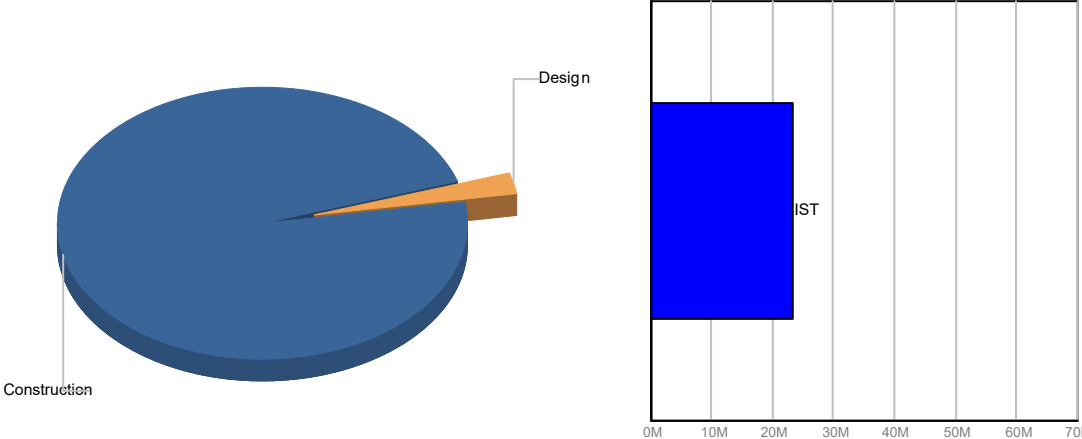
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Aqua Crest Pool Facility Replacement</p> <p>Project Number: T077</p> <p>BCC District: 07</p> <p>Delivery Method: CMR</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: Ohlson Lavoie Collaborative</p> <p>Contractor: TBD</p> <p>Project Manager: Javier Torres/David Hawke</p>	<p>The work consist of the design and renovation of the existing Aqua Crest pool facility. The scope includes but is not limited to: pool improvements such as leak detection, re-surface, lane marker replacement, filtration system replacement; pool deck renovations; demolition of wadding pool; new splash pad; relocation of ticketing booth, admin offices, guards room and weight's room; bathroom renovations; new shade structures and Marquee sign.</p> <p>FY 2019 IST: \$6,000,000</p> <p>FY 2022 IST: (\$5,000,000)</p> <p>FY 2023 IST: \$11,152,500</p> <p>FY 2024 IST: \$11,058,928</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Pre-Scope meeting</td><td>2/20/2019</td><td>2/20/2019</td></tr><tr><td>Design Services Advertisement</td><td>6/17/2019</td><td>8/4/2019</td></tr><tr><td>Consultant BCC Approval</td><td>1/14/2020</td><td>5/5/2020</td></tr><tr><td>Design Start</td><td>1/21/2020</td><td>6/6/2023</td></tr><tr><td>Construction Start</td><td>3/9/2021</td><td></td></tr><tr><td>Substantial Completion</td><td>3/8/2022</td><td></td></tr><tr><td>Project Close-out</td><td>5/3/2022</td><td></td></tr></tbody></table>		Original	Actual	Pre-Scope meeting	2/20/2019	2/20/2019	Design Services Advertisement	6/17/2019	8/4/2019	Consultant BCC Approval	1/14/2020	5/5/2020	Design Start	1/21/2020	6/6/2023	Construction Start	3/9/2021		Substantial Completion	3/8/2022		Project Close-out	5/3/2022		<p><b>Consultant</b></p> <p>SBE 20%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	
	Original	Actual																								
Pre-Scope meeting	2/20/2019	2/20/2019																								
Design Services Advertisement	6/17/2019	8/4/2019																								
Consultant BCC Approval	1/14/2020	5/5/2020																								
Design Start	1/21/2020	6/6/2023																								
Construction Start	3/9/2021																									
Substantial Completion	3/8/2022																									
Project Close-out	5/3/2022																									

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>OLC Architects have been given the FDO design and construction budget (\$22.5M). We estimate that a ±9,500 sq. ft. building is the correct total net square footage. As requested by Parks, the new 52-meter competition swimming pool, along with the 'learn-to-swim' program, will be included in the schematic design for Phase 1 while ensuring underground infrastructure is in place for Phase 2 and controlling scope to maintain the budget.</p>
	A	B	C=B/A	D	
Design	\$600,000	\$1,679,103	279.85%	\$334,024	
Construction	\$22,611,428	\$43,949	0.19%	\$43,949	
<b>TOTAL</b>	<b>\$23,211,428</b>	<b>\$1,723,053</b>	<b>7.42%</b>	<b>\$377,974</b>	





Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM

Project Title: Dyer Park Athletic Field Renovation

Project Number: T099  
BCC District: 07  
Delivery Method: CMAR  
Category: A06-Athletic Field Renovations  
Status: Construction  
Designer: Florida Transportation Engineering  
Contractor: LTG Sports Turf One  
Project Manager: David Polson

SCOPE

Replacement of existing grass field turf with synthetic turf on multi-purpose field 3, 4, & 5 as well as additional damaged area.  
Funded: FY 2020 \$6,000,000  
FY 2024 \$1,724,581

PHOTO



SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/29/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	10/23/2023
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023
Turf Contract GMP Executed	9/17/2024	9/17/2024
Turf Contract Substantial Completion	1/30/2026	

PARTICIPATION


Consultant

SBE 25%  
Local 25%  
WBE 0%  
MBE 6.13%

Contractor

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

FUNDING

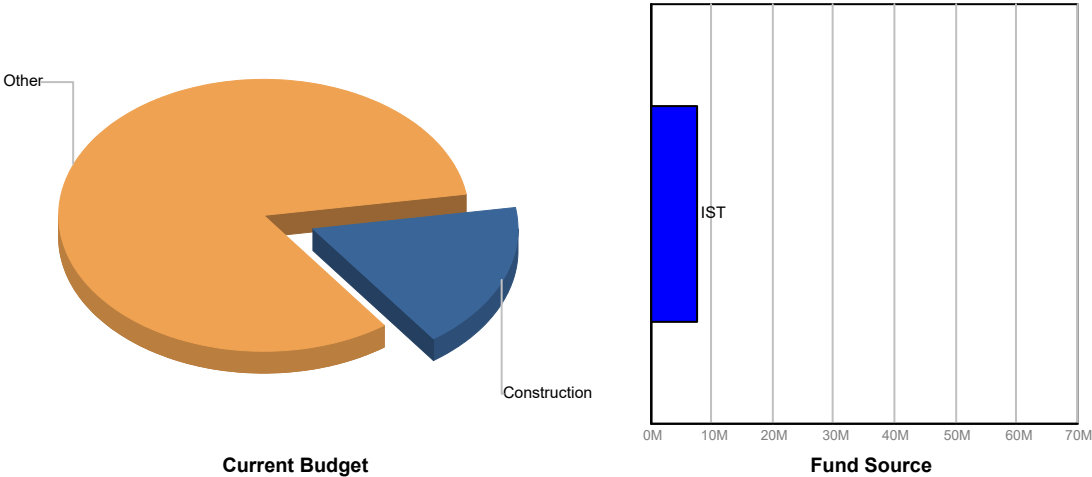

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,347,644	\$295,422	21.92%	\$291,319
Other	\$6,376,937	\$6,486,475	101.72%	\$135,640
TOTAL	\$7,724,581	\$6,781,896	87.80%	\$426,959

NOTES

The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Caloosa Park Athletic Field Renovation</p> <p>Project Number: T100</p> <p>BCC District: 04</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 &amp; 3 as well as converted from multi-purpose field 4 converted from softball.</p> <p>Funded: FY 2020 \$4,000,000 and FY 2024 \$3,812,826</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>3/30/2020</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>6/7/2020</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/10/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2023</td><td>6/6/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/18/2023</td><td>9/18/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></tbody></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	3/30/2020	Finalization of Existing Site Surveys	8/30/2020	6/7/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/10/2023	Turf Supplier RFP Proposal Due	4/30/2023	6/6/2023	Turf Contract GMP Executed	9/18/2023	9/18/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	3/30/2020																																	
Finalization of Existing Site Surveys	8/30/2020	6/7/2020																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/10/2023																																	
Turf Supplier RFP Proposal Due	4/30/2023	6/6/2023																																	
Turf Contract GMP Executed	9/18/2023	9/18/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>GMP package submitted 7/30/2024 for 9/17/2024 BCC meeting. Project funding shortfall rectification complete. Building permit submission made May 2024; issuance expected to be prior to construction NTP. Pre-construction kick off meeting held 9/25/2024. OAC meetings held 1st and 3rd Wednesday at 10:00 AM, Notice to Proceed was issued October 21, 2024. All underground utilities are complete, foundation for dugouts are being formed, topping stone is complete, turf installation anticipated week of May 5th, reclaimed water relocation continues. Anticipated substantial completion 6/4/2025.</p>
	A	B	C=B/A	D	
Construction	\$7,792,826	\$6,788,252	87.11%	\$1,094,876	
Other	\$20,000	\$193,035	965.17%	\$165,505	
<b>TOTAL</b>	<b>\$7,812,826</b>	<b>\$6,981,287</b>	<b>89.36%</b>	<b>\$1,260,381</b>	




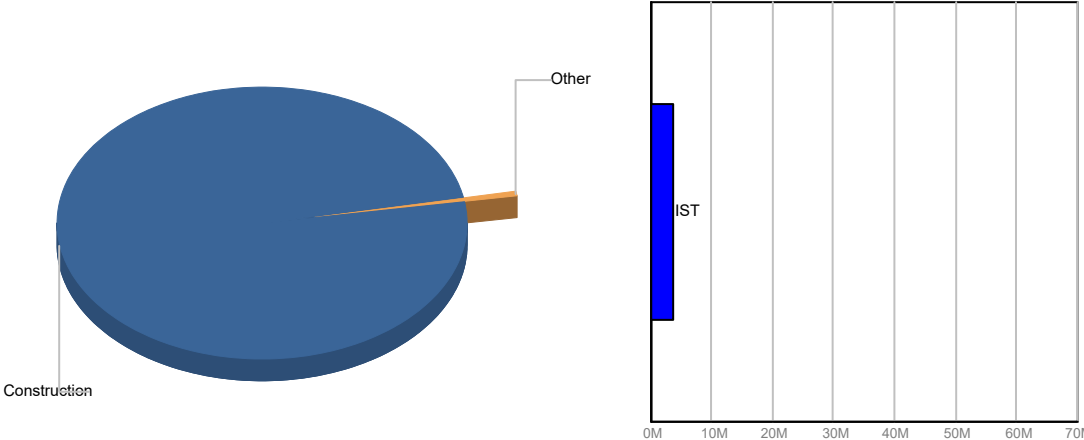
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title: JPP Athletic Field Renovation</b></p> <p>Project Number: T101</p> <p>BCC District: 03</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on the Miracle League Field as well as short field multi-purpose field, converted from softball 1.</p> <p>Funded: FY 2020 \$3,222,000 and FY2024 \$392,840</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>4/15/2020</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>10/15/2020</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/10/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>6/6/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></tbody></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	4/15/2020	Finalization of Existing Site Surveys	8/30/2020	10/15/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/10/2023	Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023	Turf Contract GMP Executed	9/17/2024	9/17/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	 <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	4/15/2020																																	
Finalization of Existing Site Surveys	8/30/2020	10/15/2020																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/10/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023																																	
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Construction	\$3,596,840	\$204,487	5.69%	\$204,487	
Other	\$16,000	\$1,054,567	6,591.05%	\$70,667	
<b>TOTAL</b>	<b>\$3,612,840</b>	<b>\$1,259,055</b>	<b>34.85%</b>	<b>\$275,154</b>	<p>The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.</p>



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Loggers Run Park Athletic Field Renovation  
**Project Number:** T102  
**BCC District:** 05  
**Delivery Method:** CMAR  
**Category:** A06-Athletic Field Renovations  
**Status:** Construction  
**Designer:** Florida Transportation Engineering  
**Contractor:** LTG Sports Turf One  
**Project Manager:** David Polson

#### SCOPE

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.  
FY 2020 IST \$3,200,000  
FY 2022 IST (\$700,000)  
FY 2024 IST \$1,221,889

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	3/16/2020
Finalization of Existing Site Surveys	8/30/2020	10/16/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	12/31/2021	10/10/2023
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023
Turf Contract GMP Executed	9/17/2024	9/17/2024
Turf Contract Substantial Completion	1/30/2026	3/25/2025

#### PARTICIPATION


##### Consultant

SBE 25%  
Local 25%  
WBE 0%  
MBE 6.13%

##### Contractor

SBE N/A  
Local N/A  
WBE N/A  
MBE N/A

#### FUNDING

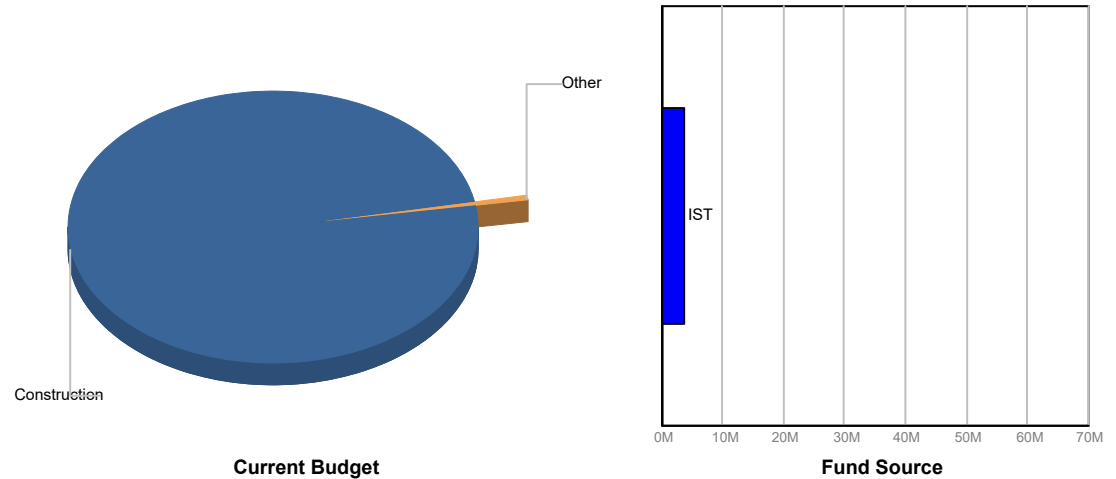

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,705,889	\$215,009	5.80%	\$188,505
Other	\$16,000	\$3,099,249	19,370.31%	\$1,550,243
<b>TOTAL</b>	<b>\$3,721,889</b>	<b>\$3,314,259</b>	<b>89.05%</b>	<b>\$1,738,748</b>

#### NOTES

GMP package submitted 7/30/2024 for 9/17/2024 BCC meeting. Project funding shortfall rectification complete. Building permit submission made May 2024; issuance expected to be prior to construction NTP. Pre-construction kick off meeting held 9/25/2024. OAC meetings held 1st and 3rd Wednesday at 10:00 AM, Notice to Proceed was issued October 21, 2024. All underground utilities are complete, foundation for dugouts are being formed, topping stone is complete, turf installation anticipated week of May 5th, reclaimed water relocation continues. Anticipated substantial completion 6/4/2025.





Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Samuel Friedland District Park Expansion</p> <p>Project Number: T103</p> <p>BCC District: 06</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 9 &amp; 10 as well as the open play field.</p> <p>Funded: FY 2020 \$3,000,000 and FY 2024 \$3,196,109</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Begin Existing Site Surveys</td><td>1/20/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>2/28/2020</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>10/16/2020</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/10/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>9/6/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></tbody></table>		Original	Actual	Begin Existing Site Surveys	1/20/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	2/28/2020	Finalization of Existing Site Surveys	8/30/2020	10/16/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/10/2023	Turf Supplier RFP Proposal Due	4/30/2022	9/6/2023	Turf Contract GMP Executed	9/17/2024	9/17/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	
	Original	Actual																																	
Begin Existing Site Surveys	1/20/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	2/28/2020																																	
Finalization of Existing Site Surveys	8/30/2020	10/16/2020																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/10/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	9/6/2023																																	
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Construction	\$6,181,109	\$187,049	3.03%	\$158,853	The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.
Other	\$15,000	\$5,244,234	34,961.56%	\$97,597	
TOTAL	\$6,196,109	\$5,431,283	87.66%	\$256,450	





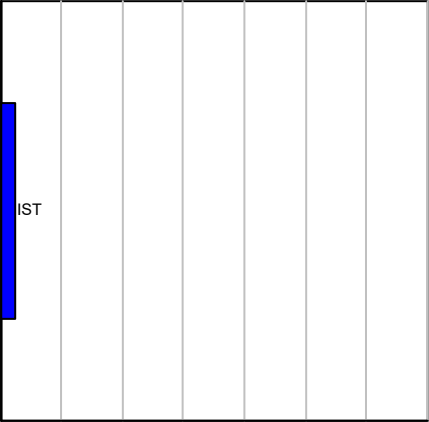
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Westgate Park Restroom and Athletic Field Renovation</p> <p>Project Number: T110</p> <p>BCC District: 07</p> <p>Delivery Method: CMAR</p> <p>Category: E02-Existing Park Redevelopment or Expansion</p> <p>Status: Construction</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.</p> <p>Funded:</p> <p>FY 2020 IST \$250,000</p> <p>FY 2022 IST \$1,750,000</p> <p>FY 2024 IST \$398,460</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>6/1/2021</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>8/25/2021</td></tr><tr><td>Design RFP Proposals Due</td><td>9/4/2020</td><td>9/10/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>4/20/2021</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/10/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>6/6/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></tbody></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	6/1/2021	Finalization of Existing Site Surveys	8/30/2020	8/25/2021	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	12/31/2021	10/10/2023	Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023	Turf Contract GMP Executed	9/17/2024	9/17/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	 <p>Other</p> <p>IST</p> <p>Construction</p> <p><b>Current Budget</b></p>  <p>Fund Source</p>
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	6/1/2021																																	
Finalization of Existing Site Surveys	8/30/2020	8/25/2021																																	
Design RFP Proposals Due	9/4/2020	9/10/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	4/20/2021																																	
Design Completion	12/31/2021	10/10/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023																																	
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date					
	A	B	C=B/A	D					
Construction	\$2,397,210	\$2,092,064	87.27%	\$192,922					
Other	\$1,250	\$13,165	1,053.17%	\$0					
TOTAL	\$2,398,460	\$2,105,229	87.77%	\$192,922					

The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.



## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Dubois Park Var Historic Building Repair and Renovation

Project Number: T111

BCC District: 01

Delivery Method: Annual Contract

Category: P08-Public Building Repair Replacement & Expansion

Status: Construction

Designer: Varies

Contractor: Robling Architecture Construction

Project Manager: Javier Torres/Benjamin Carroll

#### SCOPE

The project consists of relocating the Pineapple Packing House structure, wood framing repairs, roof replacement and new windows, doors, electrical and HVAC.

IST FY 2020 - \$250,000

IST FY 2021 - \$250,000

IST FY 2022 - \$250,000

IST FY 2023 - \$250,000

IST FY 2024 - \$644,585

IST FY 2025 - \$599,415

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
Project Start	4/12/2021	4/12/2021
Project Completion	12/13/2021	

#### PARTICIPATION

##### Consultant

SBE N/A

Local N/A

WBE N/A

MBE N/A

##### Contractor


SBE 10.46%

Local 100%


WBE 0%

MBE 0%

#### FUNDING

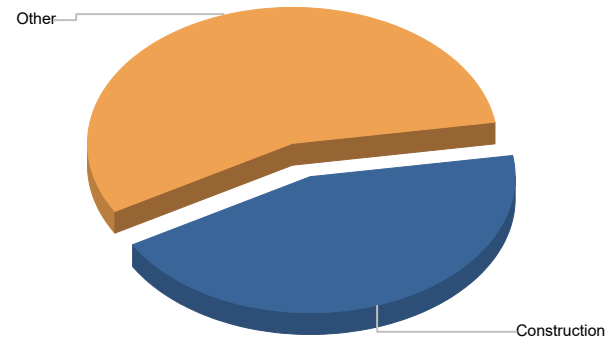

Current Budget

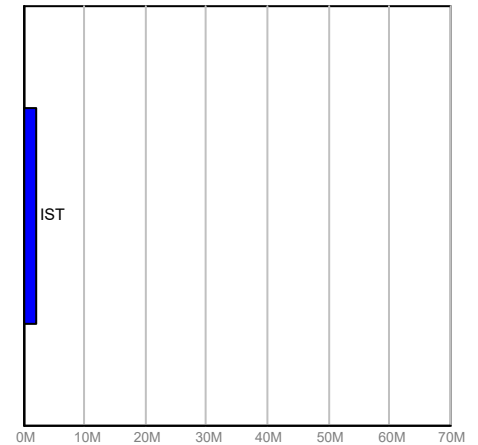

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$992,750	\$299,017	30.12%	\$291,169
Other	\$1,251,250	\$77,633	6.20%	\$52,029
<b>TOTAL</b>	<b>\$2,244,000</b>	<b>\$376,650</b>	<b>16.78%</b>	<b>\$343,198</b>

#### NOTES

Pineapple House (\$400,000): Robling's work is complete. Processing final payment. Pioneer House: CID FSPM awaits Parks comments on conceptual to forward to the architect. Dubois House: Colomé & Associates CSA #1 package, now renamed CSA #2 for the Master Plan, has been finalized and is scheduled for approval at the BCC meeting in June 2025.





## Monthly Infrastructure Sales Tax Project Report

### Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

#### DESCRIPTION/TEAM

**Project Title:** Canyon District Park New Park Development  
**Project Number:** T122  
**BCC District:** 05  
**Delivery Method:** CMAR  
**Category:** N02-New Park Development  
**Status:** Construction  
**Designer:** Architecture Green  
**Contractor:** Kaufman Lynn  
**Project Manager:** David Polson

#### SCOPE

The project consists of the construction of a 52 acre Park south of Boynton Beach Blvd, along the west side of Acme Dairy Rd. with the Canyon Lakes Communities bordering the south and west limits of the site. The park will be constructed in two phases. Phase I will need to be completed in order to transfer the multi-purpose activities that currently take place on two existing soccer fields located to the west of the park. Once transferred the old soccer fields site will become the site of the new Canyon District Library. Impact Fees \$4,755,000  
FY 2021 IST \$12,000,000  
FY 2022 IST \$12,983,740  
FY 2024 IST \$20,000,000

#### PHOTO



#### SCHEDULE SUMMARY

	Original	Actual
GMP Approval-Phase I	1/14/2021	5/4/2021
Construction Start-Phase I	1/27/2021	1/4/2021
Substantial Completion-Phase I	1/27/2022	9/27/2024
Substantial Completion-Phase II	1/30/2026	
Construction Start-Phase II	3/4/2024	8/1/2024
GMP Approval Phase 2	7/2/2024	7/2/2024

#### PARTICIPATION


##### Consultant

SBE 75.93%  
Local 100%  
WBE 21.41%  
MBE 0%

##### Contractor

SBE 22.32%  
Local 100%  
WBE 22.32%  
MBE 22.32%

#### FUNDING

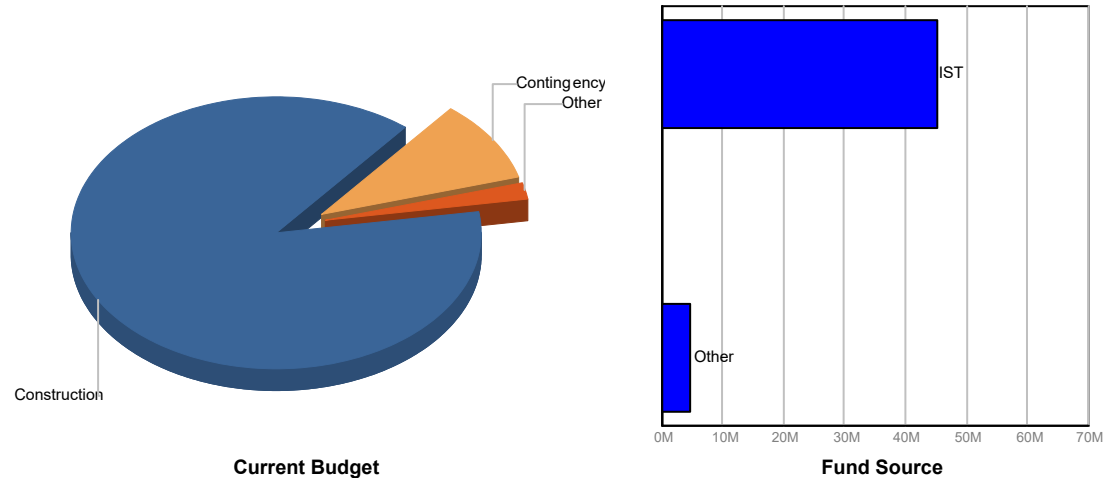

#### FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$124,726	0.00%	\$201,313
Construction	\$44,070,720	\$39,763,698	90.23%	\$24,569,304
Other	\$1,000,000	\$1,363,222	136.32%	\$1,280,773
Contingency	\$4,755,000	\$1,500,000	31.55%	\$1,500,000
<b>TOTAL</b>	<b>\$49,825,720</b>	<b>\$42,751,647</b>	<b>85.80%</b>	<b>\$27,551,389</b>

#### NOTES

Phases 1 and 1A: Construction is complete. Close-out activities are progressing, with Phase 1 A final pay application re-submitted on 3/7/25. Phase 2: Building permits issued/ Construction NTP issued on 7/16/2024, with construction commencement date of 8/1/2024. Phase 2 construction kick-off meeting held on 7/29/2024. Ground Breaking Ceremony conducted on 9/30/2024. Current Progress: Sand volleyball restroom roofing complete awaiting inspection for dry-in, play structures are complete, shade structure foundation has begun, all fields are graded to grade, outfield fencing post installation is ongoing, restroom building and concession building have been inspected and are now ready to finalize roofing installation, first lift of asphalt on parking lot and roads is complete.




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Okeeheslee Park South Expansion</p> <p>Project Number: T125</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Contract</p> <p>Category: E02-Existing Park Redevelopment or Expansion</p> <p>Status: Design</p> <p>Designer: Colome' &amp; Associates, Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: Javier Torres</p>	<p>Inclusion of new park amenities and accrual of funds for the development of a camping island, picnic island and RV park.</p> <p>FY21: \$1,000,000</p> <p>FY22: \$1,000,000</p> <p>FY24: \$452,010</p> <p>FY25: \$1,705,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING												
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Start Date</td><td>9/9/2021</td><td>2/10/2025</td></tr><tr><td>Completion Date</td><td>5/31/2022</td><td></td></tr><tr><td>Pre-Scope Meeting</td><td>11/6/2024</td><td>11/6/2024</td></tr></table>		Original	Actual	Start Date	9/9/2021	2/10/2025	Completion Date	5/31/2022		Pre-Scope Meeting	11/6/2024	11/6/2024	<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div><div></div><div>IST</div></div> <div><div>Construction</div><div>Current Budget</div></div> <div><div></div><div>Fund Source</div></div>
	Original	Actual												
Start Date	9/9/2021	2/10/2025												
Completion Date	5/31/2022													
Pre-Scope Meeting	11/6/2024	11/6/2024												

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	Review of the Master Plan proposal is ongoing.
	A	B	C=B/A	D	
Construction	\$4,157,010	\$62,122	1.49%	\$62,122	
TOTAL	\$4,157,010	\$62,122	1.49%	\$62,122	





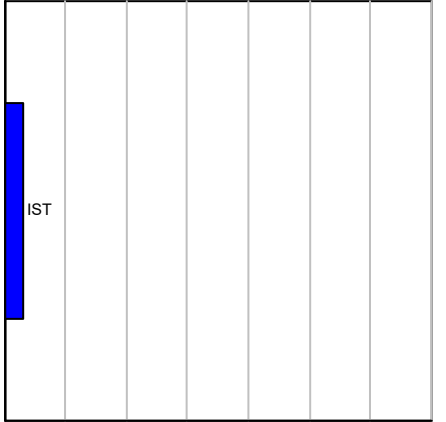
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> JPP Parks Division Office Building Addition</p> <p>Project Number: T174</p> <p>BCC District: 03</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement &amp; Expans</p> <p>Status: Design</p> <p>Designer: Colome' &amp; Associates, Inc.</p> <p>Contractor: TBD</p> <p>Project Manager: Eric Chimienti</p>	<p>Permanent office space is needed to replace two (2) modular office trailers that have exceeded their useful life and are rotting . The addition would be to the current Parks Operations Administration building (trailers more than 20 years old - rotting).</p> <p>FY2023 \$750,000.00</p> <p>FY2024 \$344,650.00</p> <p>FY2025 \$2,075,000.00</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING						
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Preliminary Proposal</td><td>11/19/2024</td><td>1/6/2025</td></tr></tbody></table>		Original	Actual	Preliminary Proposal	11/19/2024	1/6/2025	<p><b>Consultant</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><div></div><div>Construction</div></div>  <p>Current Budget</p>  <p>Fund Source</p>
	Original	Actual						
Preliminary Proposal	11/19/2024	1/6/2025						

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Recieved preliminary proposal from Parks and is currently under review within CID.				
	A	B	C=B/A	D					
Construction	\$3,169,650	\$4,486	0.14%	\$4,486					
TOTAL	\$3,169,650	\$4,486	0.14%	\$4,486					




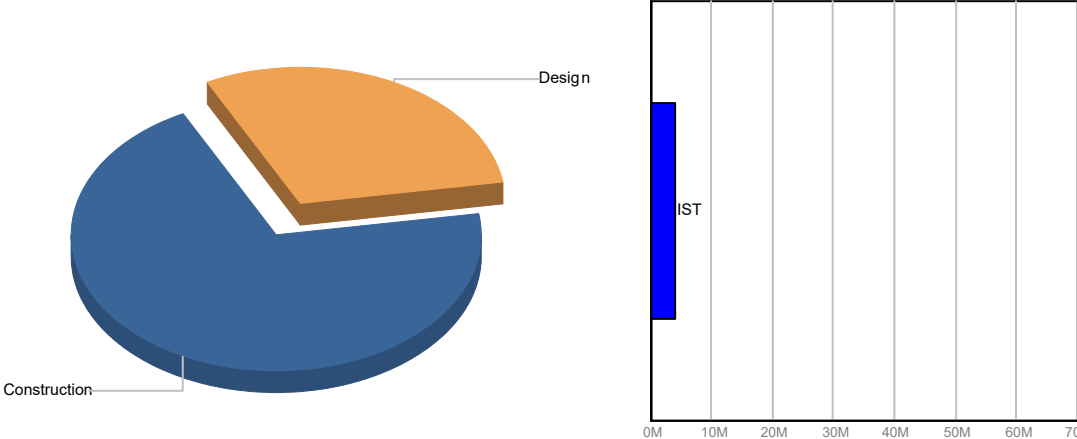
Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Glades Pioneer Park Athletic Field Renovation</p> <p>Project Number: T175</p> <p>BCC District: 06</p> <p>Delivery Method: CMAR</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Permitting</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: LTG Sports Turf One</p> <p>Project Manager: David Polson</p>	<p>Athletic facility improvement to Glades Pioneer Park will allow for year-round use of football/soccer fields. High quality artificial surfacing will provide an excellent facility for youth and allow for minimal downtime for positive youth activities.</p> <p>Funded:</p> <p>FY 2021 \$210,000</p> <p>FY 2023 \$1,009,000</p> <p>FY 2024 \$2,824,756</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																	
<table><tr><th></th><th>Original</th><th>Actual</th></tr><tr><td>Begin Existing Site Surveys</td><td>1/29/2020</td><td>1/29/2020</td></tr><tr><td>Complete Existing Site Surveys</td><td>6/30/2020</td><td>5/18/2020</td></tr><tr><td>Finalization of Existing Site Surveys</td><td>8/30/2020</td><td>9/18/2020</td></tr><tr><td>Design RFP Final Selection</td><td>10/29/2020</td><td>10/29/2020</td></tr><tr><td>Consultant Contract Issuance</td><td>12/14/2020</td><td>9/17/2024</td></tr><tr><td>Design Completion</td><td>12/31/2021</td><td>10/10/2023</td></tr><tr><td>Turf Supplier RFP Proposal Due</td><td>4/30/2022</td><td>6/6/2023</td></tr><tr><td>Turf Supplier Contract Executed</td><td>9/8/2023</td><td>9/8/2023</td></tr><tr><td>Turf Contract GMP Executed</td><td>9/17/2024</td><td>9/17/2024</td></tr><tr><td>Turf Contract Substantial Completion</td><td>1/30/2026</td><td></td></tr></table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	9/17/2024	Design Completion	12/31/2021	10/10/2023	Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023	Turf Supplier Contract Executed	9/8/2023	9/8/2023	Turf Contract GMP Executed	9/17/2024	9/17/2024	Turf Contract Substantial Completion	1/30/2026		<p><b>Consultant</b></p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	 <p>Design</p> <p>Construction</p> <p>IST</p> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual																																	
Begin Existing Site Surveys	1/29/2020	1/29/2020																																	
Complete Existing Site Surveys	6/30/2020	5/18/2020																																	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																																	
Design RFP Final Selection	10/29/2020	10/29/2020																																	
Consultant Contract Issuance	12/14/2020	9/17/2024																																	
Design Completion	12/31/2021	10/10/2023																																	
Turf Supplier RFP Proposal Due	4/30/2022	6/6/2023																																	
Turf Supplier Contract Executed	9/8/2023	9/8/2023																																	
Turf Contract GMP Executed	9/17/2024	9/17/2024																																	
Turf Contract Substantial Completion	1/30/2026																																		

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	<p>The GMP package was submitted on July 30, 2024, for the BCC meeting scheduled on September 17, 2024. The building permit submission was completed in May 2024, and the pre-construction kick-off meeting took place on September 25, 2024. OAC meetings have not yet commenced, but the Notice to Proceed was issued on October 21, 2024.</p>
	A	B	C=B/A	D	
Design	\$1,213,709	\$188,934	15.57%	\$158,325	
Construction	\$2,830,047	\$3,334,691	117.83%	\$59,559	
<b>TOTAL</b>	<b>\$4,043,756</b>	<b>\$3,523,626</b>	<b>87.14%</b>	<b>\$217,884</b>	






Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> North County Pool Facility Repairs and Renovation</p> <p>Project Number: T176</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: Architecture Green</p> <p>Contractor: Messam</p> <p>Project Manager: Rich Carlton</p>	<p>Public aquatic facility overdue for large scale capital repair and renovation - renovations would include restroom/locker-room renovation, resurfacing and coping repairs, baby pool replacement with water feature and shade structures. We receive many public complaints about the structural design of and capital condition of the restrooms.</p> <p>FY2023 \$2,062,000.00 and FY2024 \$251,564.00</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Pre-scope walk through</td><td>5/23/2023</td><td>6/2/2023</td></tr><tr><td>Phase 1 Design Start: Pool Renovations</td><td>2/16/2024</td><td>2/16/2024</td></tr><tr><td>Phase 2 Design: Restrooms/Lockers</td><td>6/24/2024</td><td>7/31/2024</td></tr><tr><td>Permit</td><td>6/16/2025</td><td></td></tr><tr><td>Construction Start</td><td>10/28/2025</td><td></td></tr></tbody></table>		Original	Actual	Pre-scope walk through	5/23/2023	6/2/2023	Phase 1 Design Start: Pool Renovations	2/16/2024	2/16/2024	Phase 2 Design: Restrooms/Lockers	6/24/2024	7/31/2024	Permit	6/16/2025		Construction Start	10/28/2025		<p><b>Consultant</b></p> <p>SBE 100%</p> <p>Local 100%</p> <p>WBE 2%</p> <p>MBE 0%</p> <p><b>Contractor</b></p> <p>SBE 0%</p> <p>Local 100%</p> <p>WBE 36.3%</p> <p>MBE 0%</p>	 <p>Construction</p>  <p>IST</p> <p>0M 10M 20M 30M 40M 50M 60M 70M</p>
	Original	Actual																		
Pre-scope walk through	5/23/2023	6/2/2023																		
Phase 1 Design Start: Pool Renovations	2/16/2024	2/16/2024																		
Phase 2 Design: Restrooms/Lockers	6/24/2024	7/31/2024																		
Permit	6/16/2025																			
Construction Start	10/28/2025																			

FINANCIAL SUMMARY					NOTES
	Project Budget	Committed	% Committed	Paid To Date	
	A	B	C=B/A	D	
Construction	\$2,363,533	\$670,362	28.36%	\$353,168	
<b>TOTAL</b>	<b>\$2,363,533</b>	<b>\$670,362</b>	<b>28.36%</b>	<b>\$353,168</b>	<p>The 50% CD design Rough Order of Magnitude estimate has been received and incorporated into the overall projected project budget, which has been provided to the user. All unit and user design comments, including Fire Rescue have been received and are being incorporated into the 95% CD design, which is on track to be provided by the Architect of Record during second week of May . Construction Manager at Risk is in the process of confirming all permit submittal requirements with the Town of Jupiter. Additional funding will be required to fulfill total anticipated project costs.</p>




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Coconut Cove Waterpark Facility Repairs and Renovation</p> <p>Project Number: T177</p> <p>BCC District: 05</p> <p>Delivery Method: Annual Contract</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: TBD</p> <p>Contractor: TBD</p> <p>Project Manager: Eric Chimienti</p>	<p>Repairs and renovations include replacement of play structure in zero depth playground, restroom refurbishment, replace old leaking concession tiki hut with a concession building, classroom and birthday party room renovation, replace old chairs/deck lounge chairs. Upgrades are necessary to maintain business operations and no loss in revenue.</p> <p>IST Funded: FY2023\$1,449,000.00 and FY2024 \$176,778</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING						
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Design Start</td><td>10/15/2024</td><td></td></tr></tbody></table>		Original	Actual	Design Start	10/15/2024		<p><b>Consultant</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p> <p><b>Contractor</b></p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div><div></div><div>Construction</div></div> <div><div></div><div>IST</div></div> <p>Current Budget</p> <p>Fund Source</p>
	Original	Actual						
Design Start	10/15/2024							

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	The design proposal provided by Song & Associates is currently being reviewed by CID.				
	A	B	C=B/A	D					
Construction	\$1,625,778	\$3,291	0.20%	\$3,291					
TOTAL	\$1,625,778	\$3,291	0.20%	\$3,291					




Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 4/17/2025

Report Date: 4/30/2025

DESCRIPTION/TEAM	SCOPE	PHOTO
<p><b>Project Title:</b> Acreage Community Park Expansion</p> <p>Project Number: T203</p> <p>BCC District: 06</p> <p>Delivery Method: TBD</p> <p>Category: E02-Existing Park Redevelopment or Expansion</p> <p>Status: Design</p> <p>Designer: Cotleur &amp; Hearing</p> <p>Contractor: LandTek(LTG)</p> <p>Project Manager: ITID/Bob Hamilton</p>	<p>The project originally consisted of construction of a community/recreation center within Acreage Community Park . The project as now proposed consists of a synthetic turf multi-purpose field, state park, equestrian drop-off area and support infrastructure.</p> <p>IST FY23 \$3,000,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING												
<table><thead><tr><th></th><th>Original</th><th>Actual</th></tr></thead><tbody><tr><td>Project Start</td><td>10/21/2021</td><td>10/7/2024</td></tr><tr><td>Permit</td><td>1/30/2025</td><td>3/17/2025</td></tr><tr><td>Construction Start</td><td>8/4/2025</td><td></td></tr></tbody></table>		Original	Actual	Project Start	10/21/2021	10/7/2024	Permit	1/30/2025	3/17/2025	Construction Start	8/4/2025		<p><b>Consultant</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p><b>Contractor</b></p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<div><div></div><div>Construction</div><div>Current Budget</div></div> <div><div></div><div>IST</div><div>Fund Source</div></div>
	Original	Actual												
Project Start	10/21/2021	10/7/2024												
Permit	1/30/2025	3/17/2025												
Construction Start	8/4/2025													

FINANCIAL SUMMARY					NOTES				
	Project Budget	Committed	% Committed	Paid To Date	Permit # PR-2024-054280-0000 issued. Construction is scheduled to begin in August 2025.				
	A	B	C=B/A	D					
Design	\$0	\$0	0.00%	\$0					
Construction	\$3,000,000	\$0	0.00%	\$0					
Other	\$0	\$0	0.00%	\$0					
TOTAL	\$3,000,000	\$0	0.00%	\$0					
