

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Headquarters R&R

Project Number: 11206
 BCC District: 02
 Delivery Method: Construction Management
 Category: S06-Sheriff - FDO
 Status: Design
 Designer: Leo Daly
 Contractor: Kast Construction
 Project Manager: Terri Wolfe

The project consists of the exterior hardening of the entire building consisting of new exterior walls, impact resistant doors and windows, roof replacement and structural tie-ins as well as the R&R of all major building systems and interior renovation of approx. 75% of the building. As part of the project, the Board has also approved the temp. relocation of employees occupying approx. 70% of the space to ensure continuity of operations during the construction, reduce the overall duration of the project and therefore total project cost. This project is funded in:
 FY 2017 IST \$1,600,000
 FY 2019 IST \$11,047,000
 FY 2020 IST \$10,835,000
 FY 2021 IST \$17,620,000



SCHEDULE SUMMARY

	Original	Actual
Project Start	3/14/2016	3/14/2016
Design Start	5/9/2017	5/9/2017
Construction Start	1/31/2019	3/22/2021
Substantial Completion	1/31/2022	
Project Completion	2/28/2022	

PARTICIPATION


Consultant

SBE 24.71%
 Local 100%
 WBE N/A
 MBE N/A


Contractor

SBE 12.75%
 Local 100%
 WBE N/A
 MBE N/A

FUNDING

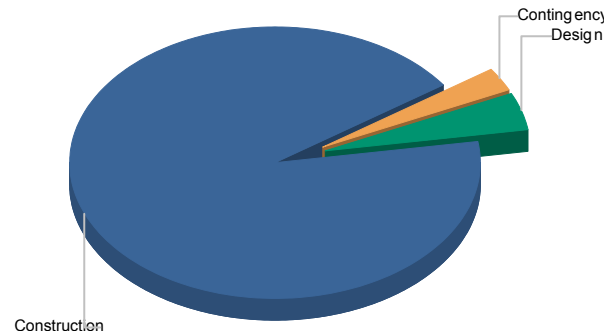

Current Budget

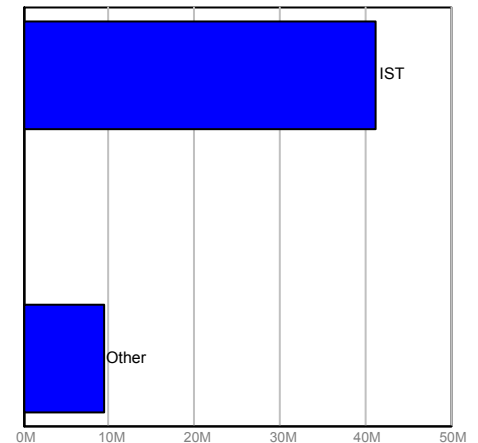

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,274,200	\$2,746,493	120.77%	\$2,235,429
Construction	\$46,915,796	\$35,314,514	75.27%	\$5,031,734
Furniture, Fixtures & Equipment	\$0	\$163,007	0.00%	\$162,841
Other	\$0	\$27,033	0.00%	\$27,033
Contingency	\$1,418,800	\$0	0.00%	\$0
TOTAL	\$50,608,796	\$38,251,046	75.58%	\$7,457,037

NOTES


West and South exterior walls are complete and have received their 1st coat of paint. Exterior window installation, stucco accessories and paint activities will continue through November 2021. Window glazing is on site in preparation for installation. East exterior wall demolition complete and block laying is underway. Roofing on the West-half is complete and cap is being installed. On the interior, Plumbing electrical and data rough-in are in motion in Phase 1. Ceiling and minor wall demo will continue in Phase 2 areas in preparation for upcoming abatement activities.


Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Ocean Inlet Park and Marina Renovation</p> <p>Project Number: 13367 BCC District: 04 Delivery Method: TBD Category: P08-Public Building Repair Replacement & Expans Status: Design Designer: Alan Gerwig & Associates, Inc. Contractor: TBD Project Manager: Rich Avery</p>	<p>The project consists of the replacement of marina components as well as new components including bulkhead wall, floating docks, floating finger docks, fixed dock, boat lifts, floating wave attenuator, landscaping, and replacement of the current Marina/Restroom and concession buildings. The project will be constructed in two phases. Phase one will consist of marina bulkhead, dock reconstruction and wave attenuator construction. The remaining scope to be completed during phase 2.</p> <p>Total available funding for this project consists of \$2,500,000 FY18 IST funds, \$2,500,000 FY20 Find Grant funds. Future funding consists of \$2,500,000 FY23 IST funds and shown as "Future Funding" within the current budget.</p>	

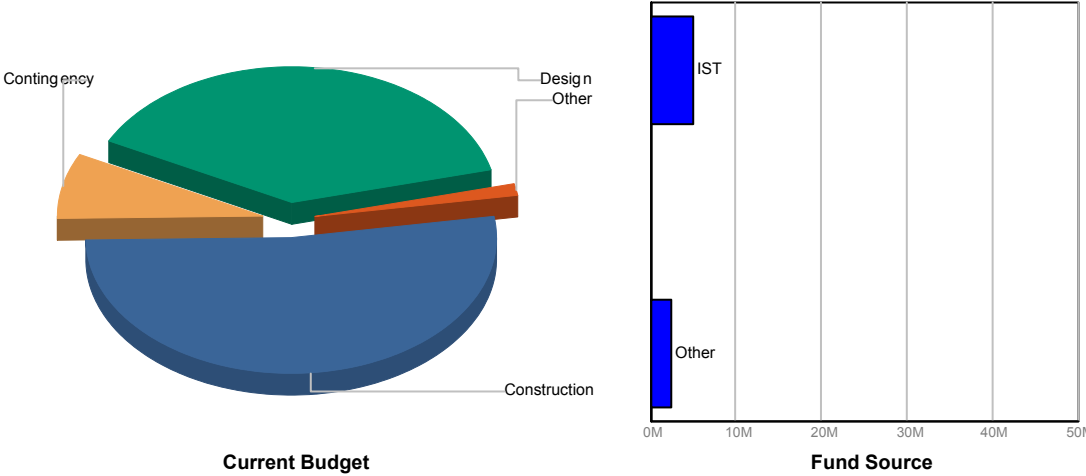SCHEDULE SUMMARY	PARTICIPATION	FUNDING															
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Phase I Start</td> <td>2/5/2018</td> <td>2/4/2018</td> </tr> <tr> <td>Design Start</td> <td>10/22/2018</td> <td>10/22/2018</td> </tr> <tr> <td>Construction Start</td> <td>12/3/2019</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>11/3/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Phase I Start	2/5/2018	2/4/2018	Design Start	10/22/2018	10/22/2018	Construction Start	12/3/2019		Substantial Completion	11/3/2020		<p>Consultant</p> <p>SBE 82.50% Local 100% WBE N/A MBE N/A</p> <p>Contractor</p> <p>SBE TBD Local TBD WBE TBD MBE TBD</p>	
	Original	Actual															
Phase I Start	2/5/2018	2/4/2018															
Design Start	10/22/2018	10/22/2018															
Construction Start	12/3/2019																
Substantial Completion	11/3/2020																

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,885,300	\$248,298	8.61%	\$248,298
Construction	\$3,906,200	\$0	0.00%	\$0
Other	\$108,500	\$94,843	87.41%	\$94,843
Contingency	\$600,000	\$0	0.00%	\$0
TOTAL	\$7,500,000	\$343,141	4.58%	\$343,141

NOTES

The Contract for Poseidon Dredge & Marine was approved by the BCC on Oct. 19, 2021. The NTP was issued with an effective date of Nov. 1, 2021. The preconstruction kickoff meeting was held on Nov. 2, 2021. The Contractor is scheduling a preconstruction meeting with the Town of Ocean Ridge for Nov. 10, 2021.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Evidence Building

Project Number: 14218
 BCC District: 02
 Delivery Method: Construction Management
 Category: S06-Sheriff - FDO
 Status: Design
 Designer: Leo Daly
 Contractor: Pirtle Construction
 Project Manager: Jeffrey Halverson

The project consists of a new 2-story Evidence Storage/Crime Scene/Crime Lab Facility (Approximately 87,000 GSF) and a 12,000 GSF metal building for impound vehicle storage. The main facility will house property seized by the Sheriff's Office, Administrative Offices, Evidence Processing via the crime scene investigation unit and the crime lab. Monitored cameras, motion detectors, and restricted access with electronic logging will be provided. The facility will accommodate secure vehicle garage bays that can store large vehicles (i.e. 56' long trailers) holding evidence for investigation or transport. Site Development (16 Acres) to include user parking (public, booking officers & staff), a fenced/gated impound lot (350 surface spaces) and a limited area of covered parking.



Palm Beach County Sheriff's Office Forensic Facility



SCHEDULE SUMMARY

	Original	Actual
Substantial Completion	11/5/2019	10/30/2020
Project Completion	11/26/2019	
Project Start	3/30/2016	12/21/2016
Design Start	6/28/2017	6/28/2017
Construction Start	7/5/2018	4/29/2019

PARTICIPATION


Consultant

SBE 33.21%
 Local 78.96%
 WBE N/A
 MBE N/A

Contractor

SBE 21.60%
 Local 55%
 WBE N/A
 MBE N/A

FUNDING

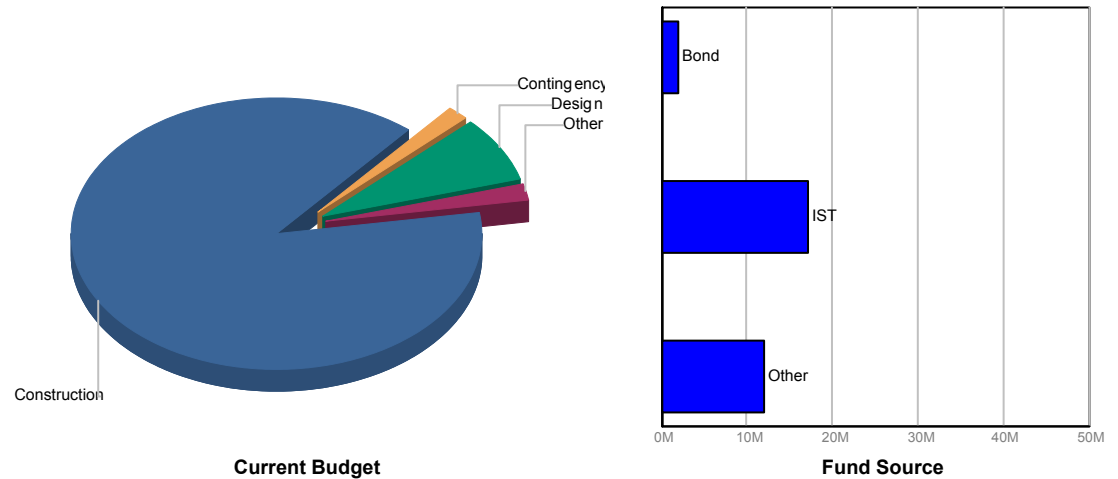

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,461,526	\$2,351,140	95.52%	\$1,968,032
Construction	\$27,680,589	\$28,241,436	102.03%	\$19,222,966
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$602,158	\$192,346	31.94%	\$192,346
Contingency	\$492,268	\$3,672	0.75%	\$3,672
TOTAL	\$31,236,542	\$30,788,595	98.57%	\$21,387,016

NOTES

Last change orders to resolve final items in process. Upon completion of these items, the contractor will apply for CO. Permit for reroute of generator exhaust in process. Closeout docs being reviewed. Some minor items to be resolved that the GC is working on to resolve by end of year so final Pay App can be processed. The funding sources for this project are as follows: Bond \$2M, Impact Fees \$6.7M, Ad Valorem \$1.2M, and IST \$21,336,540 for a total Project Budget of \$31,236,542.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: CR 880 Canal Bank Stabilization

Project Number: 1448
 BCC District: 06
 Delivery Method: Bid Contract Award
 Category: C02-CR 880 Canal Bank Stabilization
 Status: Construction
 Designer: Wantman Group
 Contractor: Dickerson Florida, Inc.
 Project Manager: Holly Knight

This project will repair, restore, and stabilize the embankment along a portion of County Road 880. The South Florida Water Management District's L-13 Canal parallels and is very close to County Road 880. The embankment area for County Road 880 to the canal is minimal. The undermining of the County Road 880 embankment continues due to storm events and increased South Florida Water Management District pumping and has progressively deteriorated. Repair of the embankment is necessary to prevent the eventual collapse of County Road 880 and to ensure the integrity of County Road 880 and provide a safe roadway for the public.
 IST Funds: FY17 \$1,000,000 FY18 \$2,000,000 FY24 \$2,000,000.



SCHEDULE SUMMARY

	Original	Actual
Construction Notice to Proceed	6/5/2017	6/5/2017
Phase III Construction Complete	11/2/2017	10/20/2017
Phase IV-Construction Complete	12/1/2018	3/27/2019
Phase IV-Construction Notice to Proceed	6/1/2018	7/9/2018
Phase V-Construction Notice to Proceed	6/1/2019	7/1/2019
Phase V-Construction Complete	12/1/2019	11/20/2019

PARTICIPATION

Consultant

SBE 15%

Local 100%

WBE 0%

MBE 0%

Contractor


SBE 23.4%

Local 23.4%

WBE 0%

MBE 0%

FUNDING

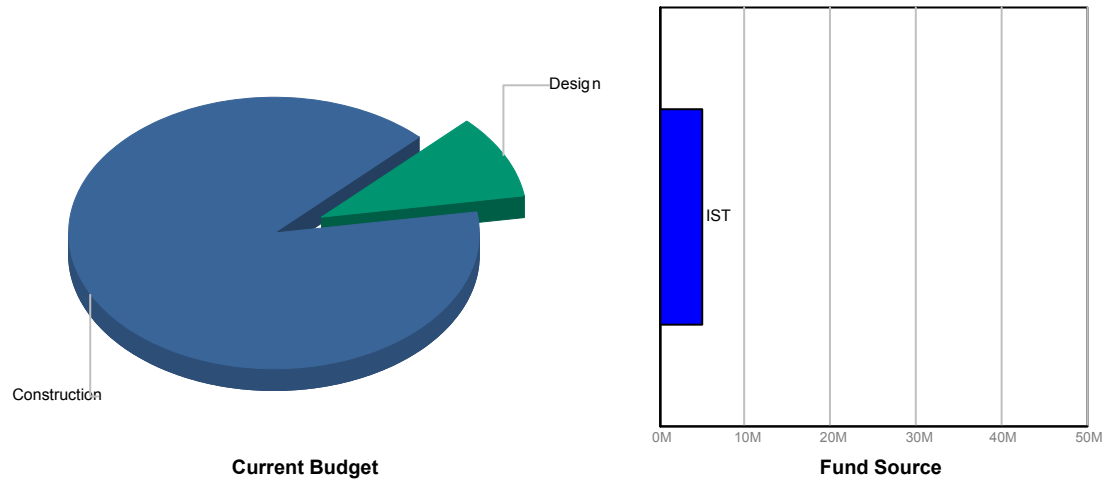

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$75,698	15.14%	\$75,698
Construction	\$4,500,000	\$2,537,336	56.39%	\$2,311,606
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$5,000,000	\$2,613,034	52.26%	\$2,387,304

NOTES

Phases I and II (constructing adjacent locations) were completed in FY 2015 and FY 2016 using non-IST funding. Phase III construction is funded at \$1,000,000 in FY 2017. Construction for Phases IV & V are funded at \$2,000,000 in FY 2018. Construction is complete for Phases III, IV and V. Project will recommence upon arrival of FY 2024 funding.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Main Detention Center Electronics

Project Number: 15218
 BCC District: 02
 Delivery Method: Construction Management
 Category: S06-Sheriff - FDO
 Status: Construction
 Designer: Leo A. Daly
 Contractor: Hedrick Brothers Construction
 Project Manager: Jeffrey Halverson

Phase II - Electronics for the South, East, and West Towers at the Main Detention Center, which have continually operated since the early 1980's. These systems include door controls, intercom, nurse's call system, CCTV, upgrade of EST3 software for fire alarm and new infrastructure for the future expansion of the CCTV system.
 Main Detention Center Electronics (B594) IST Funding
 FY 2017 IST \$5,600,000
 FY 2018 IST \$4,700,000
 The total Electronics budget is \$11,235,851 of which \$1,021,161 is funded through Ad Valorem.



SCHEDULE SUMMARY

	Original	Actual
Project Start	7/9/2015	6/9/2015
Design Start	6/21/2016	6/21/2016
Construction Start	3/19/2018	5/17/2018
Substantial Completion	3/15/2022	8/10/2020
Project Completion	6/30/2022	

PARTICIPATION


Consultant

SBE 22.60%
 Local 67%
 WBE N/A
 MBE N/A


Contractor

SBE 76.79%
 Local 80%
 WBE N/A
 MBE N/A

FUNDING

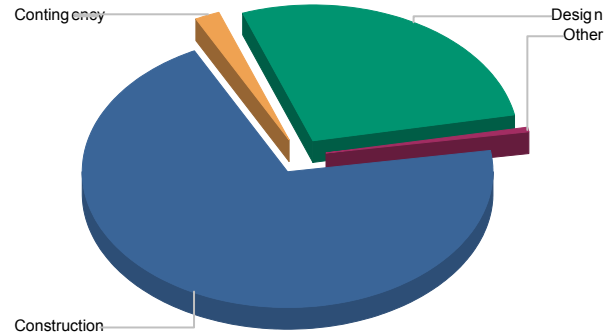

Current Budget

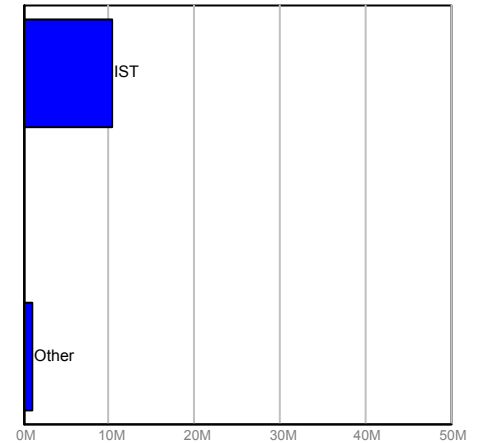

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$3,096,507	\$3,053,730	98.62%	\$2,855,440
Construction	\$7,868,421	\$7,204,857	91.57%	\$7,046,538
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$55,740	\$59,101	106.03%	\$59,101
Contingency	\$215,183	\$0	0.00%	\$0
TOTAL	\$11,235,851	\$10,317,688	91.83%	\$9,961,079

NOTES

No status change. We are processing a change order for approval for the credit we are to receive from the construction manager. This positive balance will be the subject of a future transfer.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Palm Beach Lakes Blvd over FEC R/R

This project will rehabilitate an existing bridge that was built over 50 years ago. The project will improve traffic safety (lane widths, pedestrian barrier, railings) and may involve other improvements such as shoulders, bike lanes, and sidewalks.



Project Number: 1532
 BCC District: 07
 Delivery Method: Design CCNA
 Category: B04-Bridge Modifications
 Status: Design
 Designer: HNTB
 Contractor: TBD
 Project Manager: Kathleen Farrell


SCHEDULE SUMMARY

	Original	Actual
Project Start	9/30/2017	9/30/2017
Consultant Procurement Finish	9/3/2019	12/1/2019
Study Start	4/7/2020	4/7/2020
Design Complete	6/1/2024	
Permit Application	2/1/2023	
Permit Issued	1/1/2024	
Construction Start	4/1/2025	
Construction Complete	4/1/2027	
Study Complete	11/11/2021	
Design Start	2/1/2022	

PARTICIPATION

Consultant	
SBE	36.5%
Local	96%
WBE	TBD
MBE	TBD
Contractor	
SBE	TBD
Local	TBD
WBE	TBD
MBE	TBD

FUNDING

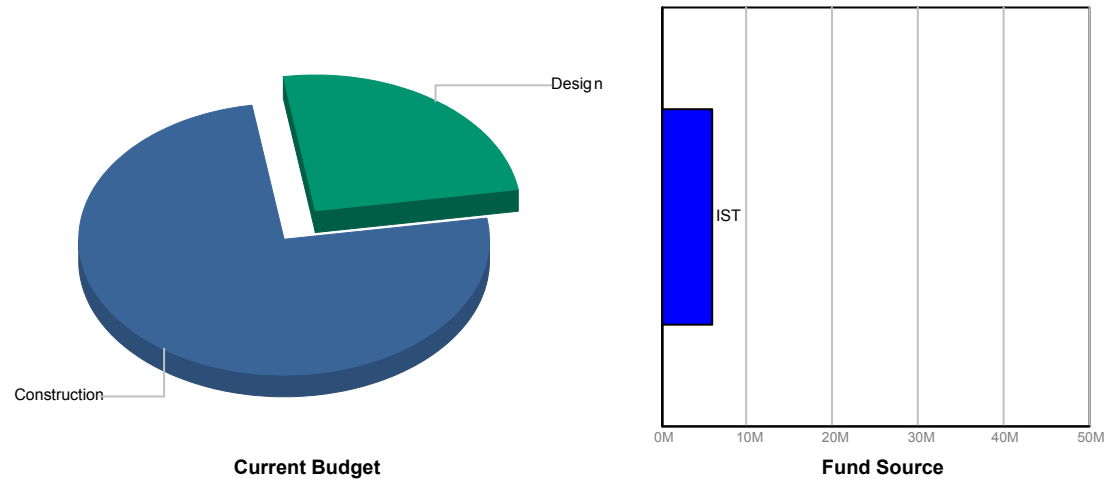

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$360,375	24.02%	\$279,586
Construction	\$4,500,000	\$603	0.01%	\$603
Other	\$0	\$15,327	0.00%	\$15,327
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$6,000,000	\$376,305	6.27%	\$295,517

NOTES


The project is in the coordination stage with stakeholders including the City of West Palm Beach and the Community Redevelopment Agency to determine scope and design parameters for the rehabilitation of the bridge superstructure. This project is funded for design in FY 2017. Construction is currently included in the plan for FY 2021. The first phase of design (Study & Stakeholder Coordination) started on 4/7/2020.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Sections of Jog Road</p> <p>Project Number: 1537</p> <p>BCC District: Multiple</p> <p>Delivery Method: Annual Striping Contract</p> <p>Category: S16-Striping</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Oglesby</p> <p>Project Manager: Larry Kelly</p>	<p>This project consists of restriping sections of Jog Road.</p> <p>FY 2017 \$350,000</p> <p>FY 2021 \$150,000</p> <p>FY 2022 \$100,000</p> <p>FY 2023 \$100,000</p> <p>FY 2024 \$200,000</p> <p>FY 2026 \$200,000</p>	

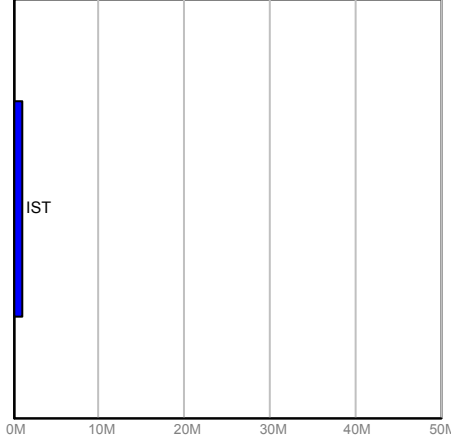SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>10th Avenue N. to Summit Complete</td> <td>1/22/2018</td> <td>1/22/2018</td> </tr> <tr> <td>Summit to Gun Club Complete</td> <td>9/20/2017</td> <td>9/20/2017</td> </tr> <tr> <td>PGA to Hood Complete</td> <td>10/31/2017</td> <td>10/31/2017</td> </tr> <tr> <td>Wallis to Roebuck Complete</td> <td>3/7/2018</td> <td>3/7/2018</td> </tr> <tr> <td>Glades to NW 55th St.</td> <td>3/19/2019</td> <td>3/19/2019</td> </tr> <tr> <td>Gateway to S. of Hypoluxo Complete</td> <td>12/17/2018</td> <td>10/18/2018</td> </tr> <tr> <td>Hood to Donald Ross</td> <td>12/2/2020</td> <td>12/12/2020</td> </tr> <tr> <td>N. Oriole to Lake Ida</td> <td>4/3/2021</td> <td>3/9/2021</td> </tr> </tbody> </table>		Original	Actual	10th Avenue N. to Summit Complete	1/22/2018	1/22/2018	Summit to Gun Club Complete	9/20/2017	9/20/2017	PGA to Hood Complete	10/31/2017	10/31/2017	Wallis to Roebuck Complete	3/7/2018	3/7/2018	Glades to NW 55th St.	3/19/2019	3/19/2019	Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018	Hood to Donald Ross	12/2/2020	12/12/2020	N. Oriole to Lake Ida	4/3/2021	3/9/2021	<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p>Contractor</p> <p>SBE 61%</p> <p>Local 61%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="text-align: center;">  <p>Construction</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>IST</p> <p>Fund Source</p> </div>
	Original	Actual																											
10th Avenue N. to Summit Complete	1/22/2018	1/22/2018																											
Summit to Gun Club Complete	9/20/2017	9/20/2017																											
PGA to Hood Complete	10/31/2017	10/31/2017																											
Wallis to Roebuck Complete	3/7/2018	3/7/2018																											
Glades to NW 55th St.	3/19/2019	3/19/2019																											
Gateway to S. of Hypoluxo Complete	12/17/2018	10/18/2018																											
Hood to Donald Ross	12/2/2020	12/12/2020																											
N. Oriole to Lake Ida	4/3/2021	3/9/2021																											

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$0	0.00%	\$0
Construction	\$1,100,000	\$367,529	33.41%	\$367,529
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$1,100,000	\$367,529	33.41%	\$367,529

NOTES

Jog Road is a North-South major County thoroughfare. This project consists of re-striping sections of Jog Road. Restriping continues on an as needed basis.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: CR 880

Resurfacing approximately 2 miles (4 lane miles) of a portion of County Road 880 from Main Street to S.R. 80 each year.



Project Number: 1539
 BCC District: 06
 Delivery Method: Annual Construction Contract
 Category: R04-Resurfacing
 Status: Construction
 Designer: N/A
 Contractor: Community
 Project Manager: Mark Kroeger

SCHEDULE SUMMARY

	Original	Actual
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/7/2018	11/30/2018
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2020 Construction Complete	12/18/2020	12/3/2020
FY 2021 Construction Complete	12/17/2021	10/5/2021
FY 2022 Construction Complete	12/16/2022	

PARTICIPATION


Consultant

SBE N/A
 Local N/A
 WBE N/A
 MBE N/A

Contractor

SBE 8.7%
 Local 95.8%
 WBE 0%
 MBE 0%

FUNDING

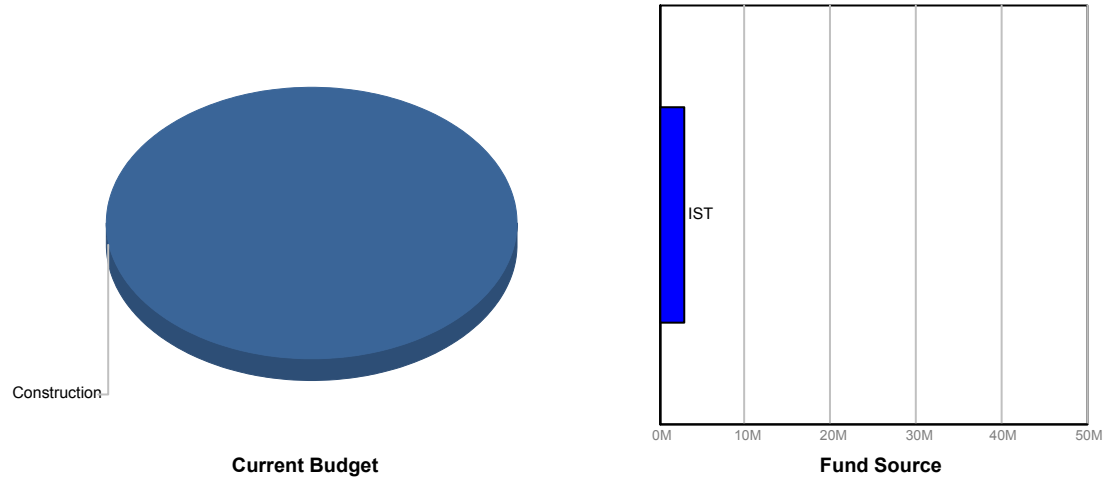

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$2,224	0.00%	\$2,224
Construction	\$3,000,000	\$1,179,188	39.31%	\$1,154,188
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$3,000,000	\$1,181,411	39.38%	\$1,156,412

NOTES

County Road 880 is approximately 19 miles in length. This project entails resurfacing a portion (\$300,000) of County Road 880 each year. Construction complete for FY2017 thru 2021.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Brown's Farms Road

Resurfacing approximately 2 miles (4 lane miles) of a portion of Brown's Farm Road from CR 880 to South Terminus each year.

Project Number: 1540
 BCC District: 06
 Delivery Method: Annual Construction Contract
 Category: R04-Resurfacing
 Status: Construction
 Designer: N/A
 Contractor: Community
 Project Manager: Mark Kroeger



SCHEDULE SUMMARY

PARTICIPATION

FUNDING


	Original	Actual
FY2021 Construction Complete	12/17/2021	
FY 2020 Construction Complete	12/18/2020	12/2/2020
FY 2019 Construction Complete	12/31/2019	11/1/2019
FY 2017 Construction Complete	12/22/2017	12/22/2017
FY 2018 Construction Complete	12/1/2018	11/30/2018

Consultant

SBE N/A
 Local N/A
 WBE N/A
 MBE N/A

Contractor

SBE 7.4%
 Local 94.4%
 WBE 0%
 MBE 0%

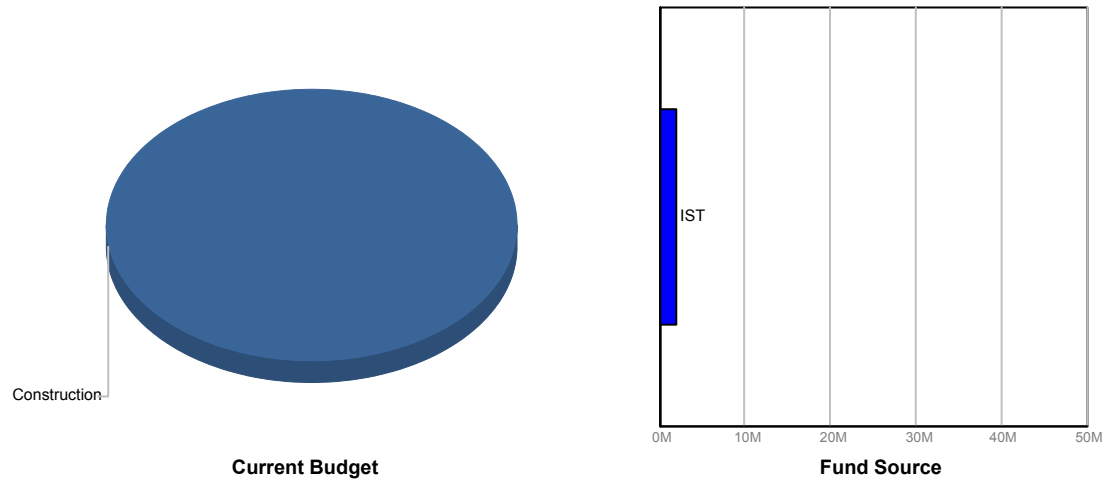

FINANCIAL SUMMARY

NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$1,551	0.00%	\$1,551
Construction	\$2,000,000	\$995,507	49.78%	\$926,752
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$2,000,000	\$997,058	49.85%	\$928,303

Brown's Farm Road is approximately 14 miles in length. This project entails resurfacing a portion (\$200,000) of Brown's Farm Road each year. Construction complete for FY2017 thru 2020.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Prosperity Farms Rd. over SFWMD C-17 Canal (934116)
Project Number: 1555
BCC District: 01
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Design
Designer: Scalar
Contractor: TBD - (bid)
Project Manager: David Young

This project will replace an existing bridge that was built over 60 years ago. The new bridge will improve traffic safety (lane widths, bike lanes, parapets), improve roadway drainage, and enhance pedestrian sidewalk safety. Note the current bridge is weight restricted.



SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/19/2019	11/19/2019
Design Completion	2/1/2022	
Construction Bid Date	6/1/2022	
Construction Start	10/1/2022	
Construction Complete	10/1/2024	

PARTICIPATION



Consultant

SBE 98%
 Local 100%
 WBE 0%
 MBE 0%

Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

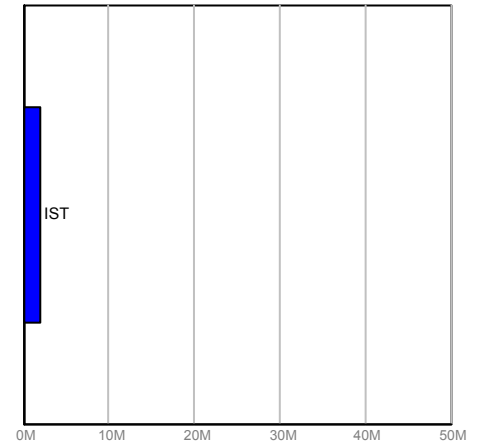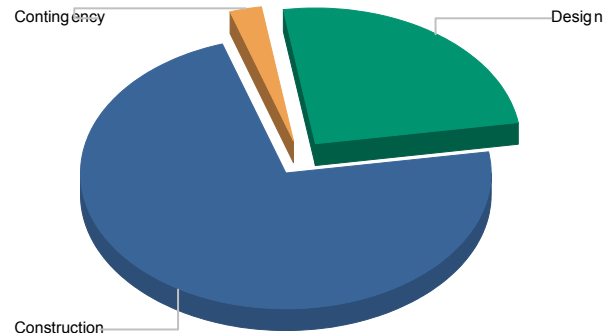

Current Budget

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$482,738	96.55%	\$190,364
Construction	\$1,450,000	\$5,003	0.35%	\$5,003
Contingency	\$50,000	\$8,365	16.73%	\$8,365
TOTAL	\$2,000,000	\$496,106	24.81%	\$203,732

NOTES

This project is under design. Construction is funded in the plan for FY 2021.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Belvedere Rd over E-3 canal (934205 & 934206)
Project Number: 1556
BCC District: 02
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Design
Designer: Stantec
Contractor: TBD (bid)
Project Manager: Kathleen Farrell

This project will replace the existing bridges that were built over 40 years ago. The new bridge(s) will improve traffic safety (lane widths, bike lanes, parapets), update the guardrail system, improve roadway drainage, restore the slope protection, and enhance pedestrian sidewalk safety.



SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	10/22/2019	10/22/2019
Design Completion	12/1/2021	
Construction Bid Date	3/1/2022	
Construction Start	8/1/2022	
Construction Complete	3/1/2024	

PARTICIPATION


Consultant

SBE 30%
 Local 100%
 WBE 0%
 MBE 0%


Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

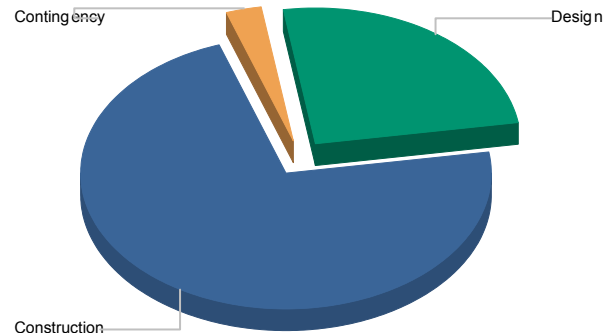

Current Budget

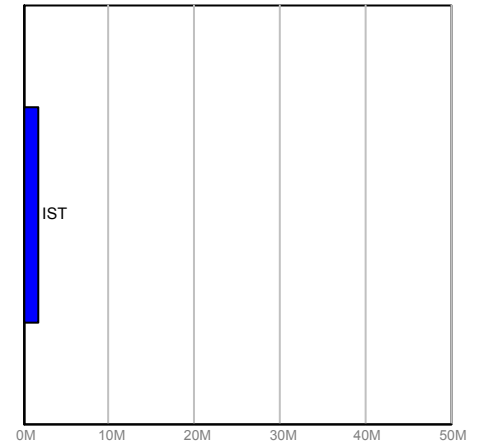

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$450,000	\$360,034	80.01%	\$237,412
Construction	\$1,300,000	\$4,612	0.35%	\$4,612
Contingency	\$50,000	\$0	0.00%	\$0
TOTAL	\$1,800,000	\$364,647	20.26%	\$242,025

NOTES

This project is under design. Construction is funded in the plan for FY 2021.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Various other locations Countywide

Project Number: 1558
 BCC District: Multiple
 Delivery Method: Annual Construction Contract
 Category: D02-Drainage (Pipe Replacements)
 Status: Construction
 Designer: N/A
 Contractor: Hinterland
 Project Manager: Mark Kroeger

This project will repair and/or replace existing pipe culverts and drainage structures along various roads and canals Countywide. These repairs are needed in order to properly drain and maintain the various roads and canals in a safe operating condition.



SCHEDULE SUMMARY

PARTICIPATION

FUNDING


	Original	Actual
Jupiter Farms (133rd Rd. & 156th St.)	8/1/2018	3/12/2018
1069 Edgehill Road	8/15/2018	6/12/2018
Limestone Creek & Palm Garden St.	8/1/2018	7/17/2018
3261 Atlantic Road	8/15/2018	7/1/2018
Van Buren Road @ E-3 Canal	8/1/2018	6/15/2018
Jupiter Farms (4 locates)	10/15/2018	8/21/2018
6361 Wood Lake Rd./19650 Red Maple F	10/1/2018	10/1/2018
19598 Trails End Terrace	9/15/2018	8/20/2018
19582 Trails End Terrace	9/1/2018	9/1/2018
6558 Wood Lake Road	9/15/2018	9/14/2018
6126 Wood Lake Road	10/15/2018	12/12/2018
6528 Wood Lake Road	11/1/2018	12/12/2018
Whispering Trail Community	6/1/2019	7/9/2019

Consultant

SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A

Contractor

SBE	100%
Local	100%
WBE	0%
MBE	0%

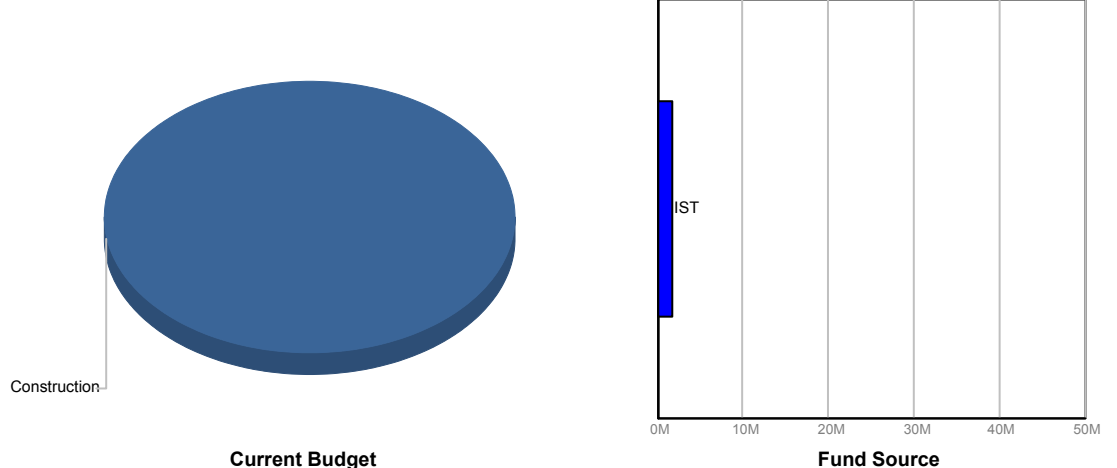

FINANCIAL SUMMARY

NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$619,373	36.43%	\$619,373
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$1,700,000	\$619,373	36.43%	\$619,373

This project is funded in:
 FY 2018 \$500,000, FY 2021 \$500,000, FY 2022 \$200,000
 FY 2023 \$200,000, FY 2024 \$200,000, FY 2025 \$100,000

The total project is estimated at \$1,700,000.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Video Detection (80 +/- intersection)

This project will replace the traffic detection at numerous signalized intersections from the existing inductive loop system to video detection. The video detection system is more reliable and easier to maintain.



Project Number: 1580
 BCC District: Multiple
 Delivery Method: Annual Traffic Signals Contract
 Category: S08-Signals and Signal Systems
 Status: Construction
 Designer: N/A
 Contractor: Gerelco
 Project Manager: Fattoush Jafar

SCHEDULE SUMMARY

	Original	Actual
Woolbright & Hagen Ranch	11/1/2018	4/4/2019
Belvedere & Country Club Road	12/1/2018	4/4/2019
Palm Beach Lakes & Wellesley	1/1/2019	4/4/2019
Military Tr. & Garden Lake	8/1/2018	11/21/2018
Gateway & Renaissance Commons	9/1/2018	4/3/2019
Australian & Turnage	10/1/2018	1/7/2019

PARTICIPATION


Consultant

SBE N/A
 Local N/A
 WBE N/A
 MBE N/A

Contractor

SBE 0%
 Local 23%
 WBE 0%
 MBE 0%

FUNDING

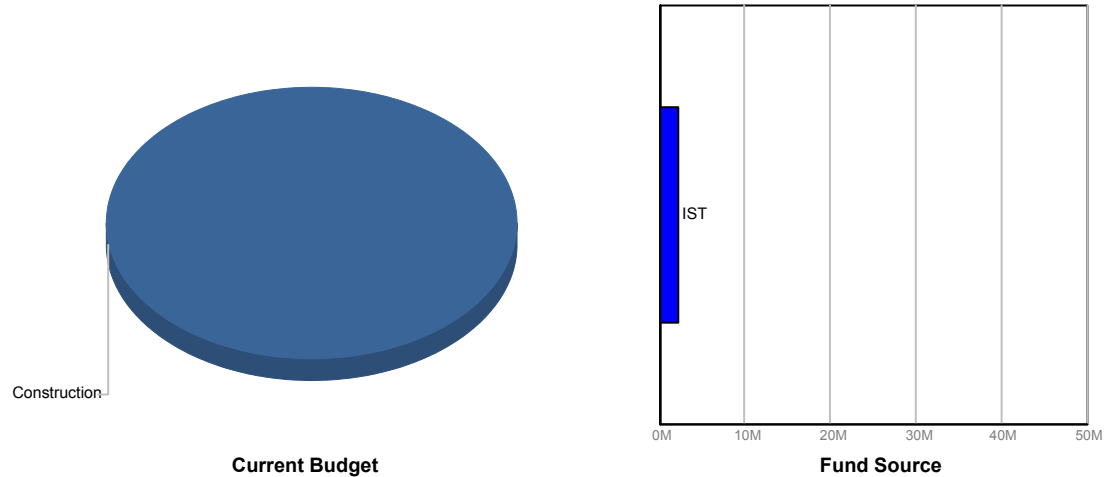

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,200,000	\$199,000	9.05%	\$199,000
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$2,200,000	\$199,000	9.05%	\$199,000

NOTES


Work has been completed at six intersections. This project is funded in:
 FY 2018 \$200,000
 FY 2023 \$300,000
 FY 2024 \$800,000
 FY 2026 \$900,000
 The total project is estimated at \$2,200,000.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: FY 2018 Street Lighting LED Replacements - Countywide</p> <p>Project Number: 1581</p> <p>BCC District: CW</p> <p>Delivery Method: Florida Power and Light</p> <p>Category: S14-Street Lighting</p> <p>Status: Construction</p> <p>Designer: Florida Power and Light</p> <p>Contractor: Florida Power and Light</p> <p>Project Manager: May Cheng</p>	<p>These projects will replace the high pressure sodium street lights with LED lights. Many of the street lights along County roads are owned and maintained by Florida Power and Light (FPL) with the County paying all the operation and maintenance costs (including power). FPL will be responsible for the final design and installation to convert the street lighting to the newer LED technology, and the County will reimburse FPL all applicable conversion costs. The result will provide a cost savings, better quality illumination, and a more desirable environmental light source.</p>	

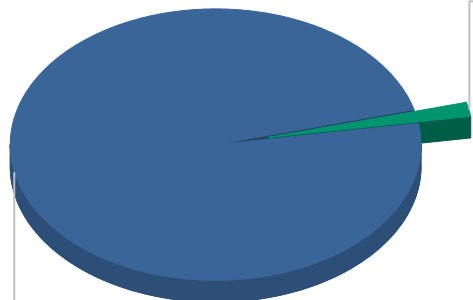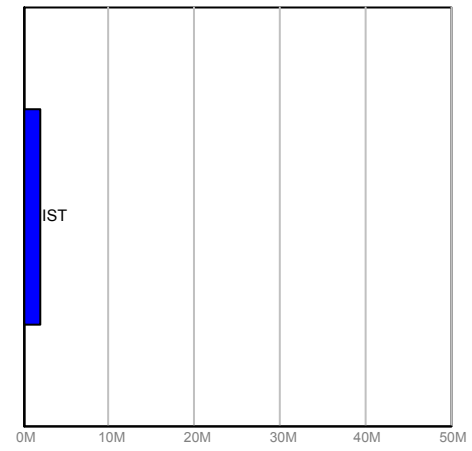SCHEDULE SUMMARY	PARTICIPATION	FUNDING																																										
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr><td>Gun Club Road/Bosque to Congress</td><td>8/16/2019</td><td>8/16/2019</td></tr> <tr><td>Congress/Okeechobee to Belvedere</td><td>8/16/2019</td><td>8/16/2019</td></tr> <tr><td>10th Avenue North/Haverhill to Kirk</td><td>12/11/2019</td><td>12/11/2019</td></tr> <tr><td>Community/Haverhill to Military</td><td>8/16/2019</td><td>8/16/2019</td></tr> <tr><td>Haverhill Road/WPB City to Haverhill City</td><td></td><td></td></tr> <tr><td>Glades Road/State Road 7 to Boca Rio</td><td></td><td></td></tr> <tr><td>Boynton Beach Boulevard/Turnpike to Kn</td><td></td><td></td></tr> <tr><td>Jog Road/Belvedere to State Road 80</td><td></td><td></td></tr> <tr><td>Forest Hill/Turnpike to Pinehurst & Jog to</td><td></td><td></td></tr> <tr><td>Haverhill/State Road 80 to Lake Worth</td><td></td><td></td></tr> <tr><td>Congress/Lantana to Hypoluxo & Gun Cl</td><td></td><td></td></tr> <tr><td>Gateway/Military to Windward</td><td></td><td></td></tr> <tr><td>Belvedere Road/RPB City to Haverhill Cit</td><td></td><td></td></tr> </tbody> </table>		Original	Actual	Gun Club Road/Bosque to Congress	8/16/2019	8/16/2019	Congress/Okeechobee to Belvedere	8/16/2019	8/16/2019	10th Avenue North/Haverhill to Kirk	12/11/2019	12/11/2019	Community/Haverhill to Military	8/16/2019	8/16/2019	Haverhill Road/WPB City to Haverhill City			Glades Road/State Road 7 to Boca Rio			Boynton Beach Boulevard/Turnpike to Kn			Jog Road/Belvedere to State Road 80			Forest Hill/Turnpike to Pinehurst & Jog to			Haverhill/State Road 80 to Lake Worth			Congress/Lantana to Hypoluxo & Gun Cl			Gateway/Military to Windward			Belvedere Road/RPB City to Haverhill Cit			<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p>Contractor</p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Design</p> <p>Construction</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>IST</p> <p>Fund Source</p> </div> </div>
	Original	Actual																																										
Gun Club Road/Bosque to Congress	8/16/2019	8/16/2019																																										
Congress/Okeechobee to Belvedere	8/16/2019	8/16/2019																																										
10th Avenue North/Haverhill to Kirk	12/11/2019	12/11/2019																																										
Community/Haverhill to Military	8/16/2019	8/16/2019																																										
Haverhill Road/WPB City to Haverhill City																																												
Glades Road/State Road 7 to Boca Rio																																												
Boynton Beach Boulevard/Turnpike to Kn																																												
Jog Road/Belvedere to State Road 80																																												
Forest Hill/Turnpike to Pinehurst & Jog to																																												
Haverhill/State Road 80 to Lake Worth																																												
Congress/Lantana to Hypoluxo & Gun Cl																																												
Gateway/Military to Windward																																												
Belvedere Road/RPB City to Haverhill Cit																																												

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$30,000	\$25,977	86.59%	\$25,977
Construction	\$1,920,000	\$1,063,409	55.39%	\$546,699
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$1,950,000	\$1,089,386	55.87%	\$572,676

NOTES

There are 16 street lighting projects (road segments) funded (\$1,950,000) for conversion in FY 2018. All 16 projects have been forwarded to FPL requesting final design and installation. As of 12/1/20, five projects have been completed, and the street lighting along a portion of the Hypoluxo Road project has also been converted.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: CR 880 (Old SR 80) Over C-51 Canal (930940)
Project Number: 1612
BCC District: 06
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Design
Designer: Alan Gerwig & Assoc.
Contractor: TBD (Bid)
Project Manager: Kathleen Farrell

This project will replace an existing bridge that was built over 80 years ago. The new bridge will improve traffic safety (lane widths and vehicle barrier walls). The current bridge is weight restricted.



SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	11/9/2018	11/9/2018
Design Completion	12/18/2021	
Construction Bid Date	4/1/2022	
Construction Start	9/1/2022	
Construction Complete	3/1/2024	

PARTICIPATION


Consultant

SBE 94.3%
 Local 100%
 WBE 0%
 MBE 0%

Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

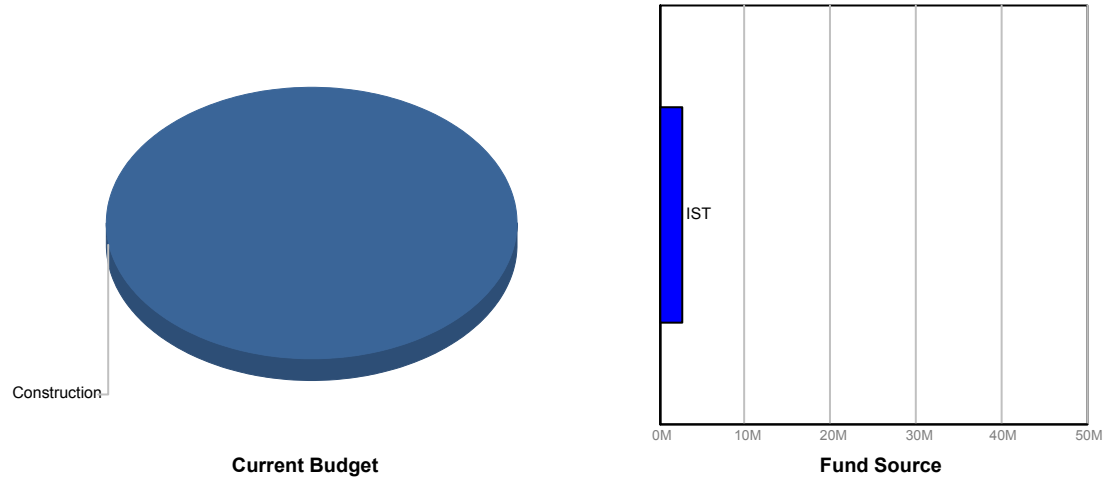

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,700,000	\$0	0.00%	\$0
TOTAL	\$2,700,000	\$0	0.00%	\$0

NOTES

This project is funded with 5-Year Road Program (RP) funding and IST funding. The project is under design (using 5-Year RP funds). The construction of the project is currently estimated at \$3.5m. The IST partially funds the construction of the project at \$2.7 m in FY 2019. The project is currently scheduled to begin construction in FY22.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Courthouse Electronics System R&R/Command Center
Project Number: 16208
BCC District: 07
Delivery Method: Construction Management
Category: J02-Judicial
Status: Construction
Designer: TLC Engineering
Contractor: Hedrick Brothers Construction Co., Inc.
Project Manager: Rich Avery

Security Systems replacement at the Main County Courthouse including the Security Management System, Access Control System, CCTV system, Duress System, Intercom, Elevator Override, and Fire Alarm. The Project will also include addressing the emergency egress procedures for the facility, as well as build-out for the expansion of the 4th floor Command Center.

Total IST, and Ad Valorem funding for this project is \$16,449,545; Total IST funds are \$12,999,700, which are comprised of FY17 IST funds of \$1,300,000 and FY18 IST funds of \$8,699,700 and FY 19 IST funds of \$3,000,000. Ad Valorem funds are \$3,449,845



SCHEDULE SUMMARY

	Original	Actual
Project Start	2/19/2016	2/19/2016
Design Start	2/15/2017	2/15/2017
Construction - Start	11/26/2018	1/7/2019
Substantial Completion	2/1/2021	
Project Completion	4/1/2021	

PARTICIPATION


Consultant

- SBE 13.4%
- Local 100%
- WBE N/A
- MBE N/A

Contractor

- SBE 25%
- Local 100%
- WBE N/A
- MBE N/A

FUNDING

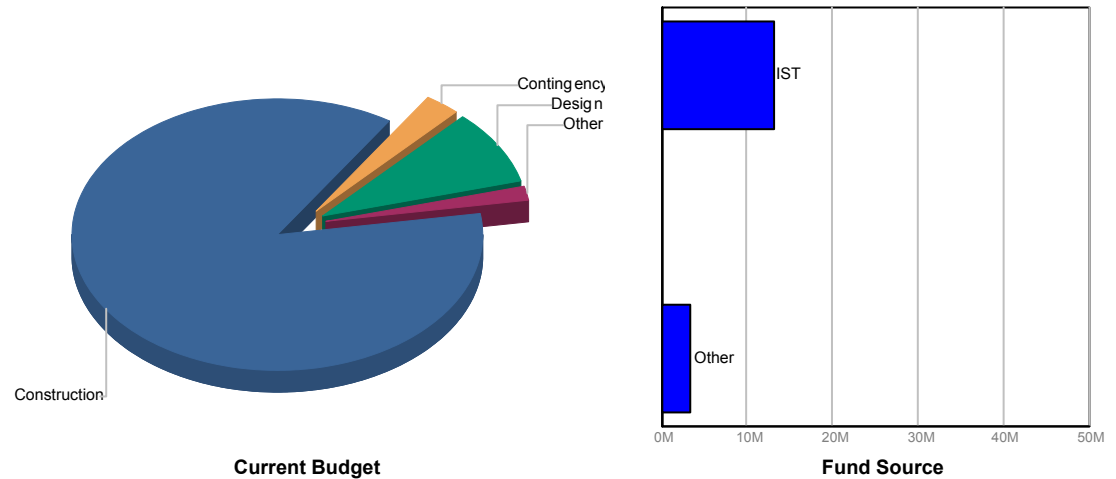

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,456,336	\$1,367,426	93.89%	\$436,761
Construction	\$14,307,700	\$14,284,827	99.84%	\$12,779,452
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$285,137	\$116,320	40.79%	\$116,320
Contingency	\$465,300	\$0	0.00%	\$0
TOTAL	\$16,514,473	\$15,768,574	95.48%	\$13,332,534

NOTES

The CO for the CEP work has been submitted for approval, also pending will be additional wiring and programming required for proper door alarming that was not originally included, has been deemed as essential for security purposes.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: 6th Ave. So. over Lake Osborne (LWDD E-4 Canal)(S Br/ East bound) (934307)
Project Number: 1634
BCC District: 03
Delivery Method: Design CCNA
Category: B08-Bridge Replacements
Status: Construction
Designer: Stantec
Contractor: Ranger
Project Manager: David Young

This project will replace an existing bridge that was built over 50 years ago. The new bridge will improve traffic safety (lane widths, bike lanes and barrier walls), improve roadway drainage, and enhance pedestrian sidewalk safety. The new bridge will also provide greater vertical clearance.



SCHEDULE SUMMARY

	Original	Actual
Design Contract Notice to Proceed	7/17/2018	7/17/2018
Design Completion	12/1/2020	2/14/2021
Construction Bid Date	3/1/2021	5/4/2021
Construction Start	12/1/2021	
Construction Complete	6/1/2023	

PARTICIPATION


Consultant

SBE 25%
 Local 100%
 WBE 0%
 MBE 0%

Contractor

SBE TBD
 Local TBD
 WBE 0%
 MBE 0%

FUNDING

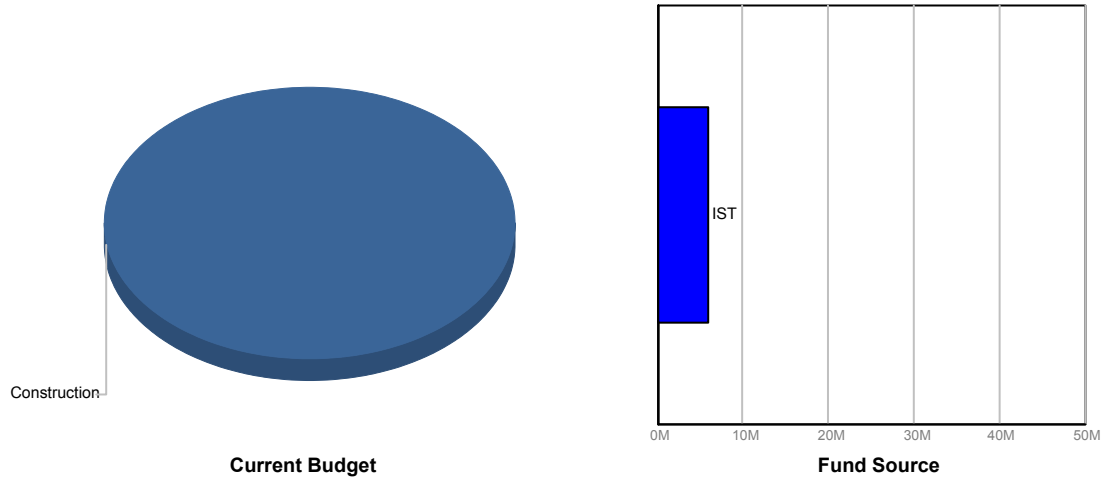

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$0	0.00%	\$0
TOTAL	\$6,000,000	\$0	0.00%	\$0

NOTES


This project is funded with 5-Year Road Program (RP) funding and IST funding. Design (using RP funds) is complete. The project was bid on 5/4/21 - with apparent low bid of \$ 11.1m The IST partially funds the construction of the project at \$6m in FY 2020. Notice to proceed with construction expected in early 2022.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Australian Ave. from Banyan St. to 45th St.</p> <p>Project Number: 1658</p> <p>BCC District: BIAF</p> <p>Delivery Method: Design CCNA</p> <p>Category: D04-Drainage Improvements</p> <p>Status: Design</p> <p>Designer: TBD</p> <p>Contractor: TBD (Bid)</p> <p>Project Manager: Kathleen Farrell</p>	<p>The project will include drainage improvements (piped drainage system) and a new paving surface for a 4-lane divided section with new pathways on both sides along Australian Avenue from Banyan Blvd. to 45th Street.</p>	

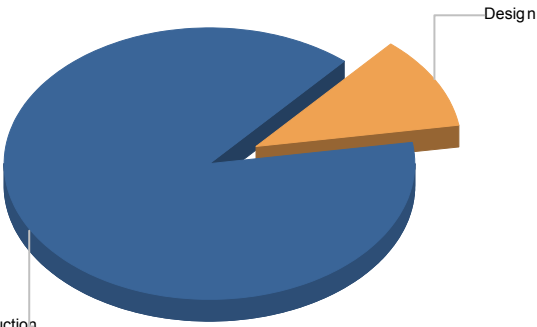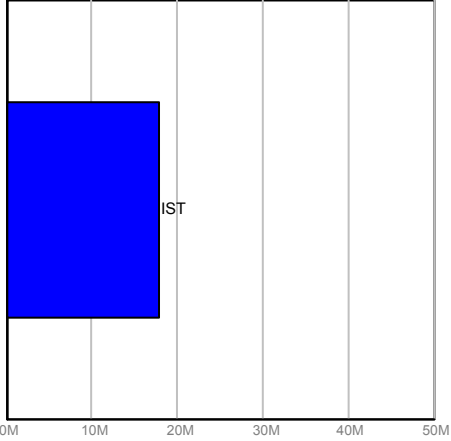SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Design Start</td> <td>3/1/2022</td> <td></td> </tr> <tr> <td>Design Complete</td> <td>9/1/2025</td> <td></td> </tr> <tr> <td>Construction Bid Date</td> <td>12/1/2025</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>4/1/2026</td> <td></td> </tr> <tr> <td>Construction Complete</td> <td>4/1/2028</td> <td></td> </tr> </tbody> </table>		Original	Actual	Design Start	3/1/2022		Design Complete	9/1/2025		Construction Bid Date	12/1/2025		Construction Start	4/1/2026		Construction Complete	4/1/2028		<p>Consultant</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
	Original	Actual																		
Design Start	3/1/2022																			
Design Complete	9/1/2025																			
Construction Bid Date	12/1/2025																			
Construction Start	4/1/2026																			
Construction Complete	4/1/2028																			

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,000,000	\$8,599	0.43%	\$8,599
Construction	\$15,800,000	\$2,227	0.01%	\$2,227
TOTAL	\$17,800,000	\$10,826	0.06%	\$10,826

NOTES

The project is in the Consultant Selection process. Scope and fee negotiation will follow culminating in a design contract. The project is funded for design (\$2m) in FY21 and for construction (\$15.8m) in FY24 and FY25.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Belvedere Rd canal piping & sidewalk addition (62nd Dr. N. to Haverhill park)
Project Number: 1661
BCC District: 02
Delivery Method: Design CCNA
Category: P04-Pathways
Status: Design
Designer: Keshavarz
Contractor: TBD (Bid)
Project Manager: Kathleen Farrell

This project will add a new sidewalk (SW) on the south side of Belvedere Road from 62nd Dr. N. to the Haverhill park (just east of the E-3 Canal) - connecting to the existing south SW at the park's frontage. The SW may require the piping of Lake Worth Drainage District's (LWDD) L-3 Canal.



SCHEDULE SUMMARY

	Original	Actual
Study Complete	2/1/2022	
Design Complete		
Construction Bid Date		
Construction Start		
Construction Complete		

PARTICIPATION


Consultant

SBE 50%
 Local 100%
 WBE 0%
 MBE 0%

Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

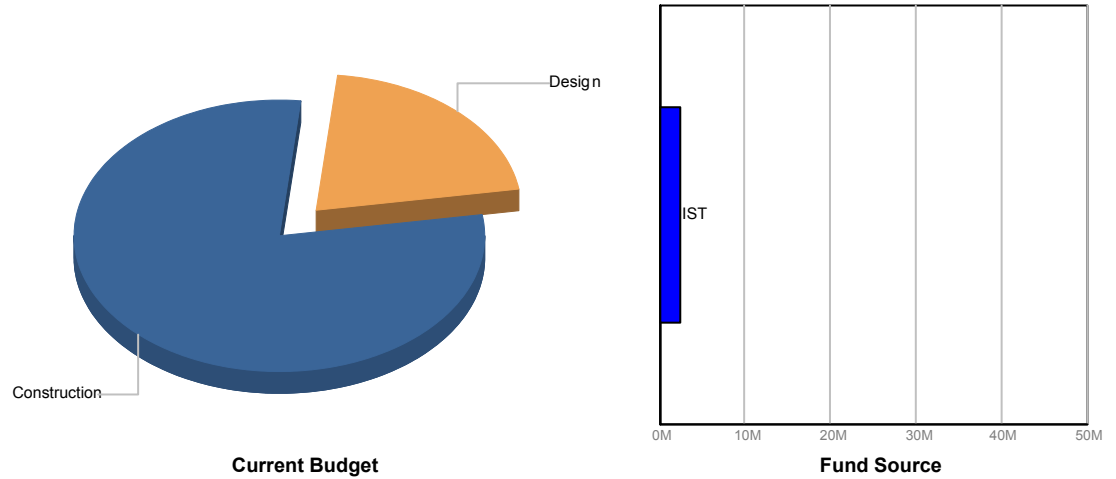

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$500,000	\$605	0.12%	\$605
Construction	\$1,900,000	\$0	0.00%	\$0
TOTAL	\$2,400,000	\$605	0.03%	\$605

NOTES


The project is in the study phase to determine a more precise work scope. The project is funded for design (\$500k) in FY21 and for construction (\$1.9m) in FY23.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Seacrest Blvd from Gulfstream Blvd. to Hypoluxo Rd.</p> <p>Project Number: 1662 BCC District: 07 Delivery Method: Annual Construction Contract Category: R04-Resurfacing Status: Construction Designer: N/A Contractor: Ranger Project Manager: Thomas Coppini</p>	<p>Resurfacing 5.8 miles (25.3 lane miles) of Seacrest Boulevard from Gulfstream Boulevard to Hypoluxo Road.</p> <p>FY 2021 IST \$2,400,000</p>	

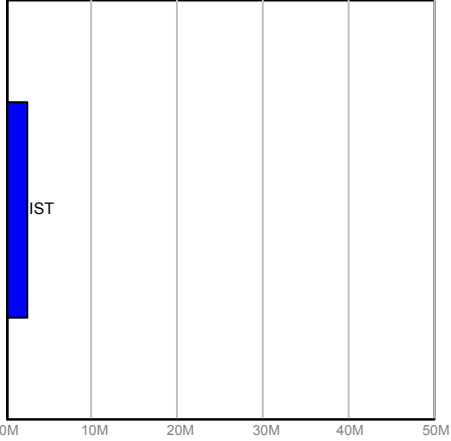SCHEDULE SUMMARY	PARTICIPATION	FUNDING																		
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Drainage Repairs</td> <td>11/1/2021</td> <td></td> </tr> <tr> <td>Milling and Pavement Complete</td> <td>2/1/2022</td> <td></td> </tr> <tr> <td>ADA (Curb/Cut Ramps) Complete</td> <td>4/1/2022</td> <td></td> </tr> <tr> <td>Traffic Striping Complete</td> <td>5/1/2022</td> <td></td> </tr> <tr> <td>Traffic Loops Complete</td> <td>7/1/2022</td> <td></td> </tr> </tbody> </table>		Original	Actual	Drainage Repairs	11/1/2021		Milling and Pavement Complete	2/1/2022		ADA (Curb/Cut Ramps) Complete	4/1/2022		Traffic Striping Complete	5/1/2022		Traffic Loops Complete	7/1/2022		<p>Consultant</p> <p>SBE N/A Local N/A WBE N/A MBE N/A</p> <p>Contractor</p> <p>SBE 15% Local 100% WBE 0% MBE 0%</p>	<div style="text-align: center;">  <p>Construction</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>IST</p> <p>Fund Source</p> </div>
	Original	Actual																		
Drainage Repairs	11/1/2021																			
Milling and Pavement Complete	2/1/2022																			
ADA (Curb/Cut Ramps) Complete	4/1/2022																			
Traffic Striping Complete	5/1/2022																			
Traffic Loops Complete	7/1/2022																			

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,400,000	\$2,302,530	95.94%	\$3,305
TOTAL	\$2,400,000	\$2,302,530	95.94%	\$3,305

NOTES

Outstanding work includes drainage repairs, milling and paving, updating ADA ramps, restriping the road, and replacing traffic loops.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Hypoluxo Rd. from Military Trail to U.S. 1

Resurfacing 3.7 miles (21.2 lane miles) of Hypoluxo Road from Military Trail to US 1.

Project Number: 1663
 BCC District: Multiple
 Delivery Method: Annual Construction Contract
 Category: R04-Resurfacing
 Status: Construction
 Designer: N/A
 Contractor: Ranger
 Project Manager: Thomas Coppini

FY 2021 IST \$1,400,000



SCHEDULE SUMMARY

PARTICIPATION

FUNDING


	Original	Actual
Milling and Pavement Complete	2/1/2021	5/11/2021
ADA (Curb/Cut Ramps) Complete	4/1/2021	
Traffic Striping Complete	5/1/2021	8/11/2021
Traffic Loops Complete	7/1/2021	

Consultant

SBE N/A
 Local N/A
 WBE N/A
 MBE N/A

Contractor

SBE 5%
 Local 100%
 WBE 0%
 MBE 0%

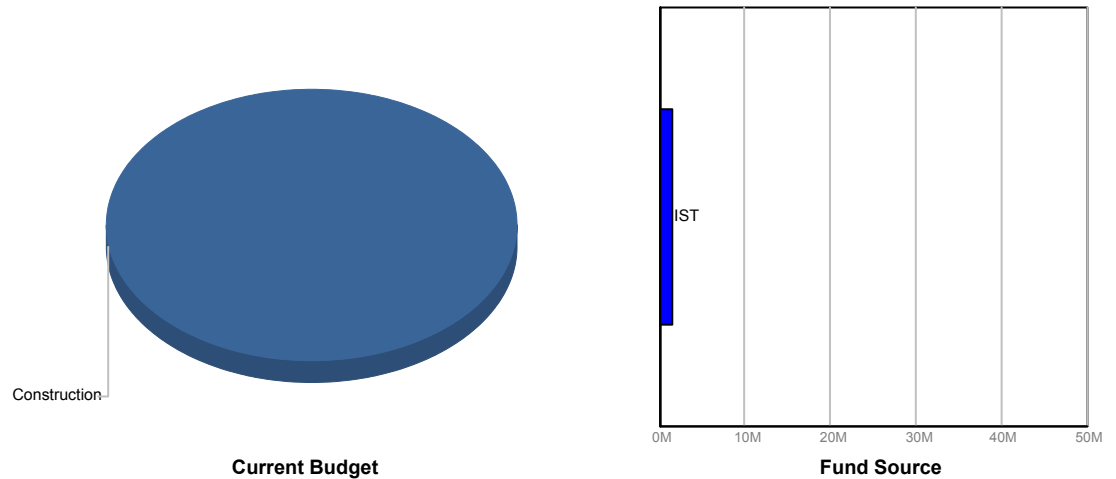

FINANCIAL SUMMARY

NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,400,000	\$1,377,614	98.40%	\$1,377,614
TOTAL	\$1,400,000	\$1,377,614	98.40%	\$1,377,614


Outstanding work includes, updating ADA ramps, and replacing traffic loops.


Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Lake Lytal Aquatic Center Replace Public Aquatic Facility</p> <p>Project Number: 17218</p> <p>BCC District: 02</p> <p>Delivery Method: Construction Management at Risk</p> <p>Category: A02-Aquatic Facility Repair and Replacement</p> <p>Status: Design</p> <p>Designer: Harvard Jolly, Inc.</p> <p>Contractor: Kauffman Lynn</p> <p>Project Manager: Rosalyn Acosta</p>	<p>The project entails constructing a new multi-phase Aquatic Complex mainly on undeveloped land along Kirk Rd. within Lake Lytal Park. The existing Pool Facility is to be demolished once the new aquatic center is opened to the public. The major components of the new Aquatic Complex will be a 70 Meter competition pool with dive well, a family water play area, 6-lane warm-up pool, flow riders, slides and building amenities such as restrooms, lockers, concession stand.</p> <p>FY 2017 IST - \$4,000,000 FY 2018 IST - \$2,000,000</p>	

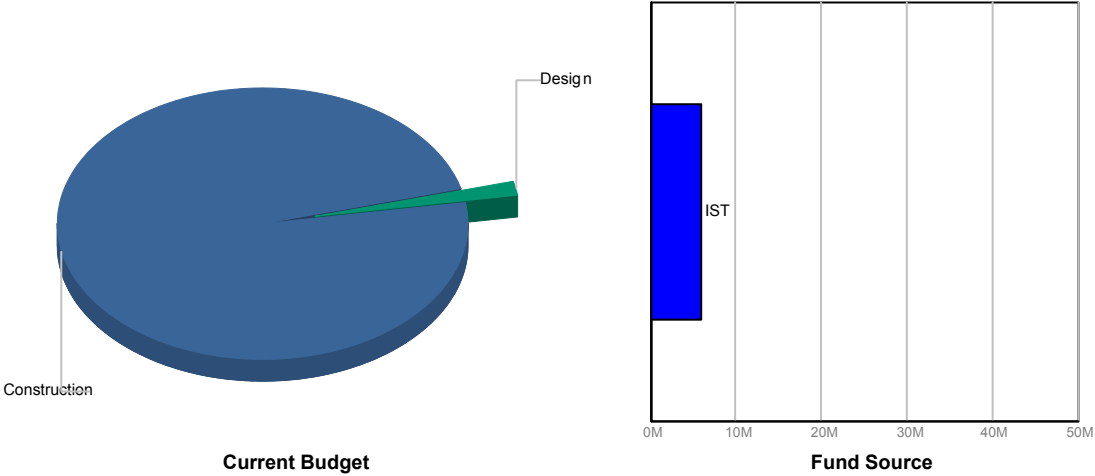SCHEDULE SUMMARY	PARTICIPATION	FUNDING																					
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>4/19/2018</td> <td>4/19/2018</td> </tr> <tr> <td>Design Start (Master Plan)</td> <td>7/10/2018</td> <td>7/10/2018</td> </tr> <tr> <td>Design Start (Aquatic Center)</td> <td>11/20/2018</td> <td></td> </tr> <tr> <td>Construction Start</td> <td>7/1/2019</td> <td></td> </tr> <tr> <td>Substantial Completion</td> <td>7/1/2020</td> <td></td> </tr> <tr> <td>Project Completion</td> <td>9/1/2020</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	4/19/2018	4/19/2018	Design Start (Master Plan)	7/10/2018	7/10/2018	Design Start (Aquatic Center)	11/20/2018		Construction Start	7/1/2019		Substantial Completion	7/1/2020		Project Completion	9/1/2020		<p>Consultant</p> <p>SBE 30%</p> <p>Local 100%</p> <p>WBE N/A</p> <p>MBE N/A</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p style="text-align: center;">Current Budget</p> <p style="text-align: center;">Fund Source</p>
	Original	Actual																					
Project Start	4/19/2018	4/19/2018																					
Design Start (Master Plan)	7/10/2018	7/10/2018																					
Design Start (Aquatic Center)	11/20/2018																						
Construction Start	7/1/2019																						
Substantial Completion	7/1/2020																						
Project Completion	9/1/2020																						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$100,000	\$268,981	268.98%	\$53,801
Construction	\$5,900,000	\$86,785	1.47%	\$400
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$37,316	0.00%	\$37,316
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$6,000,000	\$393,083	6.55%	\$91,517

NOTES

Design Development is ongoing, master plan layout is finalized, Civil consultants released.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Community Park - Paulette Burdick Park
Project Number: 18230
BCC District: CW
Delivery Method: TBD
Category: N02-New Park Development
Status: Design
Designer: Urban Design Kilday Studio
Contractor: TBD
Project Manager: Rosalyn Acosta

Construction of a neighborhood park that will service Cam Estates neighborhood, Meadowbrook and Plantation CCRT areas. The Park will mainly feature a walking pathway, children's playground and basketball courts.

IST Funding included in Current FY Budget: \$1,000,000
 IST Funding included in FY2023 Budget: \$4,900,000



SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting with User	8/7/2018	8/7/2018
Final Concept Drawings (Parks)	8/15/2018	8/15/2018
Pre-Scope with Consultant	8/29/2018	8/29/2018
Project Start (Due Diligence)	11/1/2018	11/28/2018
Design Start	1/7/2019	12/8/2020
Construction Start	4/1/2019	
Substantial Completion	9/1/2019	
Project Completion	10/1/2019	

PARTICIPATION

Consultant

SBE 100%

Local 100%

WBE N/A

MBE N/A

Contractor


SBE TBD

Local TBD


WBE TBD

MBE TBD

FUNDING

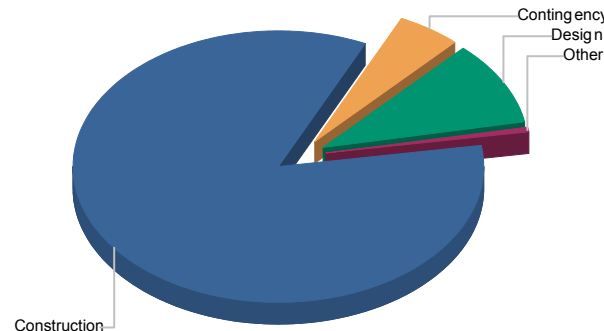

Current Budget

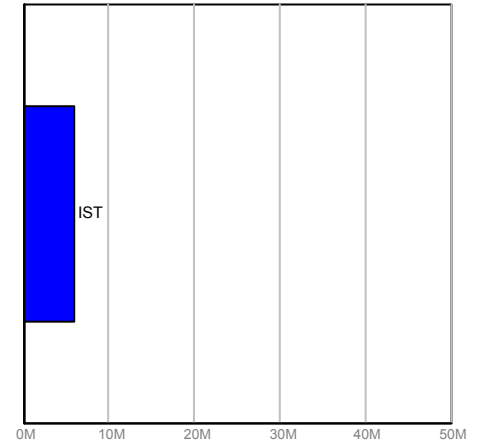

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$590,000	\$76,608	12.98%	\$76,608
Construction	\$5,015,000	\$71,236	1.42%	\$71,235
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$32,965	\$33,190	100.68%	\$33,190
Contingency	\$295,000	\$0	0.00%	\$0
TOTAL	\$5,932,965	\$181,033	3.05%	\$181,033

NOTES


Consultant authorization is currently pending signatures.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Lake Worth West Substation</p> <p>Project Number: B607 BCC District: Multiple Delivery Method: Construction Manager at Risk Category: S06-Sheriff - FDO Status: Design Designer: Ohlson Lavoie Collaborative Contractor: D Stephenson Project Manager: Sunil Jagoo</p>	<p>Provide dedicated office(s) within the HRC2 building (project-19220) for PBSO field personnel's use. Additional interior improvements include a multipurpose room for PBSO training purposes and HRC/community programming, as well as restrooms, circulation area, and other incidental improvements.</p> <p>FY 2019 IST \$1,213,460</p>	

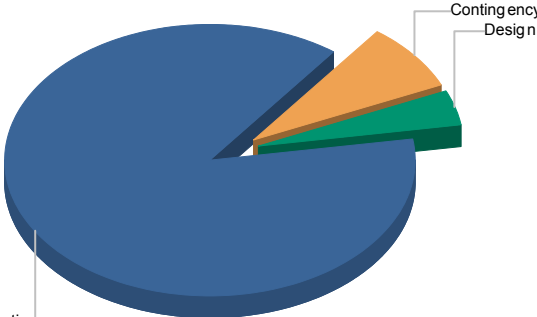SCHEDULE SUMMARY	PARTICIPATION	FUNDING				
<table border="1"> <thead> <tr> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td colspan="2">Please Refer to Central County Resource</td> </tr> </tbody> </table>	Original	Actual	Please Refer to Central County Resource		<p>Consultant</p> <p>SBE TBD Local TBD WBE TBD MBE TBD</p> <p>Contractor</p> <p>SBE TBD Local TBD WBE TBD MBE TBD</p>	 <p style="text-align: center;">Current Budget</p>  <p style="text-align: center;">Fund Source</p>
Original	Actual					
Please Refer to Central County Resource						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$2,227	4.45%	\$2,227
Construction	\$1,063,460	\$4,868	0.46%	\$4,868
Contingency	\$100,000	\$0	0.00%	\$0
TOTAL	\$1,213,460	\$7,095	0.58%	\$7,095

NOTES


Please refer to the Central County Resource Center report for current status and material project updates.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Housing Units for Homeless, Extremely Low Income, & Low Income</p> <p>Project Number: Q001</p> <p>BCC District: CW</p> <p>Delivery Method: TBD</p> <p>Category: H02-Housing</p> <p>Status: Design</p> <p>Designer: TBD</p> <p>Contractor: TBD</p> <p>Project Manager: Eric McClellan</p>	<p>This project involves the acquisition and renovation of older, possibly run down motel properties into efficiency units for use as temporary or longer term affordable housing for homeless and special populations.</p> <p>This Project is funded in: FY 2017 - FY 2026 for \$2,550,000 each year for a total project estimate at \$25,500,000.</p>	

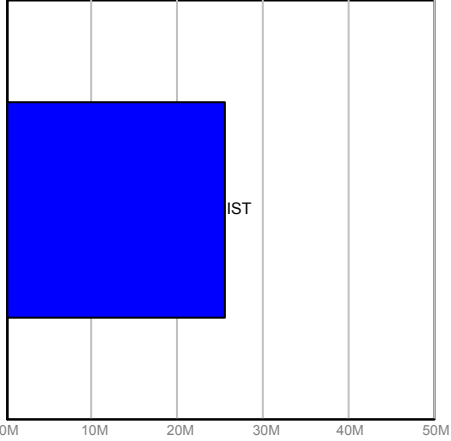SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>9/1/2017</td> <td>9/1/2017</td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> <tr> <td>Project Completion</td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> <tr> <td> </td> <td> </td> <td> </td> </tr> </tbody> </table>		Original	Actual	Project Start	9/1/2017	9/1/2017													Project Completion									<p>Consultant</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE N/A</p> <p>MBE N/A</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
	Original	Actual																											
Project Start	9/1/2017	9/1/2017																											
Project Completion																													

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$11,950	0.00%	\$11,950
Construction	\$25,470,000	\$4,818,006	18.92%	\$578,680
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$30,000	\$45,025	150.08%	\$45,025
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$25,500,000	\$4,874,980	19.12%	\$635,655

NOTES


This Project will fund multiple projects over the 10 year period. Direction from the BCC was given on 9/26/2017 to proceed with an affordable housing pilot project . Staff of FD&O, DHES, Community Services, and Administration presented a proposed Project Plan for the remainder of the funding at a BCC Workshop on February 26, 2019 and received direction. The RFP for the Cottage Homes pilot project was awarded by the BCC to the WPB Housing Authority on January 12, 2021. Permitting by the WPBHA is now in progress. An allocation of \$1M toward renovation of a non-congregate shelter in Pahokee was approved by the BCC on Sept. 15, 2020. Development of a solicitation is now commencing on the next phase of the Project Plan (i.e. Tax Deed Surplus Property Conveyance and Housing Authorities Incentive Funding).

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects


Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Countywide ADA Renovations</p> <p>Project Number: Q002 BCC District: CW Delivery Method: Annual Contract Category: G02-General Government Facilities Status: Design Designer: Colome' and Associates Contractor: Lebolo Construction Project Manager: David Lavinsky</p>	<p>Renovate multiple public facility restrooms to meet ADA requirements. The following locations are planned for renovation: Delray Health Clinic ADA Restrooms @ \$250K FY2017 Lantana Health Clinic ADA Restrooms @ \$275K FY2022 Lantana Health Clinic ADA Service Counter @ \$16K FY2022 Jupiter Health Clinic ADA Restrooms @ \$64K FY2022 West County Administration Building (aka Glades Office Building) ADA Improvements @ \$245K FY2022 and \$450K FY2023</p> <p>This Project is funded in: FY 2017 \$250,000 FY 2024 \$700,000 FY 2022 \$600,000 FY 2025 \$539,000 FY 2023 \$450,000</p>	

SCHEDULE SUMMARY		
	Original	Actual
Delray Health Start	7/27/2017	7/27/2017
Delray Health Finish	12/21/2018	
Lantana Health Start	7/7/2017	7/7/2017
Lantana Health Finish	4/8/2018	
Lantana Health (Counters) Start	11/24/2020	11/24/2020
Lantana Health (Counters) Finish		
Jupiter Health Start	12/22/2020	12/22/2020
Jupiter Health Finish		
West County Admin Start		
West County Admin Finish		

PARTICIPATION	
Consultant	
SBE	100%
Local	100%
WBE	N/A
MBE	N/A
Contractor	
SBE	N/A
Local	N/A
WBE	N/A
MBE	N/A

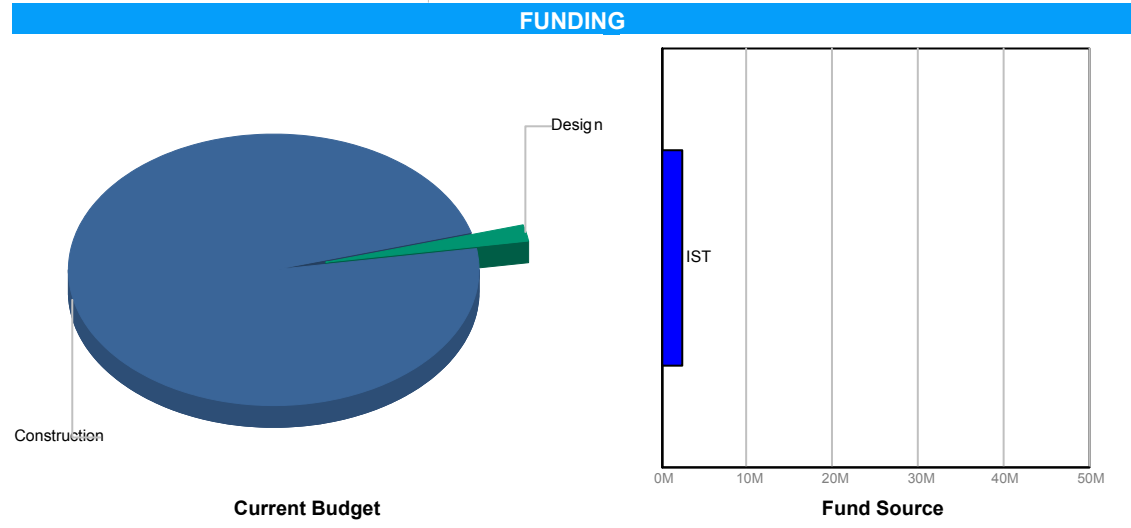

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$50,000	\$44,700	89.40%	\$34,721
Construction	\$2,489,000	\$187,024	7.51%	\$10,611
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$0	0.00%	\$0
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$2,539,000	\$231,724	9.13%	\$45,332

NOTES

Delray Health Clinic Restrooms: All sewer piping requirements and concrete patching are complete on 1st floor restrooms. 2nd floor restroom demolition is complete. Currently in process of sewer piping changes.

Jupiter Health Clinic Restrooms and Lantana Health Clinic Restrooms & Service Counter: Projects will now commence with FY2022 funding


West County Administration Building (aka Glades Office Building) ADA Improvements: Has not yet started



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Vehicle Replacement</p> <p>Project Number: Q007 BCC District: Multiple Delivery Method: Direct Purchase Category: S04-Sheriff Status: Construction Designer: N/A Contractor: N/A Project Manager: Isami Ayala-Collazo</p>	<p>This project funds the replacement of PBSO public safety vehicles and related equipment (other than radios), tools and/or services.</p> <p>FY 18 Funds: \$3,650,513 FY 19 Funds: \$3,650,513 FY 20 Funds: \$3,650,514 FY 24 Funds: \$1,669,963</p>	

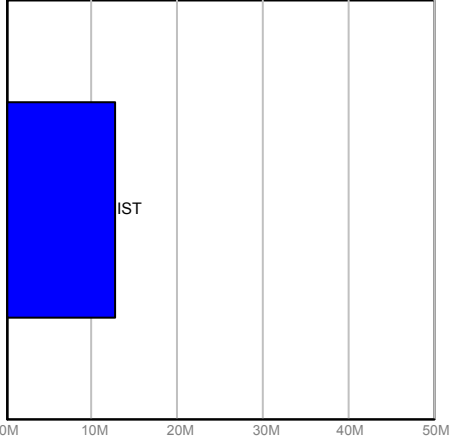SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>1 Project Start</td> <td>10/1/2018</td> <td>5/1/2018</td> </tr> <tr> <td>2 Project Completion</td> <td>9/30/2024</td> <td></td> </tr> </tbody> </table>		Original	Actual	1 Project Start	10/1/2018	5/1/2018	2 Project Completion	9/30/2024		<p>Consultant</p> <ul style="list-style-type: none"> SBE N/A Local N/A WBE N/A MBE N/A <p>Contractor</p> <ul style="list-style-type: none"> SBE N/A Local N/A WBE N/A MBE N/A 	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
	Original	Actual									
1 Project Start	10/1/2018	5/1/2018									
2 Project Completion	9/30/2024										

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Furniture, Fixtures & Equipment	\$12,621,503	\$10,933,034	86.62%	\$10,933,034
Other	\$0	\$0	0.00%	\$0
TOTAL	\$12,621,503	\$10,933,034	86.62%	\$10,933,034

NOTES

Prioritization, identification and cost of specific assets are determined by the Sheriff's Office with administration support being performed by FD&O through a Project Funding Agreement with the County.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Animal Care & Control

Project Number: Q008
 BCC District: CW
 Delivery Method: Construction Manager at Risk
 Category: G02-General Government Facilities
 Status: Design
 Designer: PGAL
 Contractor: Wharton-Smith
 Project Manager: Rich Avery

The Animal Care & Control Renovation & Expansion project for the Belvedere Rd. campus includes: renovations to existing buildings for improved functionality; possible replacement of non-air conditioned kennel buildings with air-conditioned kennel buildings pending evaluation, pricing and approval; and the creation of new spaces necessary to facilitate current and future projected operational needs. The cost of the project includes cost-estimating services necessary in order to validate the project scope, which was derived jointly by FDO & the ACC Division via a needs assessment and programming document, as well as interim arrangements to sustain continuous operations during construction.



SCHEDULE SUMMARY

	Original	Actual
PROGRAMMING	10/1/2018	10/1/2018
Commence Design Comparative Study	7/24/2019	7/24/2019
Design Start	2/3/2020	12/2/2020
Construction Start	12/1/2020	
Substantial Completion	7/3/2023	

PARTICIPATION


Consultant

SBE 20%
 Local 100%
 WBE N/A
 MBE N/A


Contractor

SBE 13.04%
 Local 13.04%
 WBE 13.04%
 MBE 13.04%

FUNDING

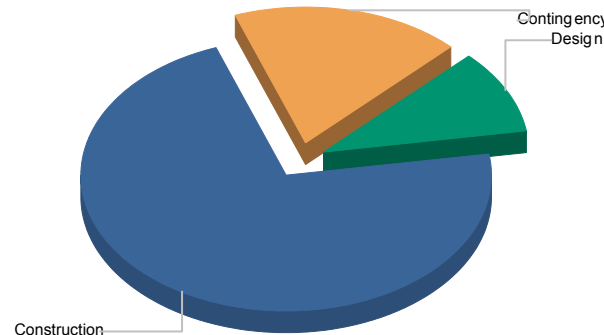

Current Budget

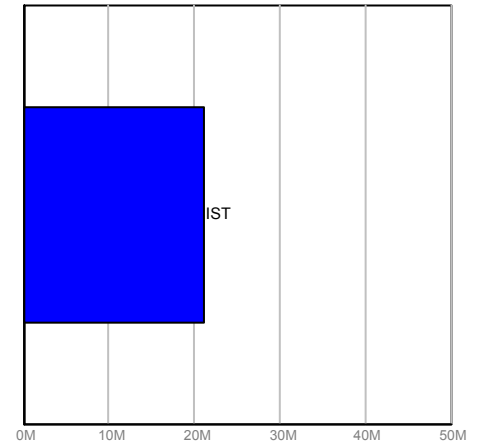

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$2,100,000	\$868,205	41.34%	\$416,773
Construction	\$15,120,000	\$213,791	1.41%	\$212,057
Contingency	\$3,780,000	\$0	0.00%	\$0
TOTAL	\$21,000,000	\$1,081,996	5.15%	\$628,831

NOTES

The schematic design has been submitted for review by the County. Pending is the scheduling of the schematic design review meeting to be scheduled by the AE. A partial DD Phase will follow.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Central County Housing Resource Center
Project Number: Q009
BCC District: CW
Delivery Method: Construction Manager at Risk
Category: H02-Housing
Status: Design
Designer: Ohlson Lavoie Collaborative
Contractor: D Stephenson
Project Manager: Sunil Jagoo

The Homeless Resource Center 2 (HRC 2) is to provide an effective Crisis Response System that provides immediate and easy access to safe and decent temporary shelter to County residents that need it and aims to re-house people as quickly as possible while receiving wrap-around social services. The facility will compliment the County's existing Senator Philip D. Lewis Center in West Palm Beach and will consist of approximately 19,000 square feet to support 74 client beds, dining and service delivery/office areas, restrooms, laundry facilities, an intake lobby, and other incidental interior and exterior improvements. Co-located within the facility will be the improvements identified in the IST Project Plan titled PBSO Lake Worth West Substation.



SCHEDULE SUMMARY

PARTICIPATION

FUNDING


	Original	Actual
Program Development	11/1/2017	11/1/2017
Public Outreach	2/1/2019	2/1/2019
Design Team Solicitation	5/1/2019	9/30/2020
CM Solicitation	9/1/2019	11/26/2019
Schematic Design	11/11/2019	1/31/2020
Design Development	5/1/2020	9/28/2020
Construction Documents	10/1/2020	2/23/2021
Permitting	1/1/2021	
Construction	6/1/2021	
CO/Substantial Completion	9/1/2022	
Occupancy	10/3/2022	

Consultant

SBE 0%
 Local 25%
 WBE 0%
 MBE 0%

Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

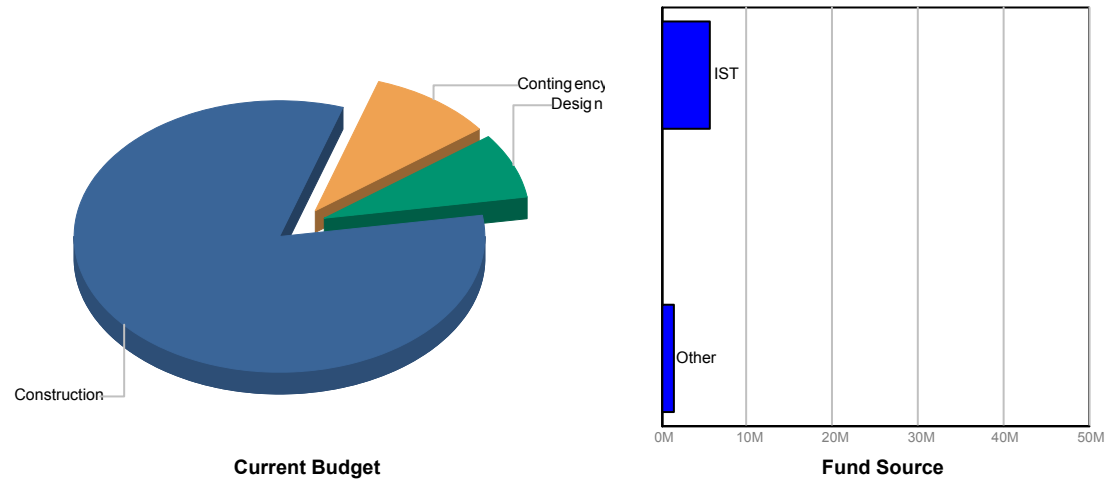

FINANCIAL SUMMARY

NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$550,000	\$74,448	13.54%	\$74,448
Construction	\$5,874,843	\$88,717	1.51%	\$52,384
Contingency	\$700,000	\$0	0.00%	\$0
TOTAL	\$7,124,843	\$163,165	2.29%	\$126,832


Revised plans to address building permit comments has been re-submitted for review. Permits by other regulatory agencies are in process. GMP negotiations are ongoing and about to be finalized. Budget reconciliation is still ongoing. Funding includes \$5.7 M from IST in FY19 and CDBG funds in the total amount of \$1,424,843



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: South County Administrative Complex</p> <p>Project Number: Q010 BCC District: 07 Delivery Method: Varies Category: G02-General Government Facilities Status: Design Designer: Varies Contractor: Varies Project Manager: Eric McClellan</p>	<p>This project funds essential Renewal and Replacement (R&R) needs to sustain the continuous operation of this 40+ year old complex prior to its future redevelopment. As such there is no defined scope of work. Any funds remaining at such time that redevelopment is funded would be utilized toward professional design services for the redevelopment. Funding includes \$3M each in FY 2020 and FY 2021, for a total of \$6M.</p>	

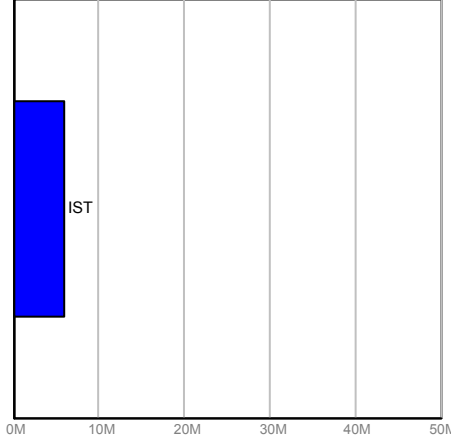SCHEDULE SUMMARY	PARTICIPATION	FUNDING				
<table border="1"> <thead> <tr> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td colspan="2">N/A. See notes for current activity.</td> </tr> </tbody> </table>	Original	Actual	N/A. See notes for current activity.		<p>Consultant</p> <ul style="list-style-type: none"> SBE 100% Local 100% WBE 78.6% MBE 0% <p>Contractor</p> <ul style="list-style-type: none"> SBE TBD Local TBD WBE TBD MBE TBD 	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Construction</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
Original	Actual					
N/A. See notes for current activity.						

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$6,000,000	\$190,388	3.17%	\$59,062
Other	\$0	\$4,902	0.00%	\$3,850
TOTAL	\$6,000,000	\$195,290	3.25%	\$62,912

NOTES

Paved vehicular surfaces throughout the complex are in need of R&R. Reconfiguration of a driveway for improved circulation, consistency with intended future site development and cross access with an adjacent property will be implemented same time to preclude future duplication of work and lost investment. Design services to permit this scope of work is in progress.

A scope of work for other R&R needs is currently under development.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Government Center
Renewal/Replacement

Project Number: Q011

BCC District: 02

Delivery Method: Construction Manager at Risk

Category: G02-General Government Facilities

Status: Design

Designer: Netta Architects

Contractor: TBD

Project Manager: Jeffrey Halverson

This project includes but is not limited to upgrades and replacement of select building finishes and systems including security, HVAC, plumbing, fire alarm, fire sprinkler, electrical, low voltage, lighting, flooring and paint. The scope of the project will additionally include a building conditions assessment, program evaluation study, interior space planning and layout improvements. The proposed renovations to the Robert Weisman Governmental Center are designed to increase the functionality of key areas within the facility and bring the building up to current County standards.

This project is funded in:
FY2022 IST \$19,000,000
FY2023 IST \$7,000,000



SCHEDULE SUMMARY

	Original	Actual
Design RFP Final Selection	11/8/2021	11/8/2021
CM RFP Proposals Due	12/2/2021	
CM Shortlist Meeting	1/19/2022	

PARTICIPATION

Consultant

SBE TBD

Local TBD

WBE TBD

MBE TBD

Contractor


SBE TBD

Local TBD

WBE TBD

MBE TBD

FUNDING

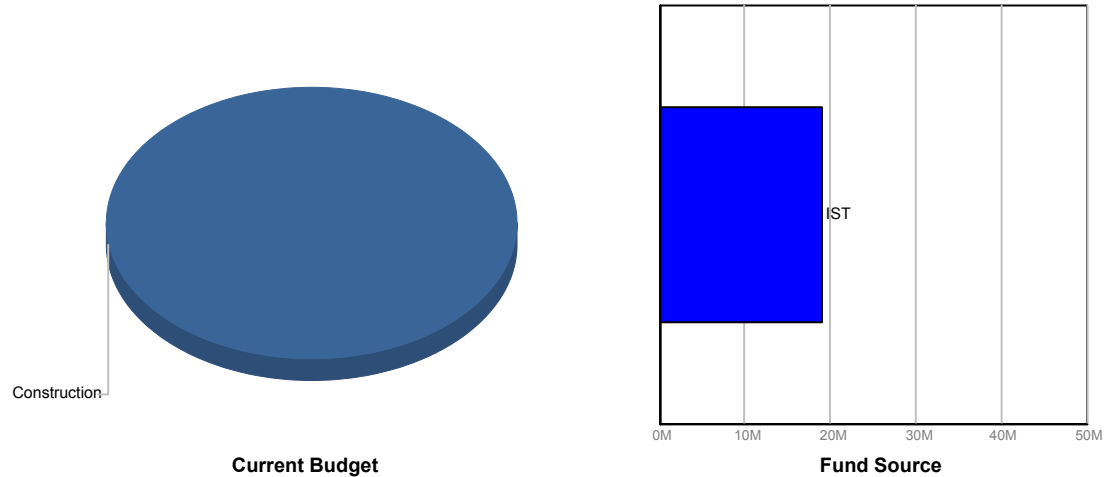

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$19,000,000	\$0	0.00%	\$0
TOTAL	\$19,000,000	\$0	0.00%	\$0

NOTES

Consultant final selection took place on 11/8/2021. Netta Architects was selected. Contract negotiation is forthcoming. CM selection is in progress.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Detention Center Facilities R/R (Phases 3-5)
Project Number: Q019
BCC District: Multiple
Delivery Method: Construction Management
Category: S06-Sheriff - FDO
Status: Construction
Designer: Leo A. Daly
Contractor: Hedrick Brothers Construction
Project Manager: Jeffrey Halverson

Phases 3-5 consist of the East Tower and West Tower which are located at the Main Detention Center. The West Detention Center is located in Belle Glade. The design for both towers and the West Detention Center will require repairing and replacing MEP, Fire Sprinkler System, Low Voltage Systems and interior finishes.
 Detention Center Facilities R/R (Phases 3-5)
 FY 2018 IST \$8,500,000
 FY 2019 IST \$14,700,000
 FY 2020 IST \$9,800,000



SCHEDULE SUMMARY

	Original	Actual
East Tower Design Start	11/12/2018	7/11/2019
East Tower Construction Start	10/14/2019	
East Tower Substantial Completion	11/10/2020	

PARTICIPATION


Consultant

SBE 19.88%
 Local 67%
 WBE N/A
 MBE N/A


Contractor

SBE 63%
 Local 84%
 WBE N/A
 MBE N/A

FUNDING

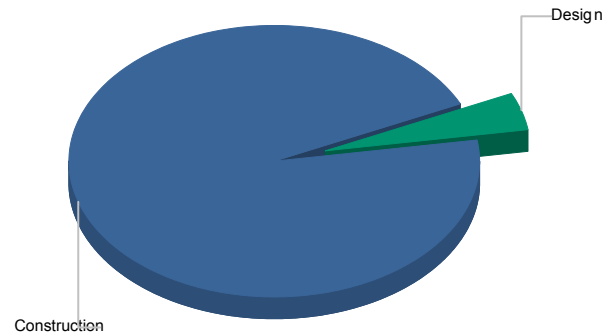

Current Budget

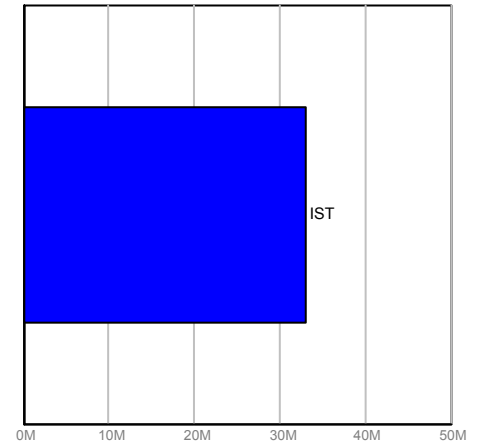

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$1,500,000	\$1,974,578	131.64%	\$984,750
Construction	\$31,595,881	\$19,756,364	62.53%	\$11,439,587
Other	\$0	\$1,298,028	0.00%	\$817,688
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$33,095,881	\$23,028,971	69.58%	\$13,242,025

NOTES


Main Detention Center South Tower: There is no R&R work scheduled for the South Tower at this time. PBSO has pursued a different direction for the quarantine block.
 Main Detention Center East Tower: Work is proceeding with lighting controls and communication wiring. Reroofing and flashing completed. Roof drains are being reviewed for lining. Intercom wiring being pulled. Exhaust fans being installed in Penthouse level. All shower vents removed for replacement. Openings for all fire dampers being cut and framed.
 Main Detention Center West Tower: Final plans in process; to be provided to HBC to prepare GMP.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: West Boynton Park Athletic Field Renovations Sports Turf</p> <p>Project Number: T002</p> <p>BCC District: 03</p> <p>Delivery Method: TBD</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.</p> <p>Funded:</p> <p>FY 2020 \$1,000,000</p> <p>FY 2023 \$1,000,000</p>	

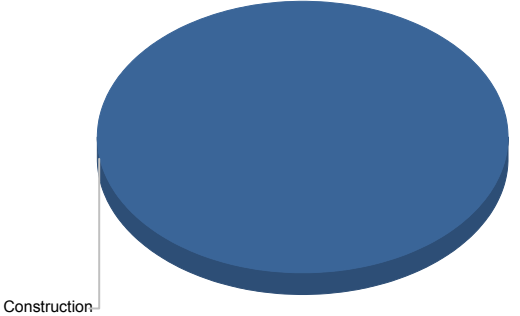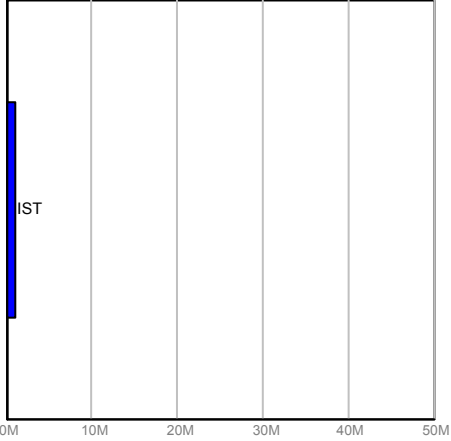SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td>4/20/2021</td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		<p>Consultant</p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	 <p>Current Budget</p>  <p>Fund Source</p>
	Original	Actual																											
Begin Existing Site Surveys	1/29/2020	1/29/2020																											
Complete Existing Site Surveys	6/30/2020	5/18/2020																											
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																											
Design RFP Proposals Due	9/4/2020	9/10/2020																											
Design RFP Final Selection	10/29/2020	10/29/2020																											
Consultant Contract Issuance	12/14/2020	4/20/2021																											
Design Completion	7/2/2021																												
Turf Supplier RFP Proposal Due	4/30/2021																												

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$175,139	0.00%	\$8,739
Construction	\$1,000,000	\$15,650	1.57%	\$15,650
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$76	0.00%	\$76
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$1,000,000	\$190,865	19.09%	\$24,465

NOTES


Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Buttonwood Park</p> <p>Project Number: T003 BCC District: 03 Delivery Method: TBD Category: A06-Athletic Field Renovations Status: Design Designer: Florida Transportation Engineering Contractor: TBD Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 2 & 3</p> <p>Funded: FY 2017 \$11,658 FY 2021 \$900,000 FY 2023 \$1,488,342</p>	

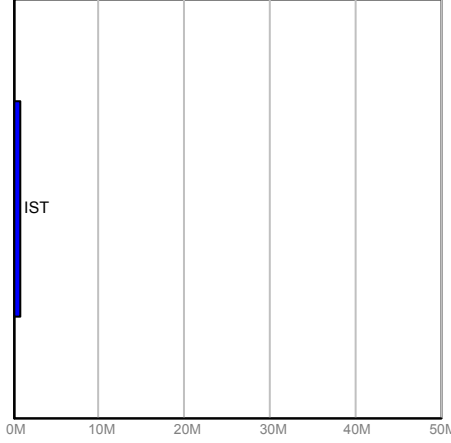SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>8/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td>4/20/2021</td> </tr> <tr> <td>Design Completion</td> <td>7/22/2001</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	8/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	7/22/2001		Turf Supplier RFP Proposal Due	4/30/2021		<p>Consultant</p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="text-align: center;">  <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div>
	Original	Actual																								
Begin Existing Site Surveys	1/29/2020	1/29/2020																								
Complete Existing Site Surveys	8/30/2020	5/18/2020																								
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																								
Design RFP Proposals Due	9/4/2020	9/10/2020																								
Consultant Contract Issuance	12/14/2020	4/20/2021																								
Design Completion	7/22/2001																									
Turf Supplier RFP Proposal Due	4/30/2021																									

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$183,402	0.00%	\$15,402
Construction	\$911,658	\$29,332	3.22%	\$0
Furniture, Fixtures & Equipment	\$0	\$0	0.00%	\$0
Other	\$0	\$12,458	0.00%	\$12,458
Contingency	\$0	\$0	0.00%	\$0
TOTAL	\$911,658	\$225,192	24.70%	\$27,861

NOTES

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: FY2017 Sports Field Lighting Replacement
Project Number: T006
BCC District: Multiple
Delivery Method: Sports Field Lighting Annual
Category: S12-Sports Lighting Replacement
Status: Design
Designer: JLRD Engineers
Contractor: Musco
Project Manager: Stuart Patterson

Replacement of Sports Field Lighting at Bert Winters Park, Caloosa Park, Glades Pioneer Park, Juno South Park, Jupiter Farms Park, Okeehetee Park, Pinewoods Park, (Burt Aaronson) South County Regional Park and Westgate Park.
 IST FY 2017 funds: \$4,100,000.



SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	
Bidding Package 1	11/6/2019	11/6/2019
Construction Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	4/2/2020
Construction Completion Phase 2	7/17/2020	4/2/2021
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	6/1/2020
Construction Completion Phase 3	8/28/2020	

PARTICIPATION


Consultant

SBE 100%
 Local 100%
 WBE N/A
 MBE N/A

Contractor

SBE 0%
 Local 75%
 WBE 0%
 MBE 0%

FUNDING

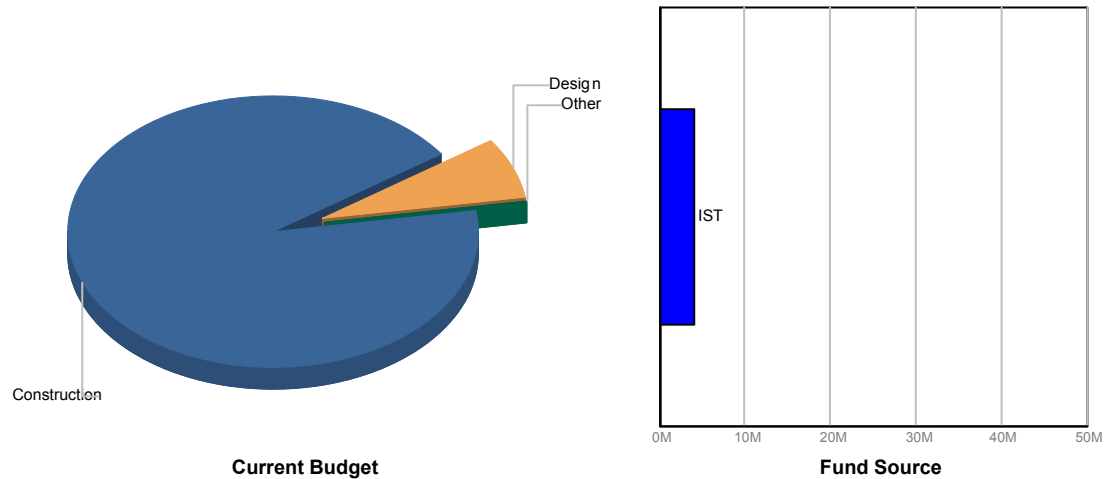

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$299,161	\$25,019	8.36%	\$25,019
Construction	\$3,800,000	\$3,780,386	99.48%	\$3,680,976
Other	\$839	\$2,952	351.65%	\$2,952
TOTAL	\$4,100,000	\$3,808,356	92.89%	\$3,708,946

NOTES


All parks associated with this fiscal year's sports field lighting replacement have been completed. The remaining balance of unused funds will be the subject of a future transfer

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects


Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: FY2018 Sports Field Lighting Replacement</p> <p>Project Number: T007</p> <p>BCC District: Multiple</p> <p>Delivery Method: Sports Field Lighting Annual</p> <p>Category: S12-Sports Lighting Replacement</p> <p>Status: Design</p> <p>Designer: JLRD Engineers</p> <p>Contractor: Musco</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of Sports Field Lighting at Dyer Park, Lake Charleston Park and (Burt Aaronson) South County Regional Park.</p> <p>IST FY 2018 funds: \$1,200,000.</p>	

SCHEDULE SUMMARY		
	Original	Actual
Bidding Package 1	11/6/2019	11/6/2019
Construction Start Phase 1	2/3/2020	2/3/2020
Construction Completion Phase 1	7/2/2020	8/24/2020
Bidding Package 2	2/13/2020	2/13/2020
Construction Start Phase 2	5/11/2020	4/2/2020
Construction Completion Phase 2	7/17/2020	4/2/2021
Bidding Package 3	3/26/2020	3/26/2020
Construction Start Phase 3	6/15/2020	6/1/2020
Construction Completion Phase 3		
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	5/9/2019
Final Completion	10/2/2020	

PARTICIPATION	
Consultant	
SBE	100%
Local	100%
WBE	N/A
MBE	N/A
Contractor	
SBE	0%
Local	75%
WBE	0%
MBE	0%

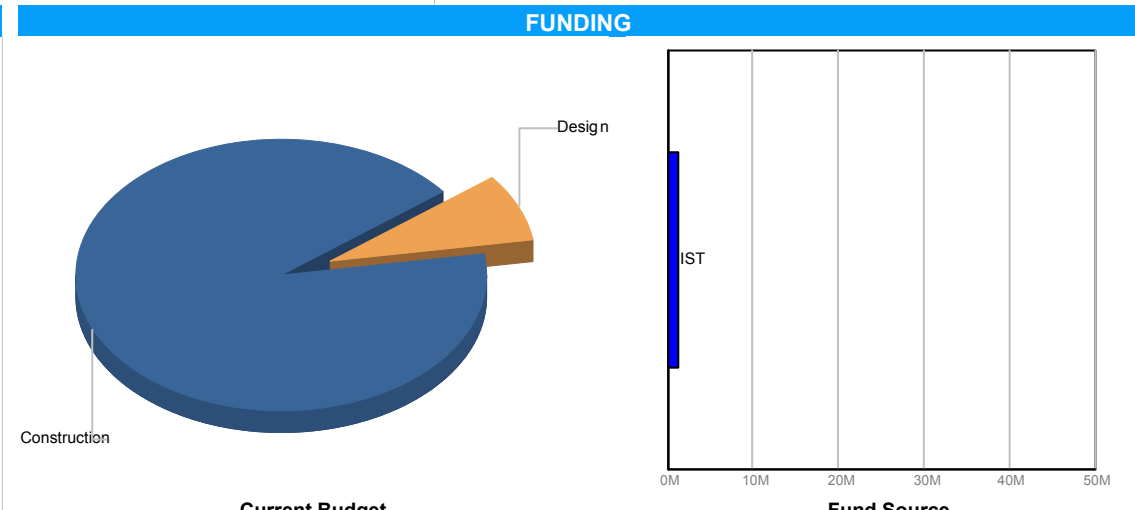

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$96,000	\$189,640	197.54%	\$189,640
Construction	\$1,104,000	\$193,788	17.55%	\$144,888
TOTAL	\$1,200,000	\$383,428	31.95%	\$334,528

NOTES

All parks associated with this fiscal year's sports field lighting replacement have been completed. The remaining balance of unused funds will be the subject of a future transfer.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: FY2020 Sports Field Lighting Replacement
Project Number: T010
BCC District: Multiple
Delivery Method: Sports Field Lighting Annual
Category: S12-Sports Lighting Replacement
Status: Design
Designer: JLRD Engineers
Contractor: Musco
Project Manager: Stuart Patterson

Lake Lytal Athletic Courts, Haverhill Tennis & Racquetball Courts, BASCR Basketball Courts, Duncan Padget Park Raquetball Courts
 IST Funds = \$1,300,000.



SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
Procurement (Light Fixture Vendor)	10/16/2018	10/16/2018
Procurement (Installation Contractor)	10/17/2018	

PARTICIPATION


Consultant

SBE 100%
 Local 100%
 WBE N/A
 MBE N/A


Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

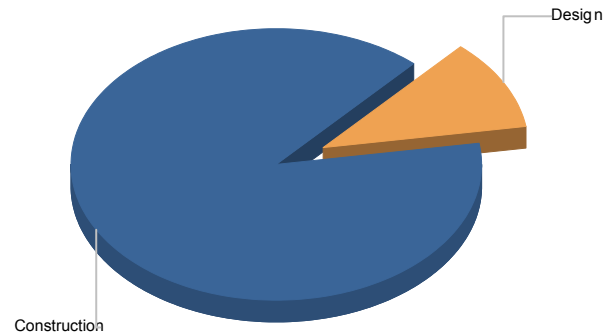

Current Budget

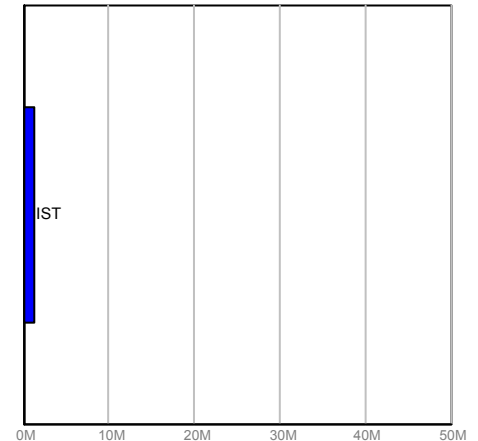

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$130,000	\$454,553	349.66%	\$79,950
Construction	\$1,070,000	\$0	0.00%	\$0
TOTAL	\$1,200,000	\$454,553	37.88%	\$79,950

NOTES

Lake Lytal (Package 1): Bids received. Project awarded to Davco Electrical Contractors Corp.
 South County Regional Park (Package 1): Bids received. Project awarded to Electrical Contracting Services, Inc.
 Haverhill Park (Package 2): Awaiting advertisement for bid. Anticipated 11/15/2021.
 Haverhill Park Racquetball Courts (Package 3): Advertisement for Bid TBD.
 Duncan Padget Park Raquetball Courts is currently on hold.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: FY2021 Sports Lighting Replacement

Project Number: T011
 BCC District: Multiple
 Delivery Method: Sports Field Lighting Annual
 Category: S12-Sports Lighting Replacement
 Status: Design
 Designer: JLRD Engineers
 Contractor: Musco
 Project Manager: Stuart Patterson

Caloosa Park Athletic Courts, Seminole Palms BF 1-8 & MPF 9-11, BASCR Tennis Courts, Carlin Park Tennis Courts, Veterans Park Tennis & Bball Courts, Dyer Park Basketball Courts, Lake Lytal Tball Multipurpose Field 5.

FY 2021 IST Funds = \$4,050,000.



SCHEDULE SUMMARY

	Original	Actual
Project Start	6/29/2017	6/29/2017
	10/16/2018	10/16/2018
	10/17/2018	

PARTICIPATION


Consultant

SBE 100%
 Local 100%
 WBE N/A
 MBE N/A

Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

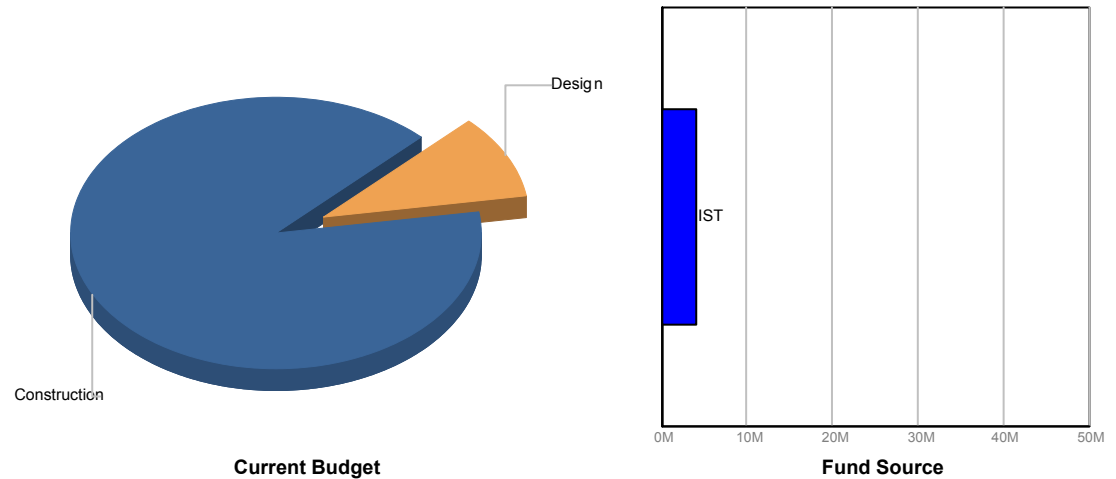

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$405,000	\$107,788	26.61%	\$13,292
Construction	\$3,645,000	\$1,795,486	49.26%	\$0
TOTAL	\$4,050,000	\$1,903,274	46.99%	\$13,292

NOTES

Carlin Park (Package 1): Bids Received; Project Awarded to Davco Electrical Contractors Corp.
 Seminole Palms Park (Package 1): Bids Received; Project Awarded to M. Gay Constructions, Inc.
 South County Regional Park (Package 1): Bids Received; Project Awarded to Electrical Contracting Services, Inc.
 Caloosa Park (Package 2), Dyer Park (Package 2), & Veteran's Memorial Park (Package 2): Awaiting Advertisement for Bid. Anticipated Release 11/15/2021
 Lake Lytal Park is currently on hold.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Bert Winters Park Redevelopment

Project Number: T041
 BCC District: 01
 Delivery Method: Annual Contract
 Category: E02-Existing Park Redevelopment or Expansion
 Status: Design
 Designer: Architecture Green
 Contractor: TBD
 Project Manager: Sunil Jagoo

Demolish former PBMI building, tennis courts, and playground. Remove lights and poles servicing Field 2. Renovate Baseball Field 1. Construct new regulation 220' x 360' multipurpose field. Construct new 30' x 60' rental pavilion. Construct new playground area. Renovate existing day use dock for public use. Construct new paved parking, curbing, landscaping, sidewalks and picnic areas. Install new underground infrastructure and site lighting.



The project is funded in:
 FY 2019 IST \$200,000
 FY 2021 IST \$1,500,000
 FY 2021 FIND Grant TBD

SCHEDULE SUMMARY

	Original	Actual
Project Start	8/22/2019	8/22/2019
Asbestos Report Initiated	8/23/2019	8/23/2019
Asbestos Report Completion	10/1/2019	10/1/2019
Demolition Start	11/12/2019	4/16/2020
Demolition Completion	12/5/2019	8/17/2020
Design Completion	TBD	

PARTICIPATION


Consultant

SBE 89.28%
 Local 100%
 WBE N/A
 MBE N/A


Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING



Current Budget

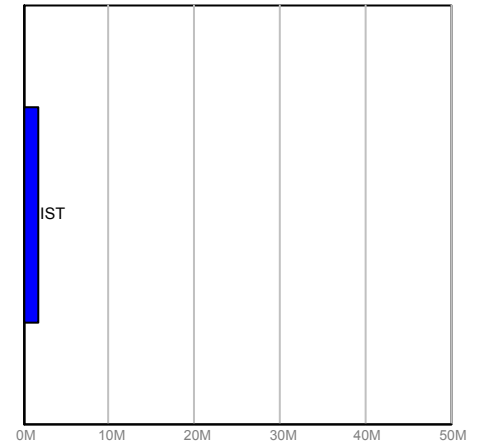

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$1,700,000	\$103,947	6.11%	\$103,947
Other	\$0	\$3,826	0.00%	\$3,781
Contingency	\$0	\$270	0.00%	\$270
TOTAL	\$1,700,000	\$108,043	6.36%	\$107,998

NOTES

Received comments from Parks on the Consultant's proposal. Comments will be forwarded to the Consultant upon completion of FDO review.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Aqua Crest Pool Facility Replacement

Project Number: T077
 BCC District: 07
 Delivery Method: CMR
 Category: A02-Aquatic Facility Repair and Replacement
 Status: Design
 Designer: Ohlson Lavoie Collaborative
 Contractor: TBD
 Project Manager: Rosalyn Acosta

The work consist of the design and renovation of the existing Aqua Crest pool facility. The scope includes but is not limited to: pool improvements such as leak detection, re-surface, lane marker replacement, filtration system replacement; pool deck renovations; demolition of wadding pool; new splash pad; relocation of ticketing booth, admin offices, guards room and weight's room; bathroom renovations; new shade structures and Marquee sign.



SCHEDULE SUMMARY

	Original	Actual
Pre-Scope meeting	2/20/2019	2/20/2019
Design Services Advertisement	6/17/2019	8/4/2019
Consultant BCC Approval	1/14/2020	
Design Start	1/21/2020	
Construction Start	3/9/2021	
Substantial Completion	3/8/2022	
Project Close-out	5/3/2022	

PARTICIPATION


Consultant

SBE TBD
 Local TBD
 WBE N/A
 MBE N/A


Contractor

SBE TBD
 Local TBD
 WBE TBD
 MBE TBD

FUNDING

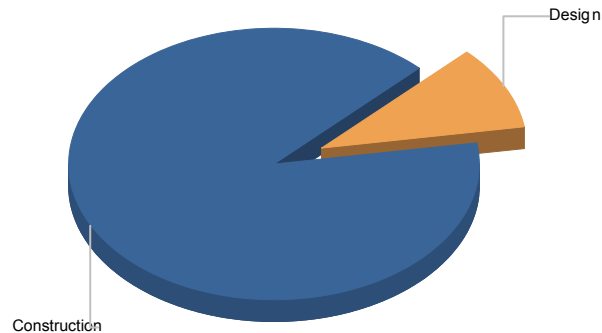

Current Budget

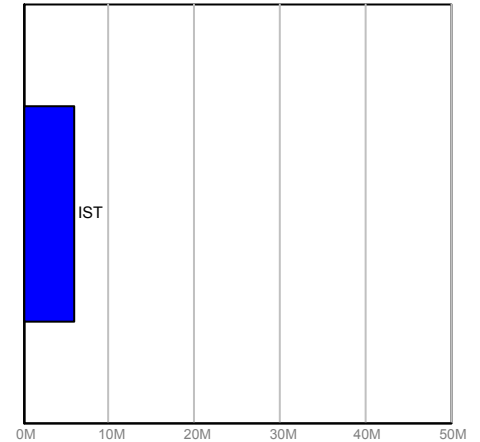

Fund Source

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$600,000	\$123,092	20.52%	\$105,826
Construction	\$5,400,000	\$14,058	0.26%	\$14,058
TOTAL	\$6,000,000	\$137,150	2.29%	\$119,884

NOTES

No status change. Project will remain on hold until additional funding resolution.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Dyer Park Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on multi-purpose field 3, 4, & 5 as well as additional damaged area.
Funded: FY 2020 \$6,000,000



Project Number: T099
BCC District: 07
Delivery Method: TBD
Category: A06-Athletic Field Renovations
Status: Design
Designer: Florida Transportation Engineering
Contractor: TBD
Project Manager: Stuart Patterson

SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020

PARTICIPATION


Consultant

SBE 25%
Local 25%
WBE 0%
MBE 6.13%

Contractor

SBE TBD
Local TBD
WBE TBD
MBE TBD

FUNDING

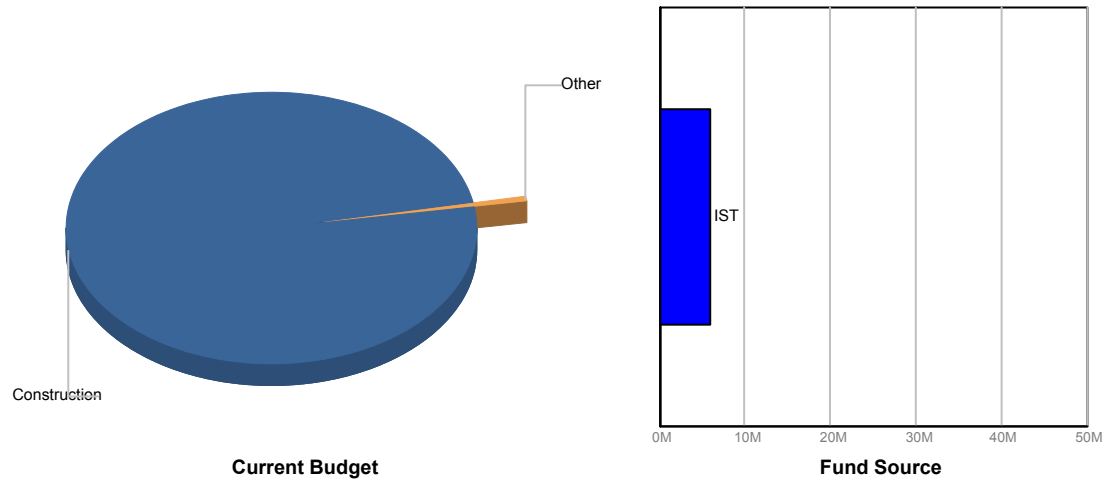

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$5,970,000	\$17,250	0.29%	\$17,250
Other	\$30,000	\$226,842	756.14%	\$20,030
TOTAL	\$6,000,000	\$244,093	4.07%	\$37,280

NOTES


Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Caloosa Park Athletic Field Renovation</p> <p>Project Number: T100 BCC District: 04 Delivery Method: TBD Category: A06-Athletic Field Renovations Status: Design Designer: Florida Transportation Engineering Contractor: TBD Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 3 as well as softball field 4. Funded: FY 2020 \$4,000,000</p>	

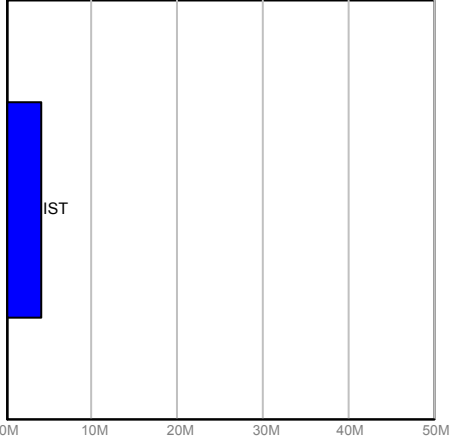SCHEDULE SUMMARY	PARTICIPATION	FUNDING																											
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td>4/20/2021</td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Proposals Due</td> <td>9/4/2020</td> <td>9/10/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Consultant Contract Issuance	12/14/2020	4/20/2021	Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Proposals Due	9/4/2020	9/10/2020	Design RFP Final Selection	10/29/2020	10/29/2020	<p>Consultant</p> <p>SBE 25% Local 25% WBE 0% MBE 6.13%</p> <p>Contractor</p> <p>SBE TBD Local TBD WBE TBD MBE TBD</p>	 <p style="text-align: center;">Current Budget</p>  <p style="text-align: center;">Fund Source</p>
	Original	Actual																											
Begin Existing Site Surveys	1/29/2020	1/29/2020																											
Complete Existing Site Surveys	6/30/2020	5/18/2020																											
Consultant Contract Issuance	12/14/2020	4/20/2021																											
Design Completion	7/2/2021																												
Turf Supplier RFP Proposal Due	4/30/2021																												
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																											
Design RFP Proposals Due	9/4/2020	9/10/2020																											
Design RFP Final Selection	10/29/2020	10/29/2020																											

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,980,000	\$227,501	5.72%	\$22,215
Other	\$20,000	\$11,806	59.03%	\$11,806
TOTAL	\$4,000,000	\$239,307	5.98%	\$34,021

NOTES

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: JPP Athletic Field Renovation

Replacement of existing grass field turf with synthetic turf on the Miracle League Field as well as softball fields 2 & 3.
Funded: FY 2020 \$3,222,000



Project Number: T101
BCC District: 03
Delivery Method: TBD
Category: A06-Athletic Field Renovations
Status: Design
Designer: Florida Transportation Engineering
Contractor: TBD
Project Manager: Stuart Patterson

SCHEDULE SUMMARY

	Original	Actual
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

PARTICIPATION


Consultant

SBE 25%
Local 25%
WBE 0%
MBE 6.13%

Contractor

SBE TBD
Local TBD
WBE TBD
MBE TBD

FUNDING

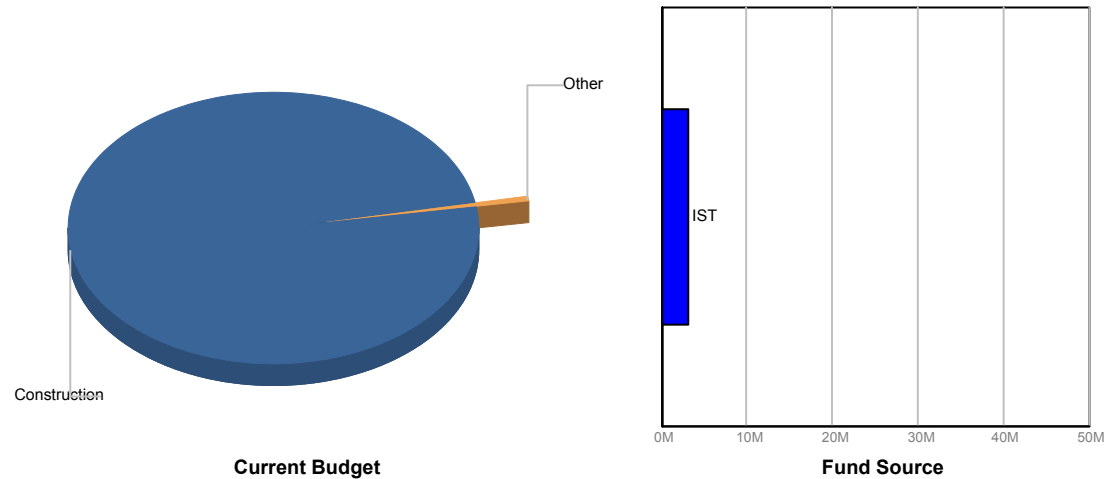

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,204,000	\$183,827	5.74%	\$16,860
Other	\$16,000	\$11,434	71.46%	\$11,434
TOTAL	\$3,220,000	\$195,261	6.06%	\$28,294

NOTES

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Loggers Run Park Athletic Field Renovation
Project Number: T102
BCC District: 05
Delivery Method: TBD
Category: A06-Athletic Field Renovations
Status: Design
Designer: TBD
Contractor: TBD
Project Manager: Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1 & 2.
 Funded: FY 2020 \$3,200,000



SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020

PARTICIPATION


Consultant

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

Contractor

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

FUNDING

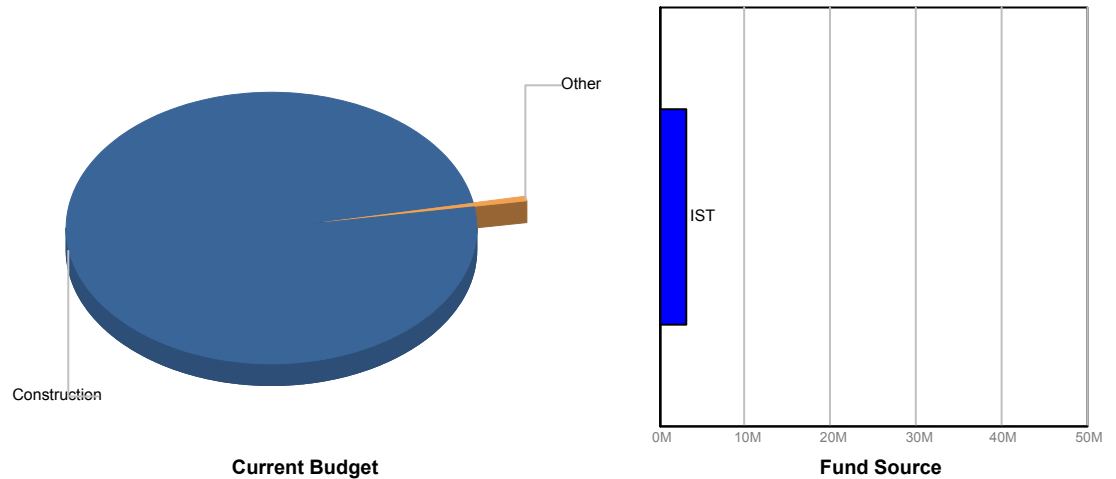

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$3,184,000	\$180,380	5.67%	\$13,750
Other	\$16,000	\$14,586	91.16%	\$14,586
TOTAL	\$3,200,000	\$194,966	6.09%	\$28,336

NOTES

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Samuel Friedland District Park Expansion
Project Number: T103
BCC District: 06
Delivery Method: TBD
Category: A06-Athletic Field Renovations
Status: Design
Designer: Florida Transportation Engineering
Contractor: TBD
Project Manager: Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 9 & 10 as well as the open play field.
 Funded: FY 2020 \$3,000,000




SCHEDULE SUMMARY

PARTICIPATION


FUNDING

	Original	Actual
Design RFP Final Selection	10/29/2020	10/29/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	
Begin Existing Site Surveys	1/20/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020

- Consultant**
- SBE TBD
 - Local TBD
 - WBE TBD
 - MBE TBD
- Contractor**
- SBE TBD
 - Local TBD
 - WBE TBD
 - MBE TBD

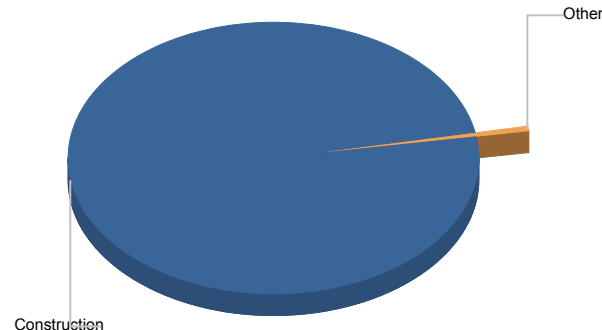

Current Budget

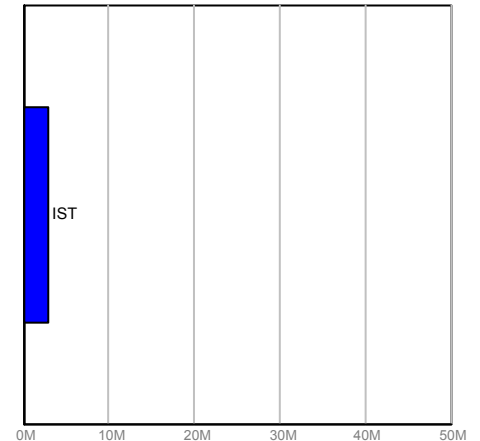

Fund Source

FINANCIAL SUMMARY

NOTES

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$2,985,000	\$179,985	6.03%	\$12,967
Other	\$15,000	\$8,519	56.79%	\$8,519
TOTAL	\$3,000,000	\$188,504	6.28%	\$21,486

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Westgate Park Restroom and Athletic Field Renovation
Project Number: T110
BCC District: 07
Delivery Method: TBD
Category: E02-Existing Park Redevelopment or Expansion
Status: Design
Designer: Florida Transportation Engineering
Contractor: TBD
Project Manager: Stuart Patterson

Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.
Funded:
 FY 2020 \$250,000
 FY 2023 \$1,750,000



SCHEDULE SUMMARY

	Original	Actual
Begin Existing Site Surveys	1/29/2020	1/29/2020
Complete Existing Site Surveys	6/30/2020	5/18/2020
Finalization of Existing Site Surveys	8/30/2020	9/18/2020
Design RFP Proposals Due	9/4/2020	9/10/2020
Design RFP Final Selection	10/29/2020	10/29/2020
Consultant Contract Issuance	12/14/2020	4/20/2021
Design Completion	7/2/2021	
Turf Supplier RFP Proposal Due	4/30/2021	

PARTICIPATION


Consultant

- SBE 25%
- Local 25%
- WBE 0%
- MBE 6.13%

Contractor

- SBE TBD
- Local TBD
- WBE TBD
- MBE TBD

FUNDING

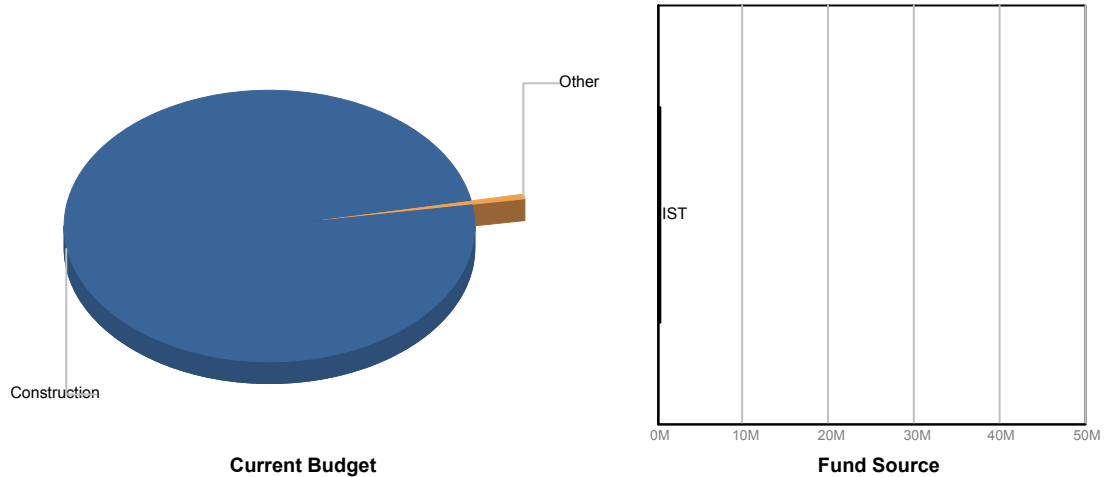

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$248,750	\$136,854	55.02%	\$0
Other	\$1,250	\$17,269	1,381.55%	\$16,647
TOTAL	\$250,000	\$154,124	61.65%	\$16,647

NOTES


Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Dubois Park Var Historic Building Repair and Renovation</p> <p>Project Number: T111</p> <p>BCC District: 01</p> <p>Delivery Method: Annual Contract</p> <p>Category: P08-Public Building Repair Replacement & Expans</p> <p>Status: Construction</p> <p>Designer: N/A</p> <p>Contractor: Robling Architecture Construction</p> <p>Project Manager: Ben Carroll</p>	<p>The project consists of relocating the Pineapple Packing House structure, wood framing repairs, roof replacement and new windows, doors, electrical and HVAC</p> <p>IST FY 2020 - \$250,000</p> <p>IST FY 2021 - \$250,000</p> <p>IST FY 2022 - \$250,000</p> <p>IST FY 2023 - \$250,000</p> <p>IST FY 2024 - \$400,585</p> <p>IST FY 2025 - \$599,415</p>	

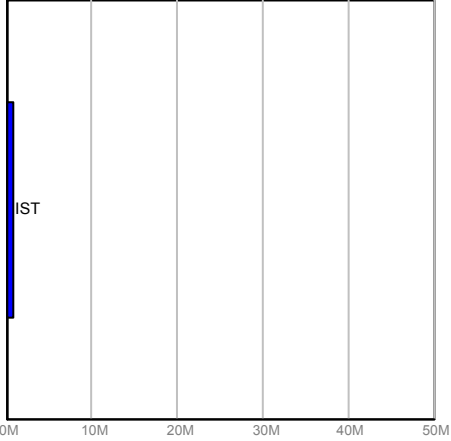SCHEDULE SUMMARY	PARTICIPATION	FUNDING									
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Project Start</td> <td>4/12/2021</td> <td>4/12/2021</td> </tr> <tr> <td>Project Completion</td> <td>12/13/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Project Start	4/12/2021	4/12/2021	Project Completion	12/13/2021		<p>Consultant</p> <p>SBE N/A</p> <p>Local N/A</p> <p>WBE N/A</p> <p>MBE N/A</p> <p>Contractor</p> <p>SBE 10.46%</p> <p>Local 100%</p> <p>WBE 0%</p> <p>MBE 0%</p>	<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Construction</p> <p>Other</p> <p>IST</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>Fund Source</p> </div> </div>
	Original	Actual									
Project Start	4/12/2021	4/12/2021									
Project Completion	12/13/2021										

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Construction	\$748,750	\$216,668	28.94%	\$42,934
Other	\$1,250	\$707	56.57%	\$707
TOTAL	\$750,000	\$217,375	28.98%	\$43,642

NOTES

Dimensional lumber is now 1 month out. Temporary fencing and foundation work has begun.

Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM

SCOPE

PHOTO

Project Title: Canyon's District Park New Park Development
Project Number: T122
BCC District: 05
Delivery Method: Construction Manager at Risk
Category: N02-New Park Development
Status: Design
Designer: Architecture Green
Contractor: Kaufman Lynn
Project Manager: Rosalyn Acosta

The project consists of the construction of a 52 acre Park south of Boynton Beach Blvd, along the west side of Acme Dairy Rd. with the Canyon Lakes Communities bordering the south and west limits of the site. The park will be constructed in two phases. Phase I will need to be completed in order to transfer the multi-purpose activities that currently take place on two existing soccer fields located to the west of the park. Once transferred the old soccer fields site will become the site of the new Canyon District Library.

 FT2021 IST \$12,000,000



SCHEDULE SUMMARY

	Original	Actual
GMP Approval	1/14/2021	5/4/2021
Construction Start	1/27/2021	
Construction Completion	1/27/2022	
Project Completion	3/27/2022	

PARTICIPATION


Consultant

SBE 75.93%
 Local 100%
 WBE 21.41%
 MBE 0%

Contractor

SBE 22.32%
 Local 100%
 WBE 22.32%
 MBE 22.32%

FUNDING

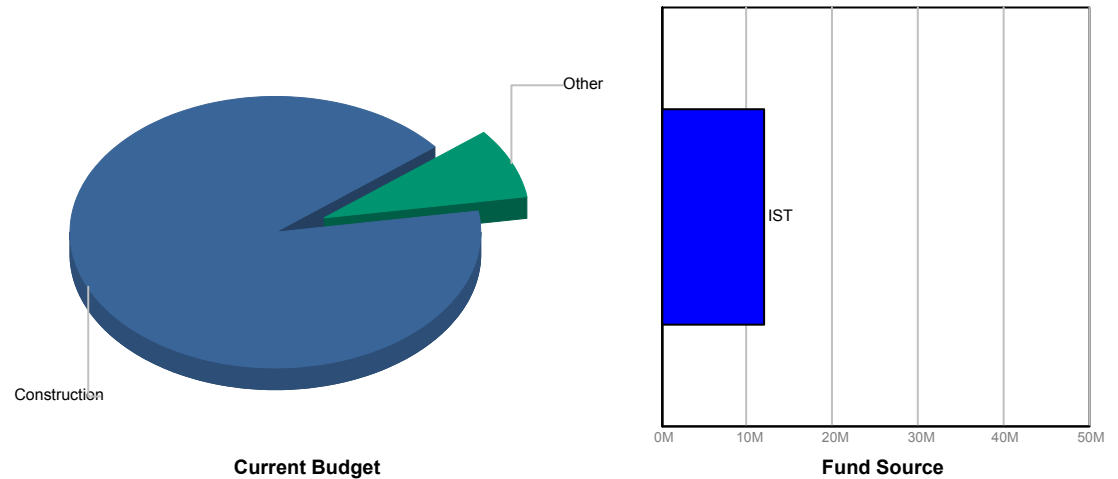

FINANCIAL SUMMARY

	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$0	\$52,727	0.00%	\$0
Construction	\$11,000,000	\$11,467,581	104.25%	\$2,904,791
Other	\$1,000,000	\$23,031	2.30%	\$23,031
TOTAL	\$12,000,000	\$11,543,340	96.19%	\$2,927,823

NOTES


Partial Substantial Completion for the work associated to the round about and opening of Joe Abruzzo Rd has been completed; contractor is putting together the close-out package. The contractor has received several DRs (deficiency reports) from the architect they are working on corrections. KL notified CID that they will be substituting the Superintendent and that the Phase 1 A PM has resigned.



Monthly Infrastructure Sales Tax Project Report

Large Cap Projects

Data Date: 10/21/2021

Report Date: 11/10/2021

DESCRIPTION/TEAM	SCOPE	PHOTO
<p>Project Title: Glades Pioneer Park Athletic Field Renovation</p> <p>Project Number: T175</p> <p>BCC District: 07</p> <p>Delivery Method: TBD</p> <p>Category: A06-Athletic Field Renovations</p> <p>Status: Design</p> <p>Designer: Florida Transportation Engineering</p> <p>Contractor: TBD</p> <p>Project Manager: Stuart Patterson</p>	<p>Replacement of existing grass field turf with synthetic turf on multi-purpose field 1.</p> <p>Funded:</p> <p>FY 2021 \$210,000</p> <p>FY 2023 \$2,000,000</p>	

SCHEDULE SUMMARY	PARTICIPATION	FUNDING																								
<table border="1"> <thead> <tr> <th></th> <th>Original</th> <th>Actual</th> </tr> </thead> <tbody> <tr> <td>Begin Existing Site Surveys</td> <td>1/29/2020</td> <td>1/29/2020</td> </tr> <tr> <td>Complete Existing Site Surveys</td> <td>6/30/2020</td> <td>5/18/2020</td> </tr> <tr> <td>Finalization of Existing Site Surveys</td> <td>8/30/2020</td> <td>9/18/2020</td> </tr> <tr> <td>Design RFP Final Selection</td> <td>10/29/2020</td> <td>10/29/2020</td> </tr> <tr> <td>Consultant Contract Issuance</td> <td>12/14/2020</td> <td></td> </tr> <tr> <td>Design Completion</td> <td>7/2/2021</td> <td></td> </tr> <tr> <td>Turf Supplier RFP Proposal Due</td> <td>4/30/2021</td> <td></td> </tr> </tbody> </table>		Original	Actual	Begin Existing Site Surveys	1/29/2020	1/29/2020	Complete Existing Site Surveys	6/30/2020	5/18/2020	Finalization of Existing Site Surveys	8/30/2020	9/18/2020	Design RFP Final Selection	10/29/2020	10/29/2020	Consultant Contract Issuance	12/14/2020		Design Completion	7/2/2021		Turf Supplier RFP Proposal Due	4/30/2021		<p>Consultant</p> <p>SBE 25%</p> <p>Local 25%</p> <p>WBE 0%</p> <p>MBE 6.13%</p> <p>Contractor</p> <p>SBE TBD</p> <p>Local TBD</p> <p>WBE TBD</p> <p>MBE TBD</p>	<div style="text-align: center;">  <p>Design</p> <p>Current Budget</p> </div> <div style="text-align: center;">  <p>IST</p> <p>Fund Source</p> </div>
	Original	Actual																								
Begin Existing Site Surveys	1/29/2020	1/29/2020																								
Complete Existing Site Surveys	6/30/2020	5/18/2020																								
Finalization of Existing Site Surveys	8/30/2020	9/18/2020																								
Design RFP Final Selection	10/29/2020	10/29/2020																								
Consultant Contract Issuance	12/14/2020																									
Design Completion	7/2/2021																									
Turf Supplier RFP Proposal Due	4/30/2021																									

FINANCIAL SUMMARY				
	Project Budget	Committed	% Committed	Paid To Date
	A	B	C=B/A	D
Design	\$210,000	\$156,318	74.44%	\$11,007
TOTAL	\$210,000	\$156,318	74.44%	\$11,007

NOTES

Design is ongoing. Expected 100% complete by 12/31/2021. Monthly Design meetings have been scheduled. DD drawings have been complete and review comments have been returned to FTE.
